

Valley View Drive - Completed



#9

**BOARD OF HEALTH, AMHERST, MASSACHUSETTS**  
**APPLICATION FOR DISPOSAL WORKS CONSTRUCTION PERMIT**

No. 12-63 Date 5/8/63 Fee 3.00 Date Rec'd. 5/10/63 By FAS

Application is hereby made for a permit to Construct () or Repair ( ) an Individual Sewage Disposal System at:

Location—Address Valley View Dr. (K.V.) or Lot No. 9

Owner Kay Vee Realty Kaddy Builders Inc. Address E. Longmeadow

Contractor Same Address \_\_\_\_\_

Type of Building Residence Dimensions 27' x 40' Size Lot 32, 308 sq ft.

Dwelling—No. of Bedrooms 3 Expansion Attic (No) Garbage Grinder (No)

Other \_\_\_\_\_ No. of persons SPEC Showers ( )

Other fixtures Complete Bath + Kitchen + Laundry

Town Water? Yes Type of Well \_\_\_\_\_

Design Flow 50 gallons per person per day. Total daily flow 600 gallons

Septic Tank—Liquid capacity 900 gallons Dimensions: L \_\_\_\_\_ W \_\_\_\_\_ D \_\_\_\_\_

Disposal Trench—No. 3 Width 3 ft. Total Length 150 ft Total leaching area 450 sq. ft.

Disposal Bed—No. \_\_\_\_\_ Diameter \_\_\_\_\_ Depth below inlet \_\_\_\_\_ Total leaching area \_\_\_\_\_ sq. ft.

Dry Well—No. \_\_\_\_\_ Diameter \_\_\_\_\_ Depth below inlet \_\_\_\_\_ Dimensions: \_\_\_\_\_ x \_\_\_\_\_ x \_\_\_\_\_

Other: Distribution box () No. 1 Dosing tank ( )

(Depth of Soil Line Below finished grade at foundation 12" or less)

Percolation Test Results Performed by Smith + Weller Eng. Date 4/30/63

Test Pit No. 1 10 minutes per inch Depth of Test Pit 3 ft.

Test Pit No. 2 \_\_\_\_\_ minutes per inch Depth of Test Pit \_\_\_\_\_

Description of Soil Sandy Clay Depth to Ground Water See affidavit

Will disposal area be filled? \_\_\_\_\_ Cut down? \_\_\_\_\_

(On reverse side or separate sheet, show plot plan with building. Include dimensions, distances from all boundaries. Show location of wells, streams, ledge, large trees, etc.)

AGREEMENT: The undersigned agrees to construct the aforedescribed individual sewage disposal system in accordance with the provisions of Article XI of the Sanitary Code and regulations of the Amherst Board of Health. The undersigned further agrees not to place the system in operation until a Certificate of Compliance has been issued by this board of health.

Application Approved by G. A. Sino

Joe Cassinai  
 Owner or builder date 5/8/63  
 date

Application Disapproved for the following reasons:

NO PARCEL

**BOARD OF HEALTH, AMHERST, MASSACHUSETTS**  
**CERTIFICATE OF COMPLIANCE**

THIS IS TO CERTIFY, That the individual Sewage Disposal System installed () or repaired ( ) by Keddy Builders Inc at Lot No. 9 has been constructed in accordance with the provisions of

INSTALLER

Article XI of the State Sanitary Code as described in the application for Disposal Works Construction Permit No. 12-63 dated 5/8/63

The issuance of this certificate shall not be construed as a guarantee that the system will function satisfactorily.

DATE 7/19/63

Inspector G. A. Sino

**BOARD OF HEALTH, AMHERST, MASSACHUSETTS**  
**DISPOSAL WORKS CONSTRUCTION PERMIT**


No. 12-63

Permission is hereby granted Keddy Builders Inc. to construct () or repair ( ) an Individual Sewage Disposal System at Lot 9 - Valley View Dr. as shown on the application for Disposal Works Construction Permit No. 12-63

This permit is issued with the understanding that future alterations or additions will be made if necessary. This permit shall not be construed as permission to create or maintain any sewage nuisance and in the issuance of this permit the Board of Health assumes no responsibility for the future operation or maintenance of the system.

DATE 5/8/63

F. A. Sino  
 Board of Health G.J.

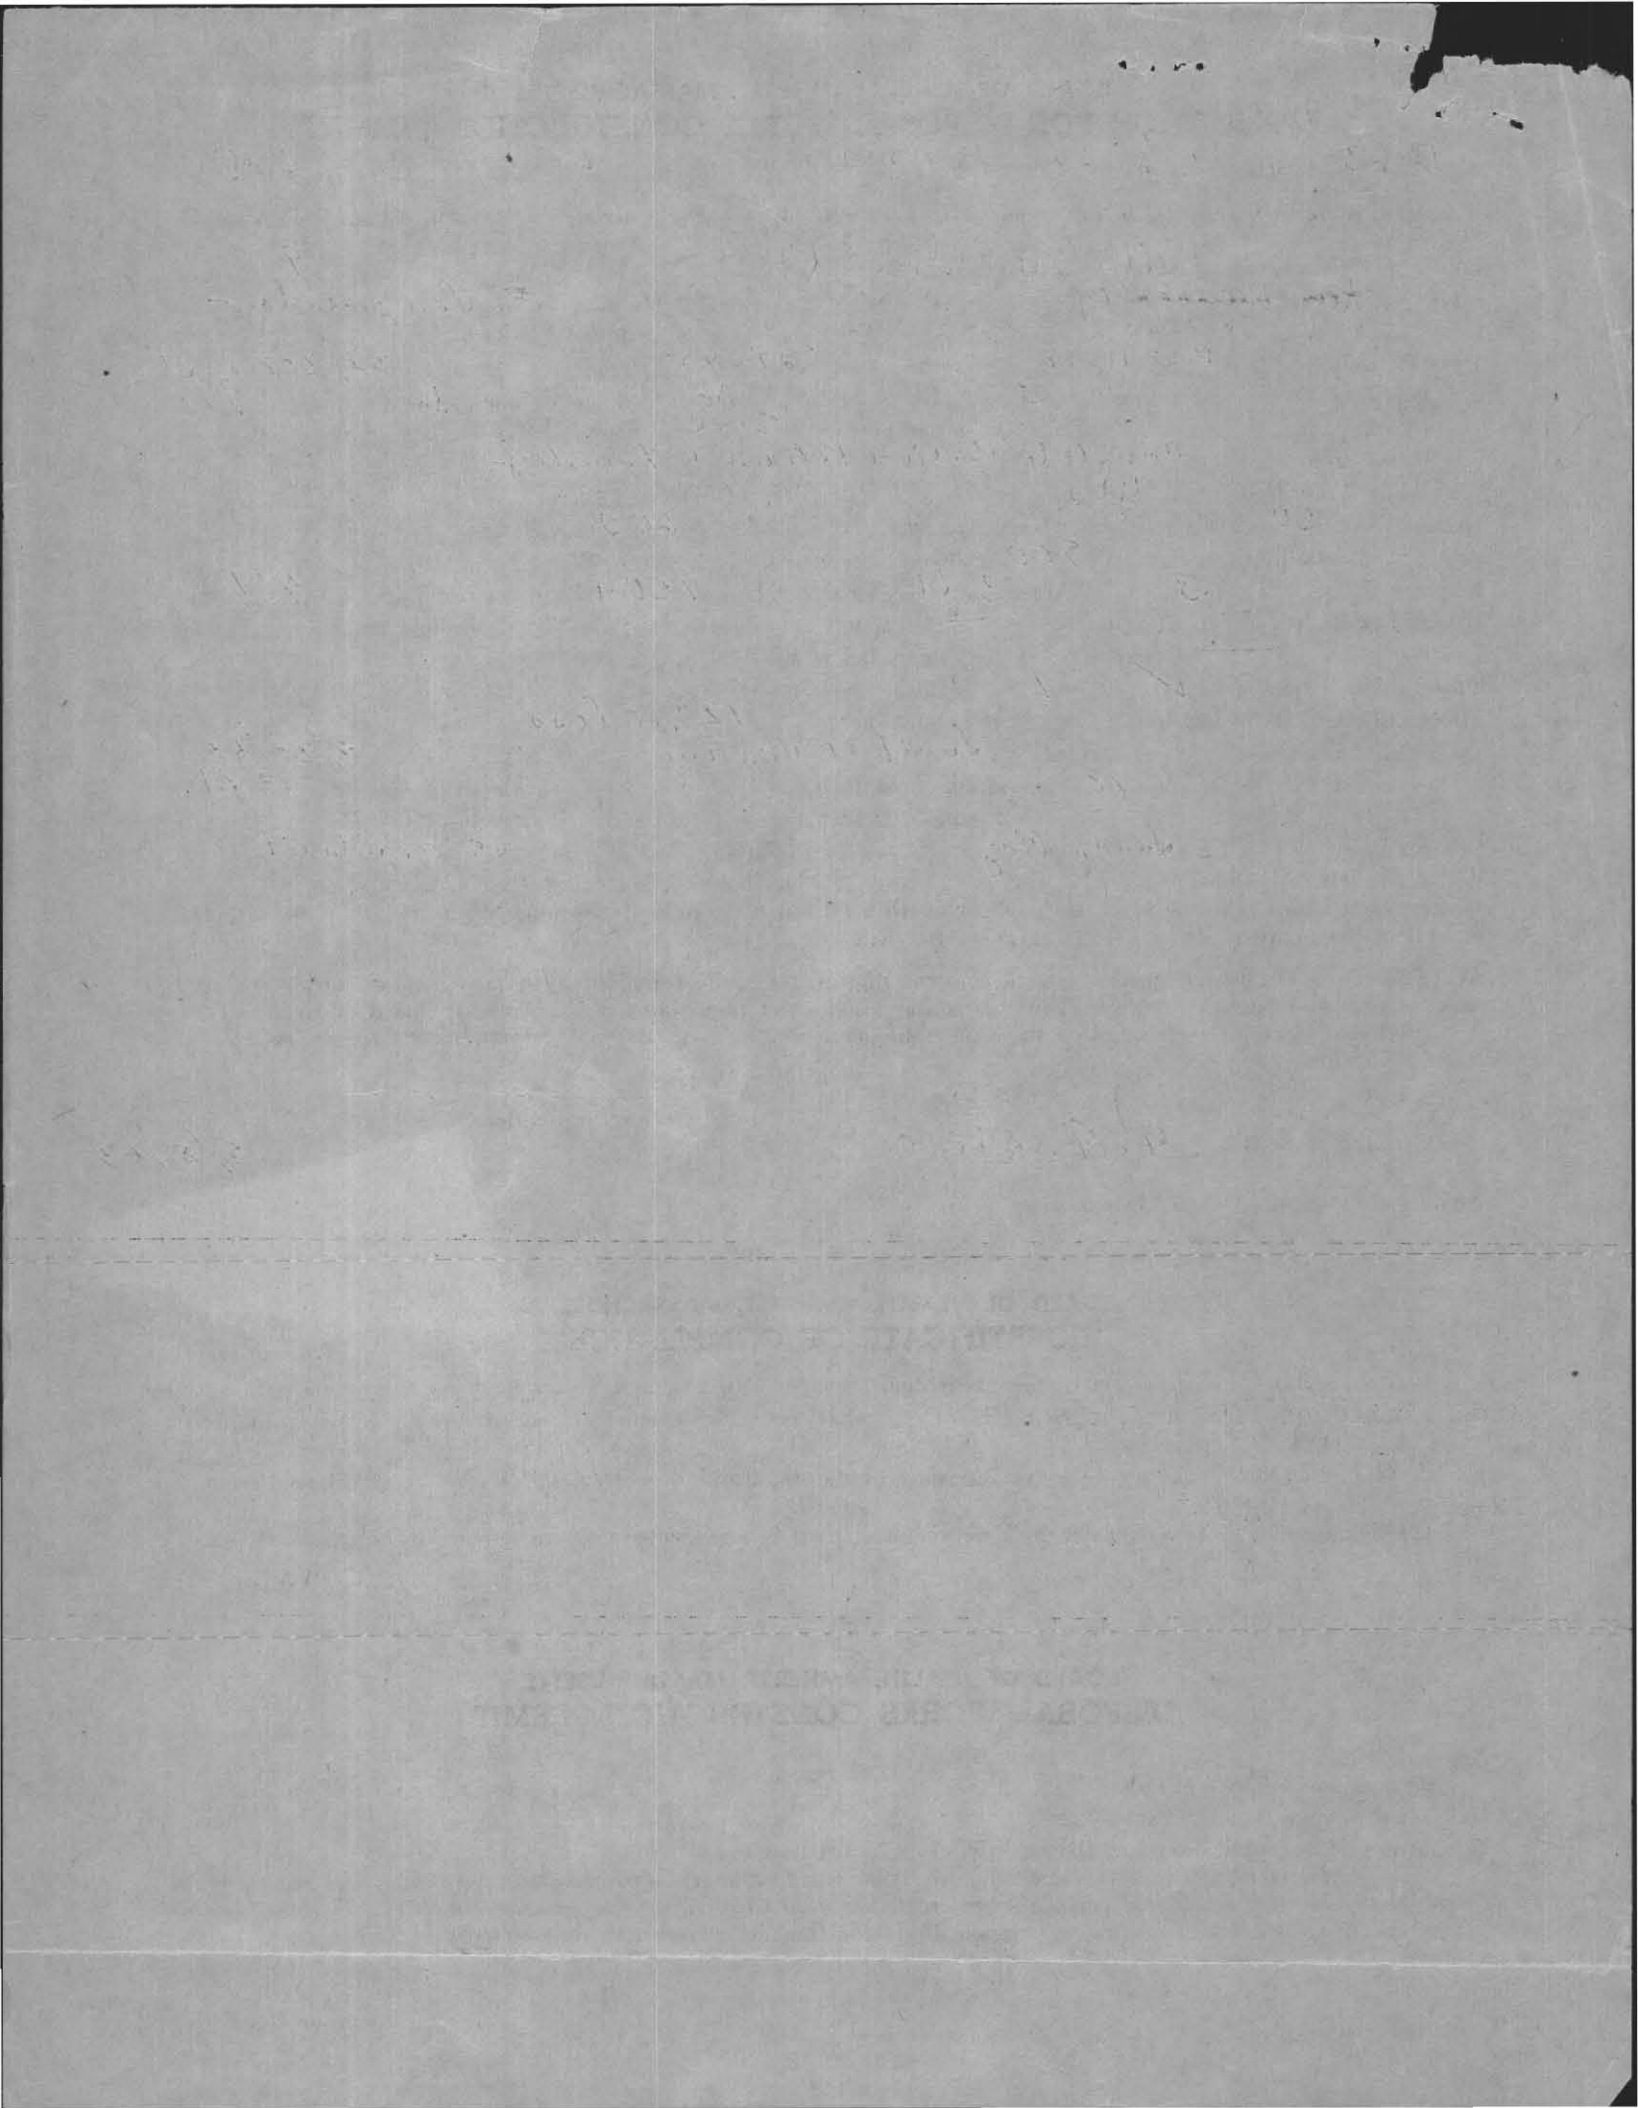

VETERANS ADMINISTRATION  
**REPORT OF INSPECTION, INDIVIDUAL WATER SUPPLY AND SEWAGE-DISPOSAL SYSTEM**

(THIS SECTION FOR VA USE ONLY)

REGIONAL OFFICE <b>Boston, Massachusetts</b>		PROPERTY ADDRESS <b>Lot # Valley View Drive</b>		SUBDIVISION NAME <b>Briar Cliff Manor Section II</b>	
NAME OF BUILDER <b>Keddy Builders, Inc.</b>		NAME OF LENDER <b>Amherst Savings Bank</b>		BLOCK NO.	LOT NO.
TOTAL NUMBER		BASEMENT	CAN ATTIC OR OTHER AREA BE MADE INTO ADDITIONAL BEDROOMS?	WATER SUPPLY AND SEWAGE DISPOSAL (Check)	
LIVING UNITS	BEDROOMS	<input checked="" type="checkbox"/> YES <input type="checkbox"/> NO	<input type="checkbox"/> YES <input checked="" type="checkbox"/> NO	IF YES, HOW MANY?	
<b>1</b>	<b>3</b>				
				PUBLIC <input checked="" type="checkbox"/> COMMUNITY <input type="checkbox"/> INDIVIDUAL <input type="checkbox"/>	
				WATER SUPPLY BY <input checked="" type="checkbox"/> SEWAGE DISPOSAL BY <input checked="" type="checkbox"/>	

**PART I—FOR USE OF INSPECTING OFFICIAL** (Fill in below information applicable to subject installation)

INSTRUCTIONS: If new installation, inspect for compliance with approved exhibits and record any observed information not shown on, or which varies from, the approved exhibits. If existing installation, furnish as much of the information as may be available. As applicable use inspector's sketch on reverse.

**INDIVIDUAL WATER SUPPLY SYSTEM**

Distance to nearest public water main, \_\_\_\_\_ feet. Size of main, \_\_\_\_\_ inches.  
 Individual wells  are  are not customary in neighborhood.  
 Give most recent record of failure of wells in immediate vicinity to furnish adequate supply of water \_\_\_\_\_

Properties in neighborhood  are  are not being developed with both individual water-supply and sewage-disposal systems.  
 Lot size: \_\_\_\_\_ feet wide, \_\_\_\_\_ feet deep. Dwelling set back from front property line, \_\_\_\_\_ feet.  
 Individual water supply from:  Drilled well.  Driven well.  Dug well.  Bored well.  
 Distance of well from:  
 Building foundation, \_\_\_\_\_ feet; nearest lot line at  front,  side,  rear, \_\_\_\_\_ feet;  
 cast iron sewer, \_\_\_\_\_ feet; tile sewer, \_\_\_\_\_ feet; septic tank, \_\_\_\_\_ feet; disposal field, \_\_\_\_\_ feet;  
 seepage pit, \_\_\_\_\_ feet; cesspool, \_\_\_\_\_ feet; other sources of possible pollution, \_\_\_\_\_ feet.  
 Well construction:  
 Diameter, \_\_\_\_\_ inches. Total depth, \_\_\_\_\_ feet. Type of casing, \_\_\_\_\_ Depth of casing, \_\_\_\_\_ feet.  
 Approximate depth of pumping level of water in well, \_\_\_\_\_ feet. Approximate yield, \_\_\_\_\_ gallons per minute.  
 Sealed watertight to depth of \_\_\_\_\_ feet.  
 Exterior space around casing sealed with:  Cement grout.  Puddled clay.  Ordinary backfill.  
 Well cover:  Concrete.  Wood.  Metal. Openings in well cover watertight:  Yes.  No.  
 Pump:  Shallow well.  Deep well. Length of drop pipe, \_\_\_\_\_ feet. Pump capacity, \_\_\_\_\_ gallons per minute.  
 Located in:  Basement.  Pump room off basement.  Pump house above ground.  Pump pit.  
 Pump room properly drained:  Yes.  No. Pump mounting watertight:  Yes.  No.  
 Type of storage:  Pressure.  Gravity. Capacity, \_\_\_\_\_ gallons.  
 Has bacteriological examination of water been made?  Yes.  No. If answer is "yes," give date \_\_\_\_\_, 19\_\_\_\_.  
 Quality of water  is  is not satisfactory for human consumption.  
 Installation  does  does not comply with approved exhibits, if any.

**INDIVIDUAL SEWAGE-DISPOSAL SYSTEM**

PRIMARY TREATMENT consists of  Septic tank.  Cesspool.

Septic tank:  
 Distance from well, none feet. Material, concrete Number of compartments 1  
 Total liquid capacity, 900 gallons. Capacity inlet compartment, 900 gallons.  
 Inside length, 8 feet. Inside width, 4 feet. Liquid depth, 4 feet.

Cesspool:  
 Distance from: Well, \_\_\_\_\_ feet; foundation, \_\_\_\_\_ feet; nearest lot line at  front,  side,  rear, \_\_\_\_\_ feet.  
 Inside diameter, \_\_\_\_\_ feet. Depth, \_\_\_\_\_ feet. Liquid capacity, \_\_\_\_\_ gallons. Lining material \_\_\_\_\_

SECONDARY TREATMENT consists of  Distribution box and  Tile disposal field.  Seepage pits. Other \_\_\_\_\_

Tile disposal field:  
 Distance from: Well, \_\_\_\_\_ feet; foundation, 30 feet; nearest lot line at  front,  side,  rear, 30 feet.  
 Total length of tile lines, \_\_\_\_\_ feet. Number of lines, 3. Distance between lines, 12 feet.  
 Total effective absorption area in bottom of trenches, 500 square feet. Trench width, 36 inches.  
 Length of each line, \_\_\_\_\_ feet. Depth, top of tile to finish grade, 18 inches.  
 Type of filter material:  Gravel.  Broken stone.  Cinders. Other \_\_\_\_\_  
 Depth of filter material beneath tile, 10-12 inches. Depth of filter material over tile, 2 inches.


Seepage pits:  
 Number of pits, \_\_\_\_\_ Outside diameter, \_\_\_\_\_ feet. Depth, \_\_\_\_\_ feet. Lining material \_\_\_\_\_  
 Distance from: Well, \_\_\_\_\_ feet; foundation, \_\_\_\_\_ feet; nearest lot line at  front,  side,  rear, \_\_\_\_\_ feet.

If existing installation, give all the following additional information available:  
 Distance to nearest: Public sewer, \_\_\_\_\_ feet. Community system, \_\_\_\_\_ feet.  
 Approximate direction of surface drainage of lot, \_\_\_\_\_ Approximate slope, \_\_\_\_\_ feet per 100 feet.  
 Soil is:  Loam.  Sandy loam.  Clay.  Sandy clay.  Coarse sand or gravel.  Hardpan.  Rock. Other \_\_\_\_\_  
 Number of bathrooms, \_\_\_\_\_. Is there a basement?  Yes.  No. Basement drains to \_\_\_\_\_  
 Fixtures in basement:  Laundry tray.  Toilet.  Bathtub.  Shower.  None.  Floor drain.  Sump pump.  
 Laundry waste disposal: Direct to  Seepage pit. Other \_\_\_\_\_ Through sump pit to:  Septic tank.  Seepage pits.  
 Is footing drain provided?  Yes.  No. Drains to:  Surface.  Dry well.  Sump in basement. Other \_\_\_\_\_  
 Downspouts or areaway drain to:  Surface discharge.  Dry well. Other \_\_\_\_\_  
 Depth of house sewer below finish grade at foundation, \_\_\_\_\_ feet.

PART I (Continued on reverse)

**PART I (Continued)**

INSPECTOR'S SKETCH (Show by sketch below any pertinent findings not fully described on other side.)

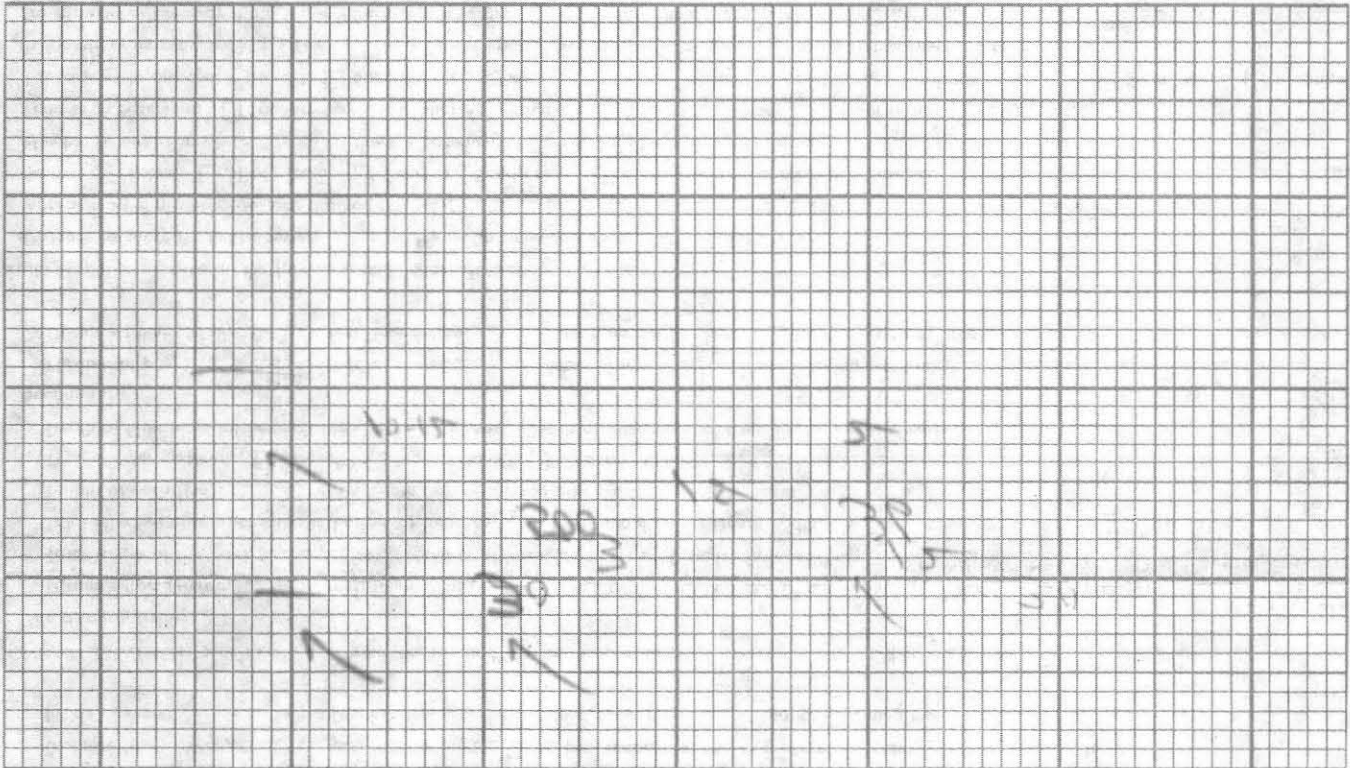

COMMENTS (Note any supplemental pertinent information. If conditions are found which may result in an opinion that the system is unsatisfactory, describe in detail.)

INSPECTION OF INDIVIDUAL WATER SUPPLY SYSTEM MADE BY: <input type="checkbox"/> STATE <input type="checkbox"/> COUNTY <input type="checkbox"/> LOCAL HEALTH AUTHORITY <input type="checkbox"/> VA COMPLIANCE INSPECTOR	DATE OF INSPECTION
SIGNATURE OF INSPECTING OFFICIAL	TITLE

INSPECTION OF INDIVIDUAL SEWAGE-DISPOSAL SYSTEM MADE BY: <input type="checkbox"/> STATE <input type="checkbox"/> COUNTY <input checked="" type="checkbox"/> LOCAL HEALTH AUTHORITY <input type="checkbox"/> VA COMPLIANCE INSPECTOR	DATE OF INSPECTION
SIGNATURE OF INSPECTING OFFICIAL	TITLE <i>Director of Public Health</i>

**PART II—FOR USE OF THE HEALTH DEPARTMENT OFFICIAL REVIEWING REPORT**

BASED ON THE INFORMATION REPORTED HEREON AND OTHER AVAILABLE INFORMATION, IT IS THE OPINION OF THE (Check) <input type="checkbox"/> STATE <input type="checkbox"/> COUNTY <input type="checkbox"/> LOCAL DEPARTMENT OF HEALTH THAT THIS INDIVIDUAL WATER SUPPLY SYSTEM IS:	<input type="checkbox"/> SATISFACTORY AS A DOMESTIC WATER SUPPLY FOR THE SUBJECT PROPERTY <input type="checkbox"/> NOT SATISFACTORY AS A DOMESTIC WATER SUPPLY FOR THE SUBJECT PROPERTY
BASED ON THE INFORMATION REPORTED HEREON, AND OTHER AVAILABLE INFORMATION, IT IS THE OPINION OF THE (Check) <input type="checkbox"/> STATE <input type="checkbox"/> COUNTY <input checked="" type="checkbox"/> LOCAL DEPARTMENT OF HEALTH THAT THIS INDIVIDUAL SEWAGE-DISPOSAL SYSTEM, WITH PROPER MAINTENANCE:	<input checked="" type="checkbox"/> CAN BE EXPECTED TO FUNCTION SATISFACTORILY AND IS NOT LIKELY TO CREATE AN INSANITARY CONDITION <input type="checkbox"/> CANNOT BE EXPECTED TO FUNCTION SATISFACTORILY

REMARKS

DATE <i>7/15/63</i>	SIGNATURE OF REVIEWING OFFICIAL <i>Fredrick A. Sims</i>	TITLE <i>DIRECTOR OF PUBLIC HEALTH</i>
------------------------	--	---

**PART III—FOR USE OF VA OFFICE**

I have reviewed the foregoing and the pertinent VA Compliance Inspection Report and recommend that the

individual water supply system be considered	<input type="checkbox"/> Acceptable	<input type="checkbox"/> Not acceptable
individual sewage-disposal system be considered	<input type="checkbox"/> Acceptable	<input type="checkbox"/> Not acceptable

REMARKS

DATE	SIGNATURE OF CHIEF, APPRAISAL SECTION
------	---------------------------------------
