

343 MONTAGUE ROAD

SPT 2002-00004



TITLE 5
OFFICIAL INSPECTION FOR - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM FORM
PART A
CERTIFICATION

Property Address: 343 Montague Road Amherst MA

Owner's Name: Kenneth and Louise Havemon C/O Cindy Arbour, Daughter

Owner's Address: 34 James Street
Greenfield, MA 01301

Date of Inspection: July 18, 2001

Name of Inspector: Alan E. Weiss, R.S # 933

Company Name: Cold Spring Environmental Inc.

Mailing Address: 350 Old Enfield Road
Belchertown, Massachusetts 01007

Telephone Number: (413) 323-5957 fax: 413-323-4916

CERTIFICATION STATEMENT

I certify that I have personally inspected the sewage disposal system at this address and that the information reported below is true, accurate and complete as of the time of the inspection. The inspection was performed based on my training and experience in the proper function and maintenance of on site sewage disposal systems. I am a DEP approved system inspector pursuant to Section 15.340 of Title 5 (310 CMR 15.000). The system:

- Passes
 Conditionally Passes
 Needs Further Evaluation by the Local Approving Authority
 XX Fails

Inspector's Signature:  Date: **July 18, 2001**

The system inspector shall submit a copy of this inspection report to the Approving Authority (Board of Health or DEP) within 30 days of completing this inspection. If the system is a shared system or has a design flow of 10,000 gpd or greater, the inspector and the system owner shall submit the report to the appropriate regional office of the DEP. The original should be sent to the system owner and copies sent to the buyer, if applicable, and the approving authority.

Notes and Comments

System is very old (1960s), Five people were living in house. The dry well had staining to top and was recently full of Liquid.

****This report only describes conditions at the time of inspection and under the conditions of use at that time. This inspection does not address how the system will perform in the future under the same different conditions of use.

OFFICIAL INSPECTION FORM - NOT FOR VOLUNTARY ASSESSMENTS

1. The first part of the document discusses the importance of maintaining accurate records of all transactions. It emphasizes that this is crucial for ensuring the integrity of the financial statements and for providing a clear audit trail.

2. The second part of the document outlines the various methods used to collect and analyze data. It describes how different types of information are gathered and how they are processed to identify trends and patterns.

3. The third part of the document focuses on the results of the analysis. It presents the findings in a clear and concise manner, highlighting the key areas of concern and the potential implications for the organization.

4. The fourth part of the document discusses the recommendations for future action. It provides a list of specific steps that should be taken to address the issues identified in the analysis and to improve the overall performance of the organization.

5. The fifth part of the document concludes with a summary of the key points and a final statement of the author's conclusions. It reiterates the importance of the findings and the need for continued vigilance in monitoring the organization's performance.

6. The sixth part of the document provides a list of references and sources used in the research. It includes a bibliography of books, articles, and other documents that have been consulted during the course of the study.

7. The seventh part of the document is a list of appendices. It contains additional information that is relevant to the study but that is too detailed to include in the main body of the report.

OFFICIAL INSPECTION FORM - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART A
CERTIFICATION (continued)

Property Address: 343 Montague rd.

Owner: Hase meo

Date of Inspection: 7/18/01

Inspection Summary: Check A,B,C,D or E / ALWAYS complete all of Section D

A. System Passes:

No I have not found any information which indicates that any of the failure criteria described in 310 CMR 15.303 or in 310 CMR 15.304 exist. Any failure criteria not evaluated are indicated below.

Comments:

B. System Conditionally Passes:

No One or more system components as described in the "Conditional Pass" section need to be replaced or repaired. The system, upon completion of the replacement or repair, as approved by the Board of Health, will pass.

Answer yes, no or not determined (Y,N,ND) in the ____ for the following statements. If "not determined" please explain.

____ The septic tank is metal and over 20 years old* or the septic tank (whether metal or not) is structurally unsound, exhibits substantial infiltration or exfiltration or tank failure is imminent. System will pass inspection if the existing tank is replaced with a complying septic tank as approved by the Board of Health.

*A metal septic tank will pass inspection if it is structurally sound, not leaking and if a Certificate of Compliance indicating that the tank is less than 20 years old is available.

ND explain:

____ Observation of sewage backup or break out or high static water level in the distribution box due to broken or obstructed pipe(s) or due to a broken, settled or uneven distribution box. System will pass inspection if (with approval of Board of Health):


- ____ broken pipe(s) are replaced
- ____ obstruction is removed
- ____ distribution box is leveled or replaced

ND explain:

____ The system required pumping more than 4 times a year due to broken or obstructed pipe(s). The system will pass inspection if (with approval of the Board of Health):

- ____ broken pipe(s) are replaced
- ____ obstruction is removed

ND explain:

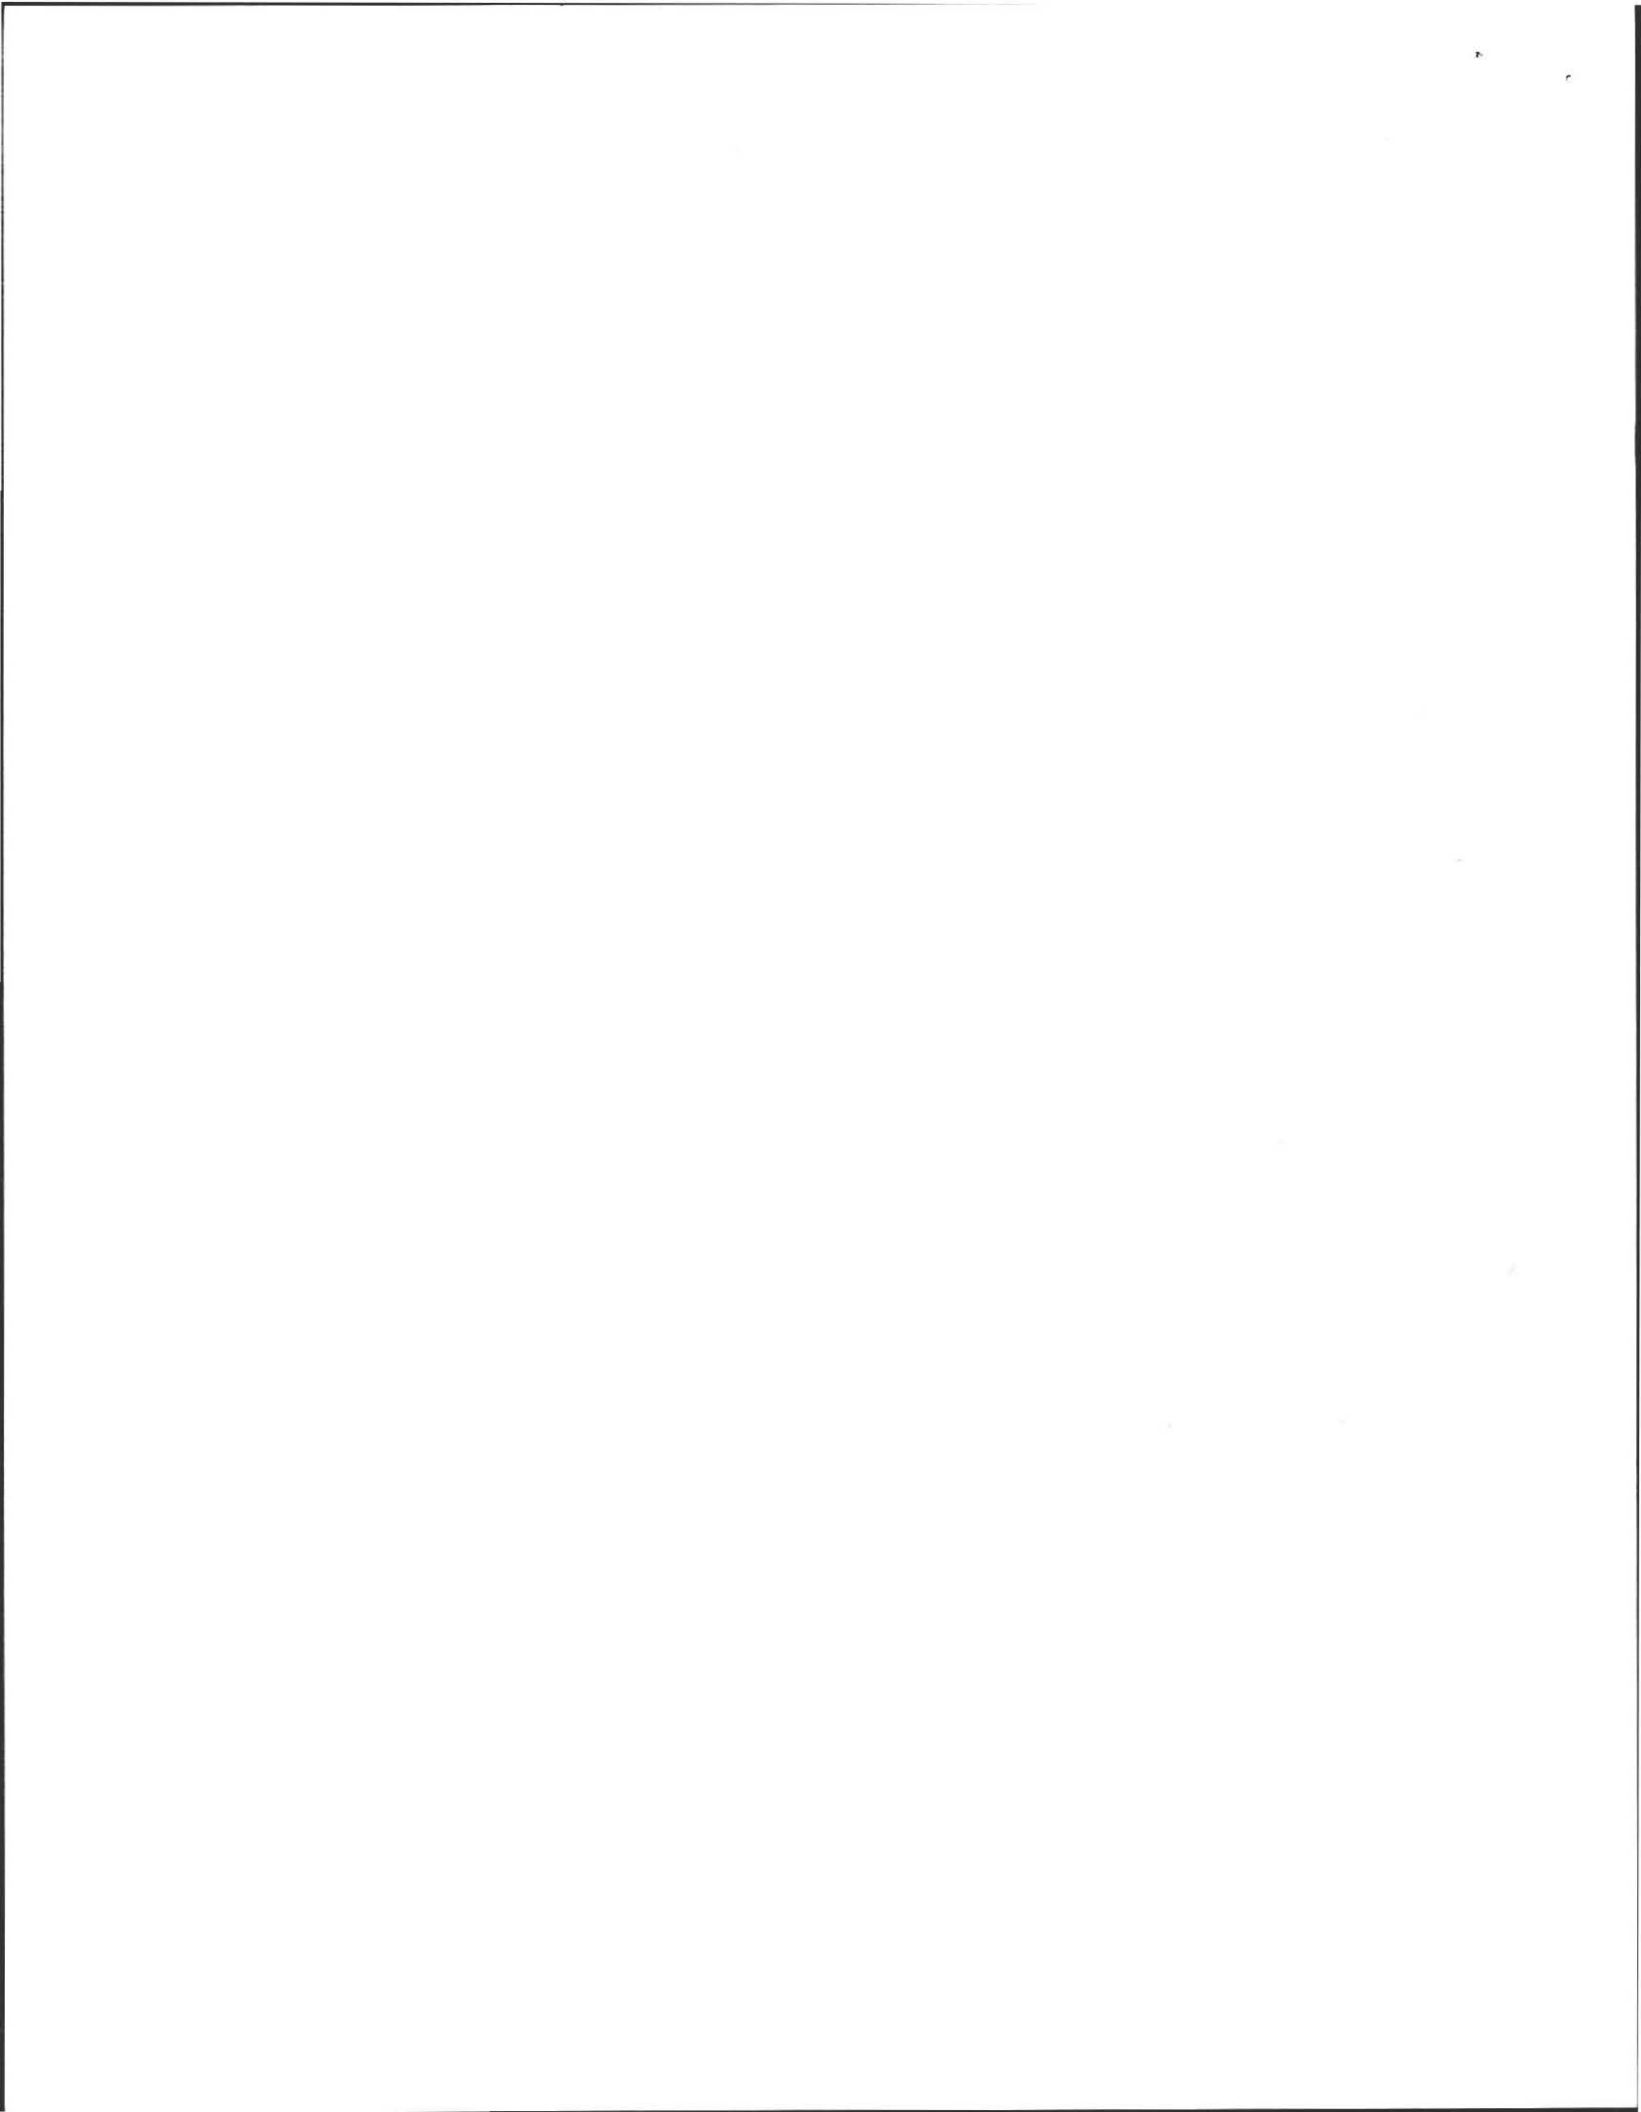

OFFICIAL INSPECTION FORM - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART A
CERTIFICATION (continued)

Property Address: 343 Montague Rd

Owner: Hareman

Date of Inspection: 7/18/01

C. Further Evaluation is Required by the Board of Health:

No Conditions exist which require further evaluation by the Board of Health in order to determine if the system is failing to protect public health, safety or the environment.

1. System will pass unless Board of Health determines in accordance with 310 CMR 15.303(1)(b) that the system is not functioning in a manner which will protect public health, safety and the environment:


- Cesspool or privy is within 50 feet of a surface water
- Cesspool or privy is within 50 feet of a bordering vegetated wetland or a salt marsh

2. System will fail unless the Board of Health (and Public Water Supplier, if any) determines that the system is functioning in a manner that protects the public health, safety and environment:

- The system has a septic tank and soil absorption system (SAS) and the SAS is within 100 feet of a surface water supply or tributary to a surface water supply.
- The system has a septic tank and SAS and the SAS is within a Zone 1 of a public water supply.
- The system has a septic tank and SAS and the SAS is within 50 feet of a private water supply well.
- The system has a septic tank and SAS and the SAS is less than 100 feet but 50 feet or more from a private water supply well**. Method used to determine distance _____

**This system passes if the well water analysis, performed at a DEP certified laboratory, for coliform bacteria and volatile organic compounds indicates that the well is free from pollution from that facility and the presence of ammonia nitrogen and nitrate nitrogen is equal to or less than 5 ppm, provided that no other failure criteria are triggered. A copy of the analysis must be attached to this form.

3. Other:

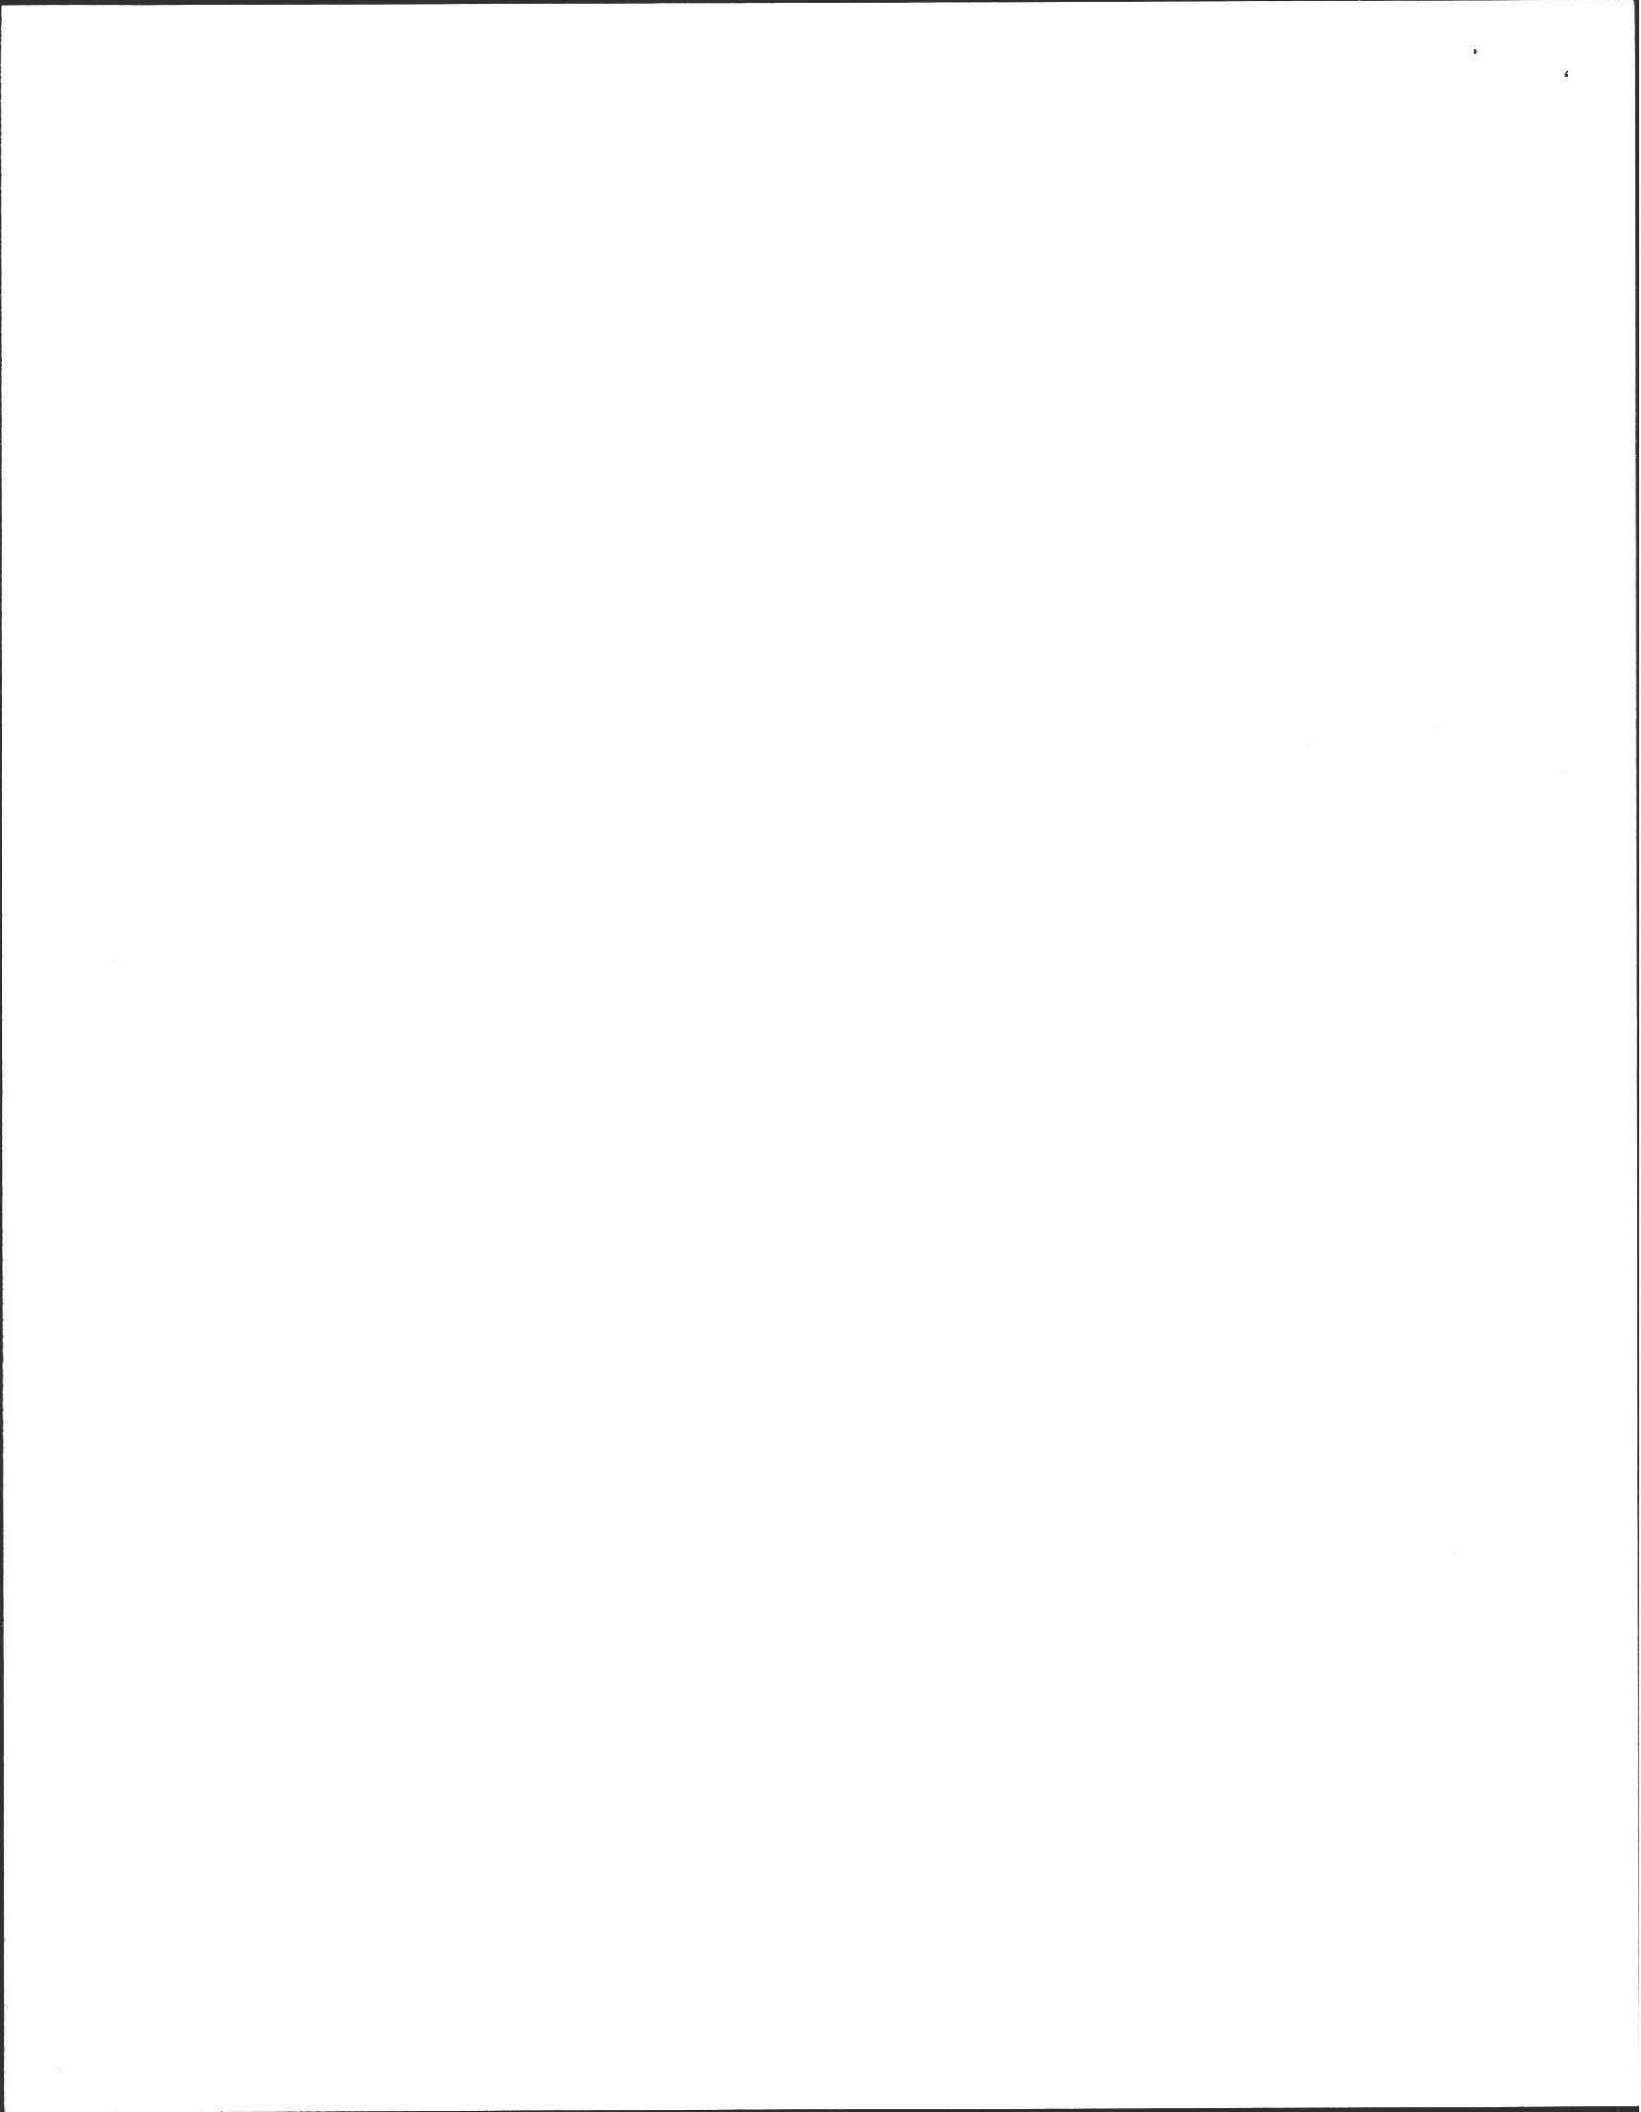

**OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM**

**PART A
CERTIFICATION (continued)**

Property Address: 343 Montague Rd.

Owner: Homedex.

Date of Inspection: 7/1/07

D. System Failure Criteria applicable to all systems:

You must indicate "yes" or "no" to each of the following for all inspections:

- | Yes | No | |
|------------|------------|--|
| <u>Yes</u> | <u> </u> | Backup of sewage into facility or system component due to overloaded or clogged SAS or cesspool |
| <u> </u> | <u>No</u> | Discharge or ponding of effluent to the surface of the ground or surface waters due to an overloaded or clogged SAS or cesspool |
| <u> </u> | <u>N/A</u> | Static liquid level in the distribution box above outlet invert due to an overloaded or clogged SAS or cesspool |
| <u> </u> | <u>No</u> | Liquid depth in cesspool is less than 6" below invert or available volume is less than 1/2 day flow |
| <u> </u> | <u>No</u> | Required pumping more than 4 times in the last year <u>NOT</u> due to clogged or obstructed pipe(s). Number of times pumped <u> </u> . |
| <u> </u> | <u>No</u> | Any portion of the SAS, cesspool or privy is below high ground water elevation. |
| <u> </u> | <u>No</u> | Any portion of cesspool or privy is within 100 feet of a surface water supply or tributary to a surface water supply. |
| <u> </u> | <u>No</u> | Any portion of a cesspool or privy is within a Zone 1 of a public well. |
| <u> </u> | <u>No</u> | Any portion of a cesspool or privy is within 50 feet of a private water supply well. |
| <u> </u> | <u>No</u> | Any portion of a cesspool or privy is less than 100 feet but greater than 50 feet from a private water supply well with no acceptable water quality analysis. [This system passes if the well water analysis, performed at a DEP certified laboratory, for coliform bacteria and volatile organic compounds indicates that the well is free from pollution from that facility and the presence of ammonia nitrogen and nitrate nitrogen is equal to or less than 5 ppm, provided that no other failure criteria are triggered. A copy of the analysis must be attached to this form.] |

Yes (Yes/No) The system fails. I have determined that one or more of the above failure criteria exist as described in 310 CMR 15.303, therefore the system fails. The system owner should contact the Board of Health to determine what will be necessary to correct the failure.

E. Large Systems:


To be considered a large system the system must serve a facility with a design flow of 10,000 gpd to 15,000 gpd.

You must indicate either "yes" or "no" to each of the following:

(The following criteria apply to large systems in addition to the criteria above)

- | yes | no | |
|------------|------------|--|
| <u> </u> | <u> </u> | the system is within 400 feet of a surface drinking water supply |
| <u> </u> | <u> </u> | the system is within 200 feet of a tributary to a surface drinking water supply |
| <u> </u> | <u> </u> | the system is located in a nitrogen sensitive area (Interim Wellhead Protection Area – JWPA) or a mapped Zone II of a public water supply well |

If you have answered "yes" to any question in Section E the system is considered a significant threat, or answered "yes" in Section D above the large system has failed. The owner or operator of any large system considered a significant threat under Section E or failed under Section D shall upgrade the system in accordance with 310 CMR 15.304. The system owner should contact the appropriate regional office of the Department.

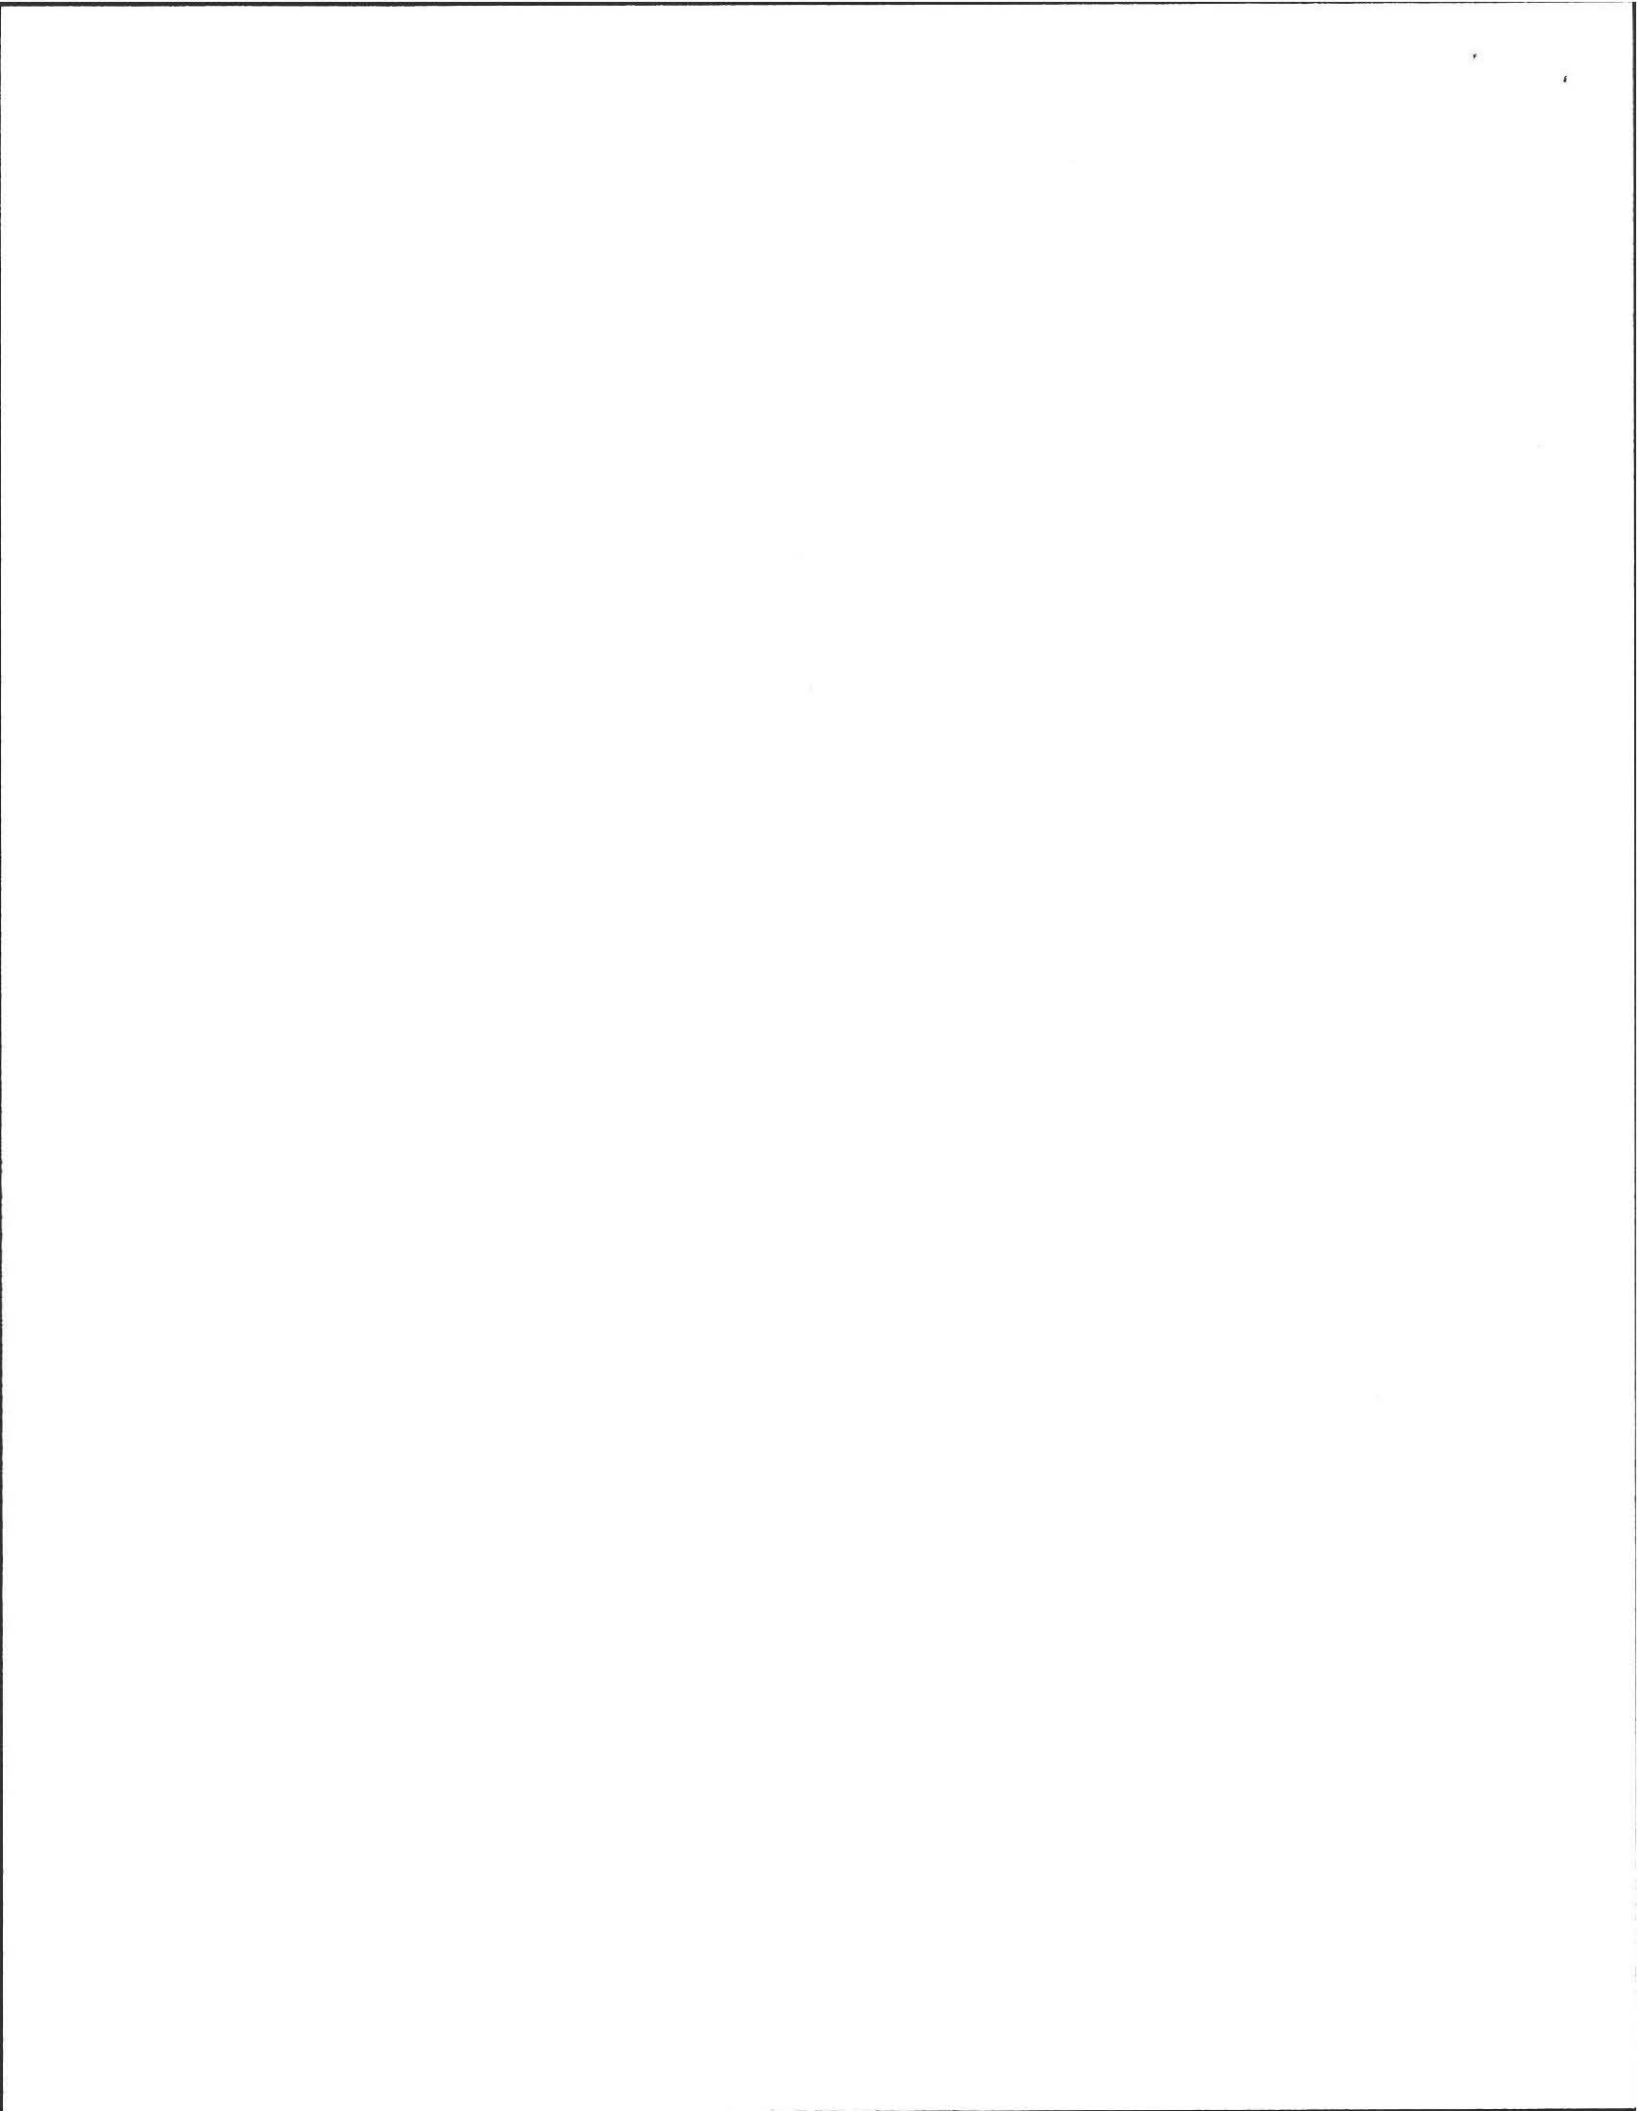

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART B
CHECKLIST

Property Address: 343 Montague Rd

Owner: Haweman


Date of Inspection: 7/18/01

Check if the following have been done. You must indicate "yes" or "no" as to each of the following:

- Yes No
- Pumping information was provided by the owner, occupant, or Board of Health
- Were any of the system components pumped out in the previous two weeks ?
- Has the system received normal flows in the previous two week period? *unoccupied 1 month +*
- Have large volumes of water been introduced to the system recently or as part of this inspection ?
- Were as built plans of the system obtained and examined? (If they were not available note as N/A)
- Was the facility or dwelling inspected for signs of sewage back up ?
- Was the site inspected for signs of break out ?
- Were all system components, excluding the SAS, located on site ?
- Were the septic tank manholes uncovered, opened, and the interior of the tank inspected for the condition of the baffles or tees, material of construction, dimensions, depth of liquid, depth of sludge and depth of scum ?
- Was the facility owner (and occupants if different from owner) provided with information on the proper maintenance of subsurface sewage disposal systems ?

The size and location of the Soil Absorption System (SAS) on the site has been determined based on:

- Yes no
- Existing information. For example, a plan at the Board of Health.
- Determined in the field (if any of the failure criteria related to Part C is at issue approximation of distance is unacceptable) [310 CMR 15.302(3)(b)]

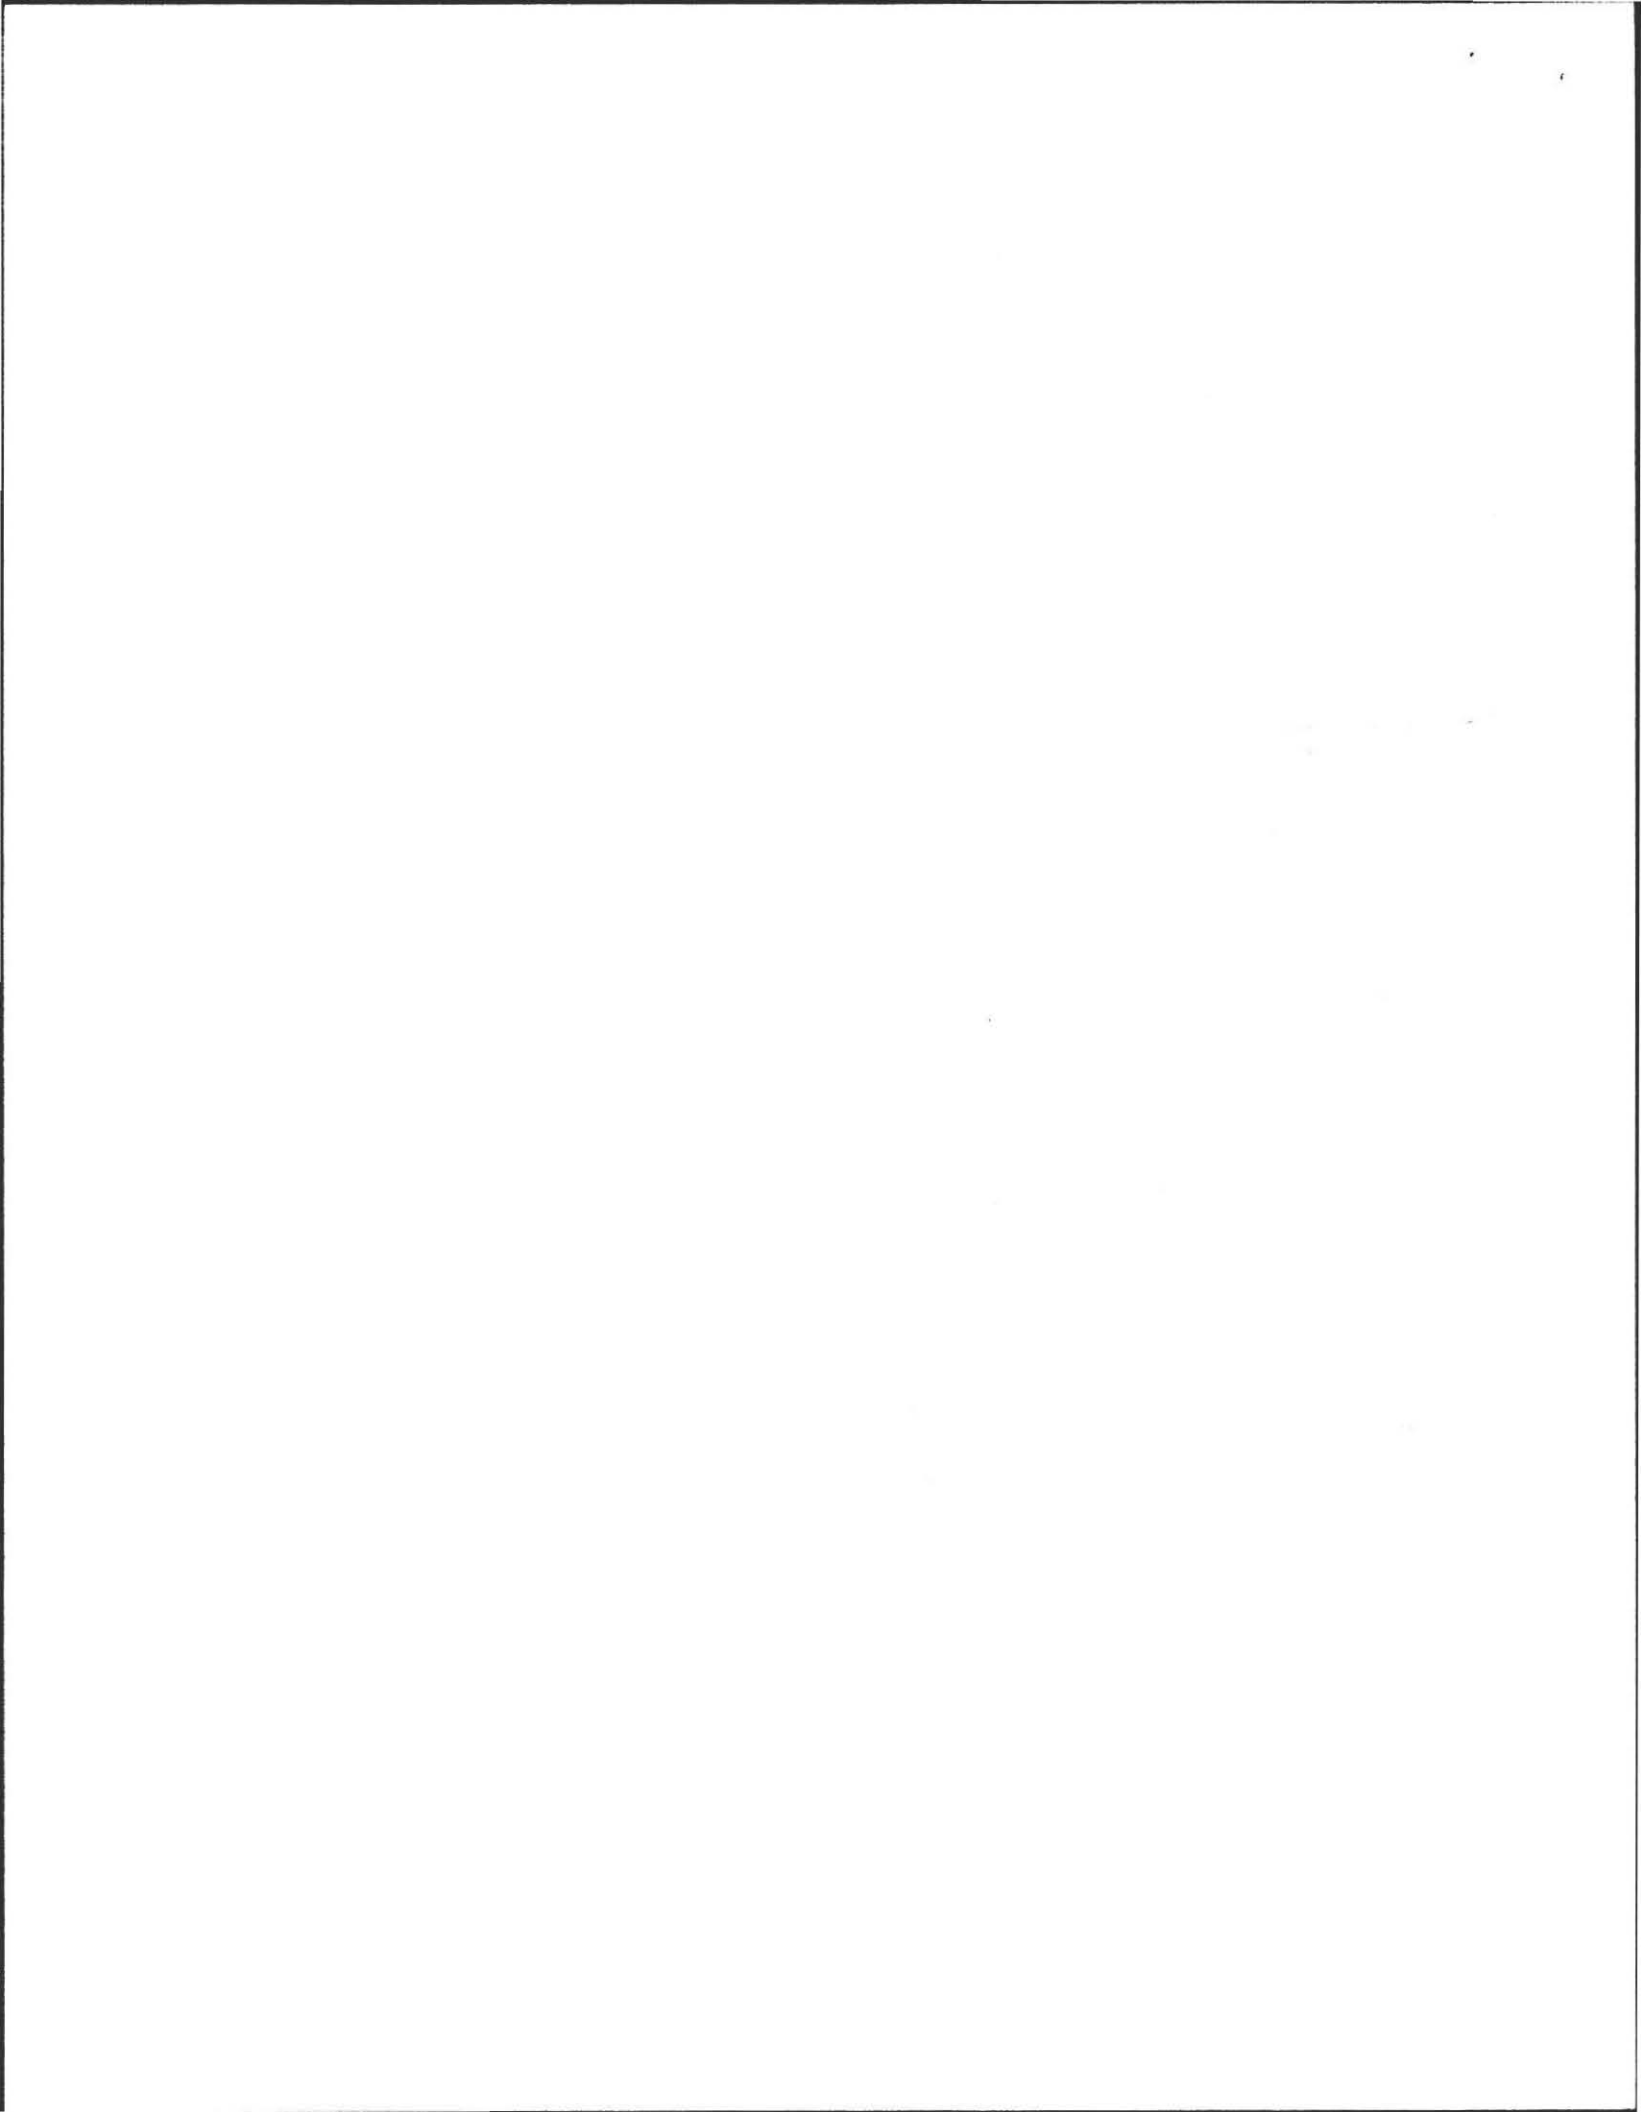

OFFICIAL INSPECTION FORM - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION

Property Address: 343 Montague Rd.

Owner: Havenwood

Date of Inspection: 7/19/01

FLOW CONDITIONS

RESIDENTIAL

Number of bedrooms (design): ? Number of bedrooms (actual): 4
DESIGN flow based on 310 CMR 15.203 (for example: 110 gpd x # of bedrooms): ?

Number of current residents: 5 until last month

Does residence have a garbage grinder (yes or no): No
Is laundry on a separate sewage system (yes or no): No [if yes separate inspection required]

Laundry system inspected (yes or no): -

Seasonal use: (yes or no): No

Water meter readings, if available (last 2 years usage (gpd)): N/A

Sump pump (yes or no): No

Last date of occupancy: 1 month

COMMERCIAL/INDUSTRIAL

Type of establishment: _____

Design flow (based on 310 CMR 15.203): _____ gpd

Basis of design flow (seats/persons/sqft, etc.): _____

Grease trap present (yes or no): _____

Industrial waste holding tank present (yes or no): _____

Non-sanitary waste discharged to the Title 5 system (yes or no): _____

Water meter readings, if available: _____

Last date of occupancy/use: _____

OTHER (describe): _____

GENERAL INFORMATION

Pumping Records

Source of information: 3 yrs ago + Nov. 2000

Was system pumped as part of the inspection (yes or no): Yes

If yes, volume pumped: 1500 gallons -- How was quantity pumped determined? - measured

Reason for pumping: Request

TYPE OF SYSTEM

Septic tank, distribution box, soil absorption system

Single cesspool

Overflow cesspool

Privy

Shared system (yes or no) (if yes, attach previous inspection records, if any)

Innovative/Alternative technology. Attach a copy of the current operation and maintenance contract (to be obtained from system owner)


Tight tank Attach a copy of the DEP approval

Other (describe): _____

Approximate age of all components, date installed (if known) and source of information:

35 yrs. (SITANK 3 yrs)

Were sewage odors detected when arriving at the site (yes or no): _____

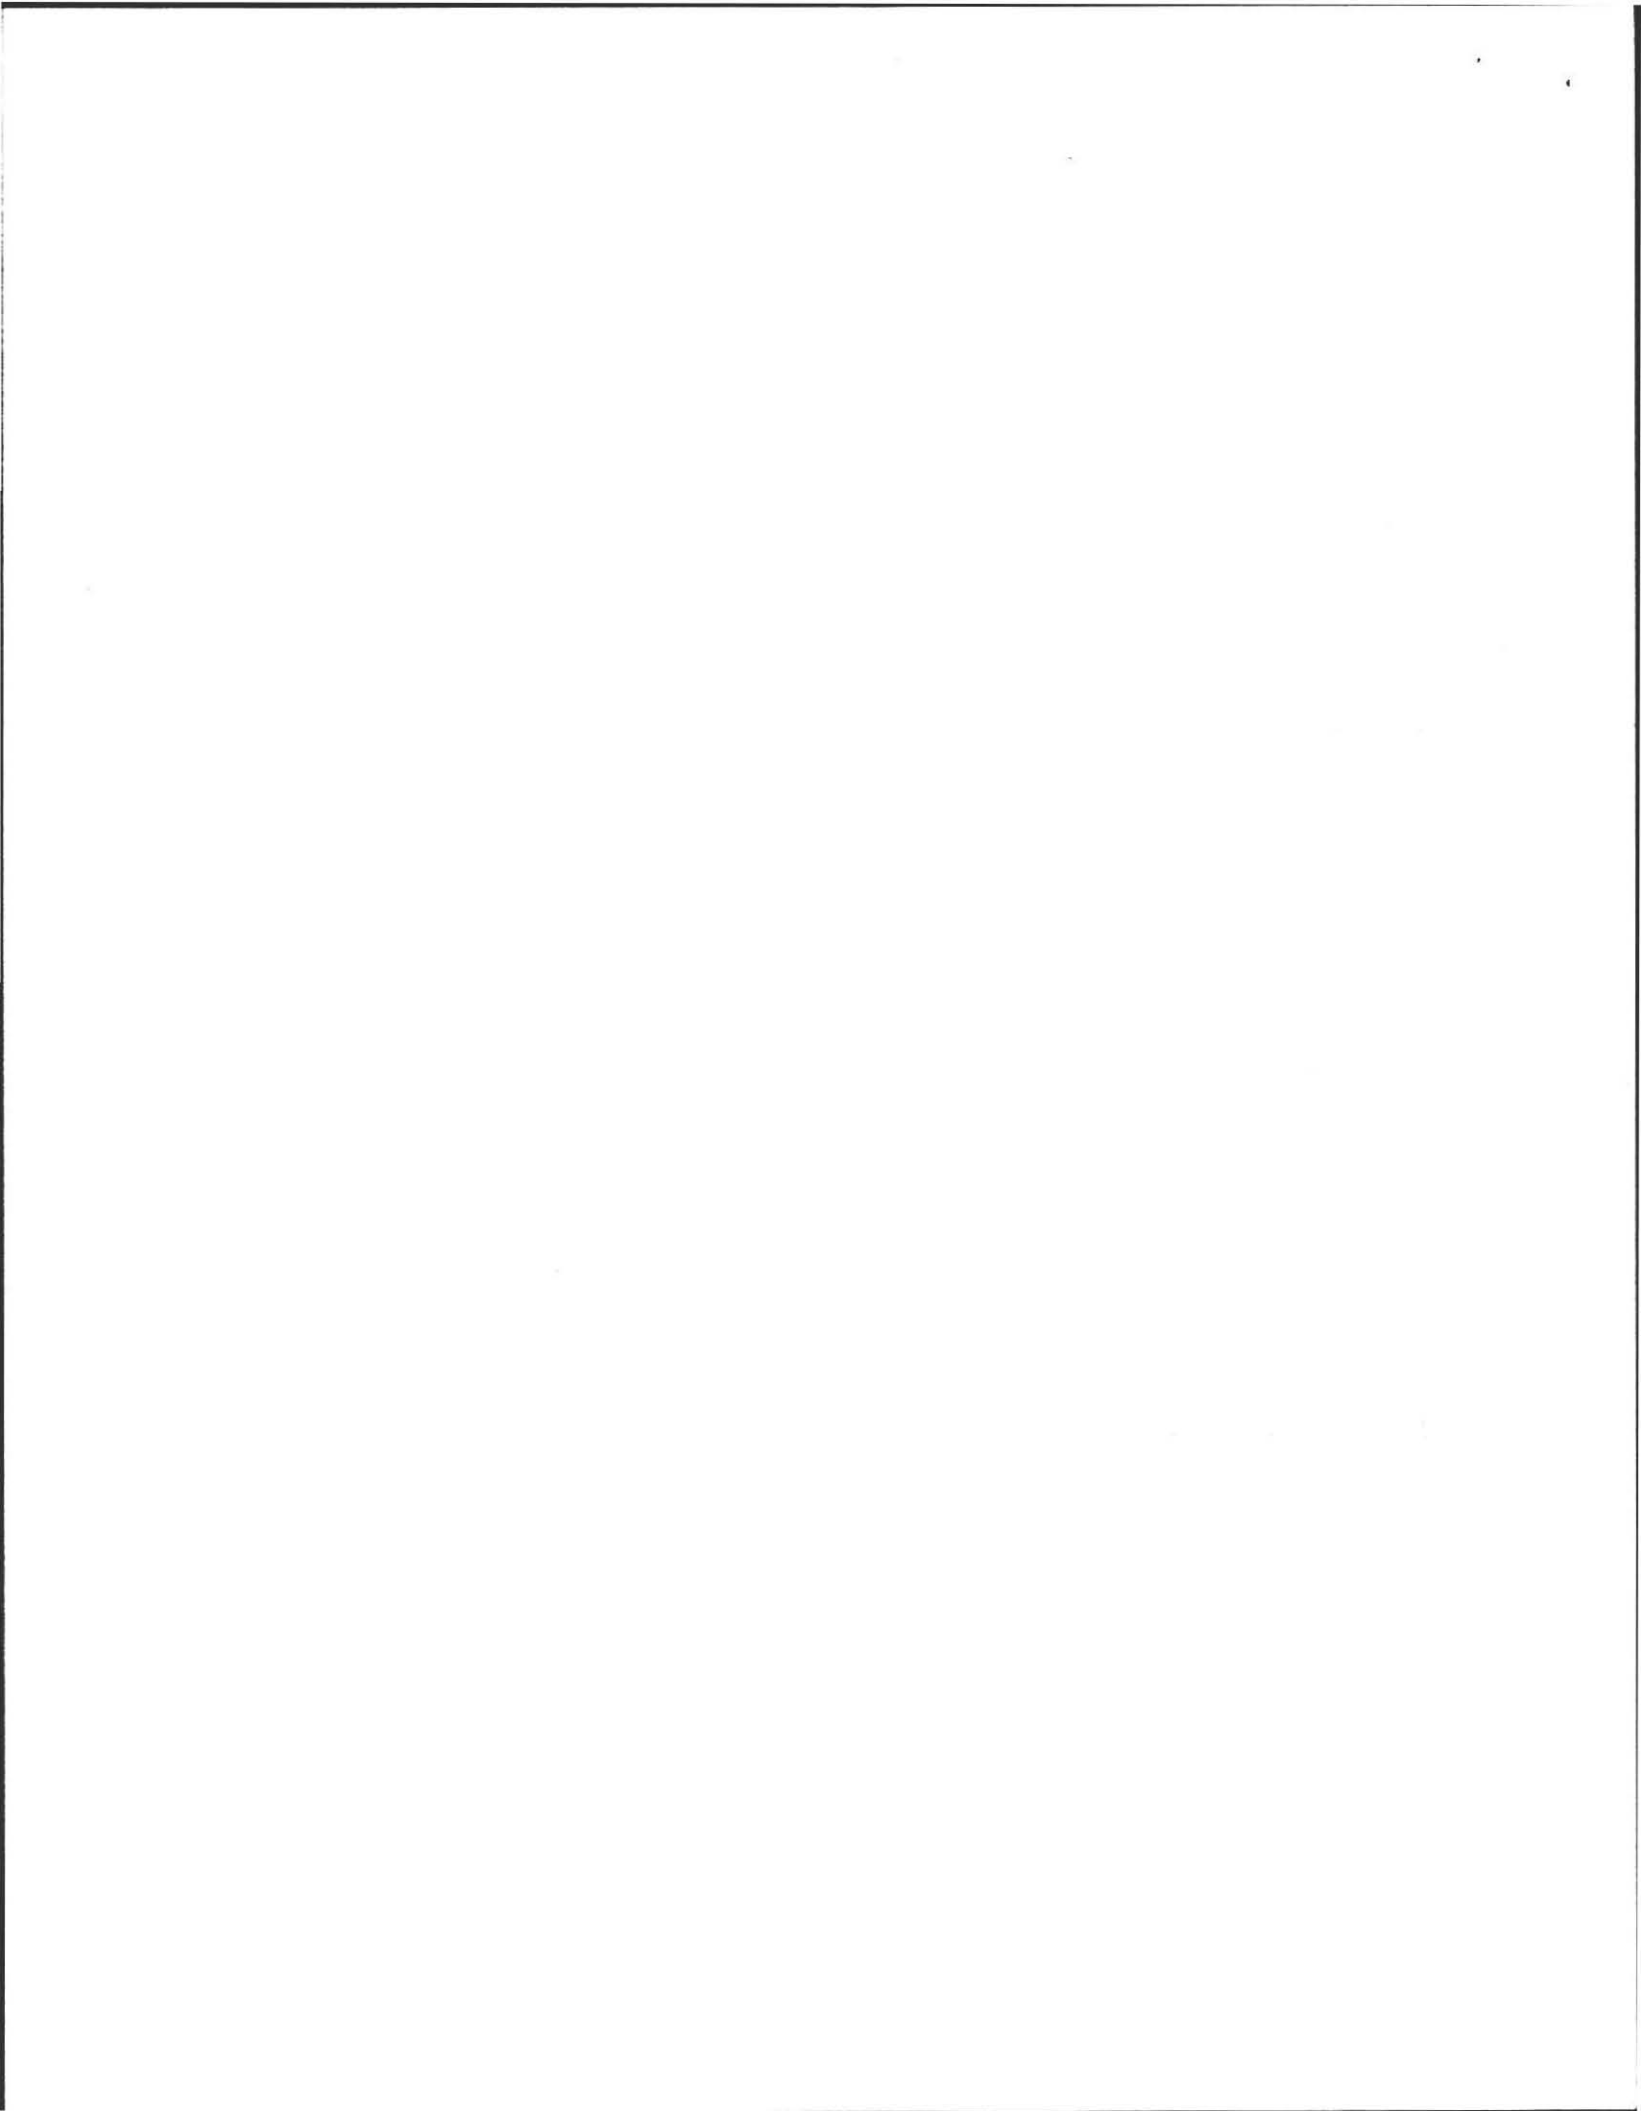

OFFICIAL INSPECTION FORM - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C

SYSTEM INFORMATION (continued)

Property Address: 343 Montague Rd.

Owner: Havenwood

Date of Inspection: 7/2/01

BUILDING SEWER (locate on site plan)

Depth below grade: 10" +

Materials of construction: cast iron 40 PVC other (explain): _____

Distance from private water supply well or suction line: 10' +

Comments (on condition of joints, venting, evidence of leakage, etc.):

SEPTIC TANK: Yes (locate on site plan)

Depth below grade: 10"

Material of construction: concrete metal fiberglass polyethylene
 other(explain) _____

If tank is metal list age: _____ Is age confirmed by a Certificate of Compliance (yes or no): _____ (attach a copy of certificate)

Dimensions: 10.5 x 5.0 x 4.5'

Sludge depth: 1"

Distance from top of sludge to bottom of outlet tee or baffle: 40"

Scum thickness: 1"

Distance from top of scum to top of outlet tee or baffle: 6"

Distance from bottom of scum to bottom of outlet tee or baffle: 12"

How were dimensions determined: MEAS

Comments (on pumping recommendations, inlet and outlet tee or baffle condition, structural integrity, liquid levels as related to outlet invert, evidence of leakage, etc.):

New S. TANK in 1998

GREASE TRAP: No (locate on site plan)

Depth below grade: _____

Material of construction: concrete metal fiberglass polyethylene other (explain): _____

Dimensions: _____


Scum thickness: _____

Distance from top of scum to top of outlet tee or baffle: _____

Distance from bottom of scum to bottom of outlet tee or baffle: _____

Date of last pumping: _____

Comments (on pumping recommendations, inlet and outlet tee or baffle condition, structural integrity, liquid levels as related to outlet invert, evidence of leakage, etc.):

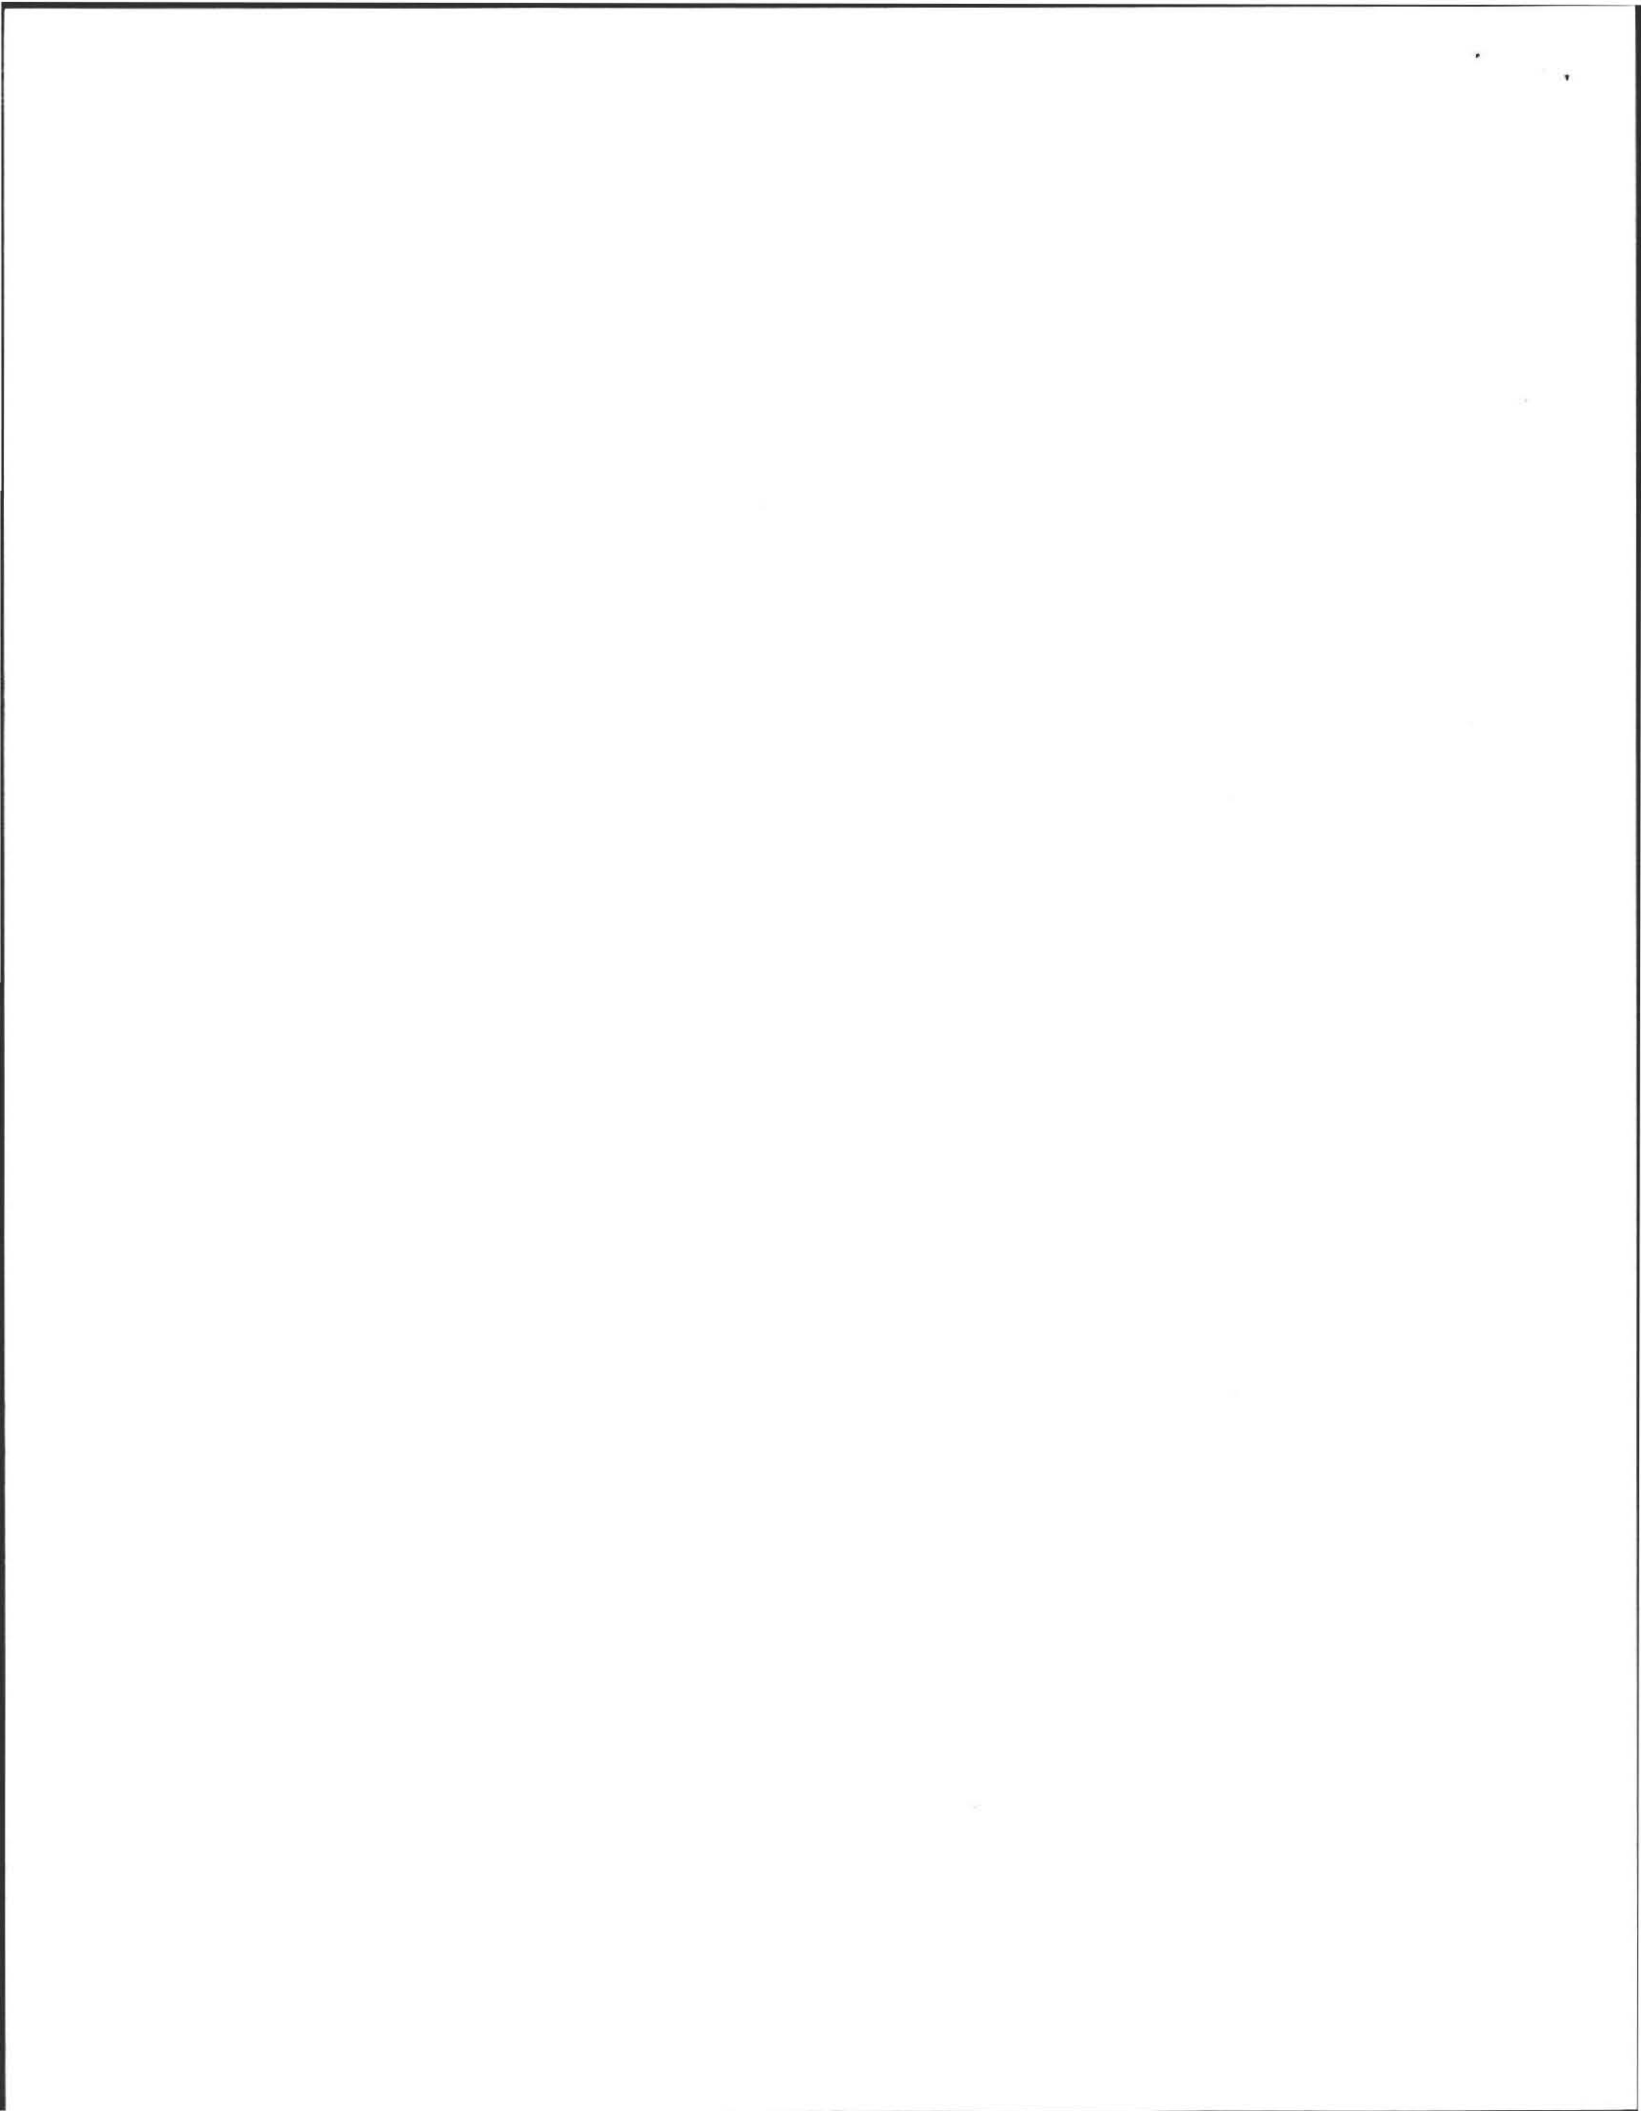

OFFICIAL INSPECTION FORM - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION (continued)

Property Address: 343 Montague rd.

Owner: Haverdew

Date of Inspection: 7/18/01

TIGHT or HOLDING TANK: No (tank must be pumped at time of inspection)(locate on site plan)

Depth below grade: _____

Material of construction: _____ concrete _____ metal _____ fiberglass _____ polyethylene _____ other(explain): _____

Dimensions: _____

Capacity: _____ gallons

Design Flow: _____ gallons/day

Alarm present (yes or no): _____

Alarm level: _____ Alarm in working order (yes or no): _____

Date of last pumping: _____

Comments (condition of alarm and float switches, etc.): _____

DISTRIBUTION BOX: No (if present must be opened)(locate on site plan)

Depth of liquid level above outlet invert: _____

Comments (note if box is level and distribution to outlets equal, any evidence of solids carryover, any evidence of leakage into or out of box, etc.): _____

PUMP CHAMBER: No (locate on site plan)

Pumps in working order (yes or no): _____

Alarms in working order (yes or no): _____

Comments (note condition of pump chamber, condition of pumps and appurtenances, etc.): _____

11

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION (continued)

Property Address: 343 Montague Rd.

Owner: Havemo

Date of Inspection: 7/18/01

SOIL ABSORPTION SYSTEM (SAS): Yes (locate on site plan, excavation not required)

If SAS not located explain why:

Type

- 1 leaching pits, number: (1) Block Buil. 48" x 90" D - 2.5' LIQUID-
- leaching chambers, number: _____
- leaching galleries, number: _____
- leaching trenches, number, length: _____
- leaching fields, number, dimensions: _____
- overflow cesspool, number: _____
- innovative/alternative system Type/name of technology: _____

Comments (note condition of soil, signs of hydraulic failure, level of ponding, damp soil, condition of vegetation, etc.):
STAINING over inlet pipe was visible.

CESSPOOLS: No (cesspool must be pumped as part of inspection)(locate on site plan)


- Number and configuration: _____
- Depth – top of liquid to inlet invert: _____
- Depth of solids layer: _____
- Depth of scum layer: _____
- Dimensions of cesspool: _____
- Materials of construction: _____
- Indication of groundwater inflow (yes or no): _____

Comments (note condition of soil, signs of hydraulic failure, level of ponding, condition of vegetation, etc.):

PRIVY: No (locate on site plan)

- Materials of construction: _____
- Dimensions: _____
- Depth of solids: _____

Comments (note condition of soil, signs of hydraulic failure, level of ponding, condition of vegetation, etc.):

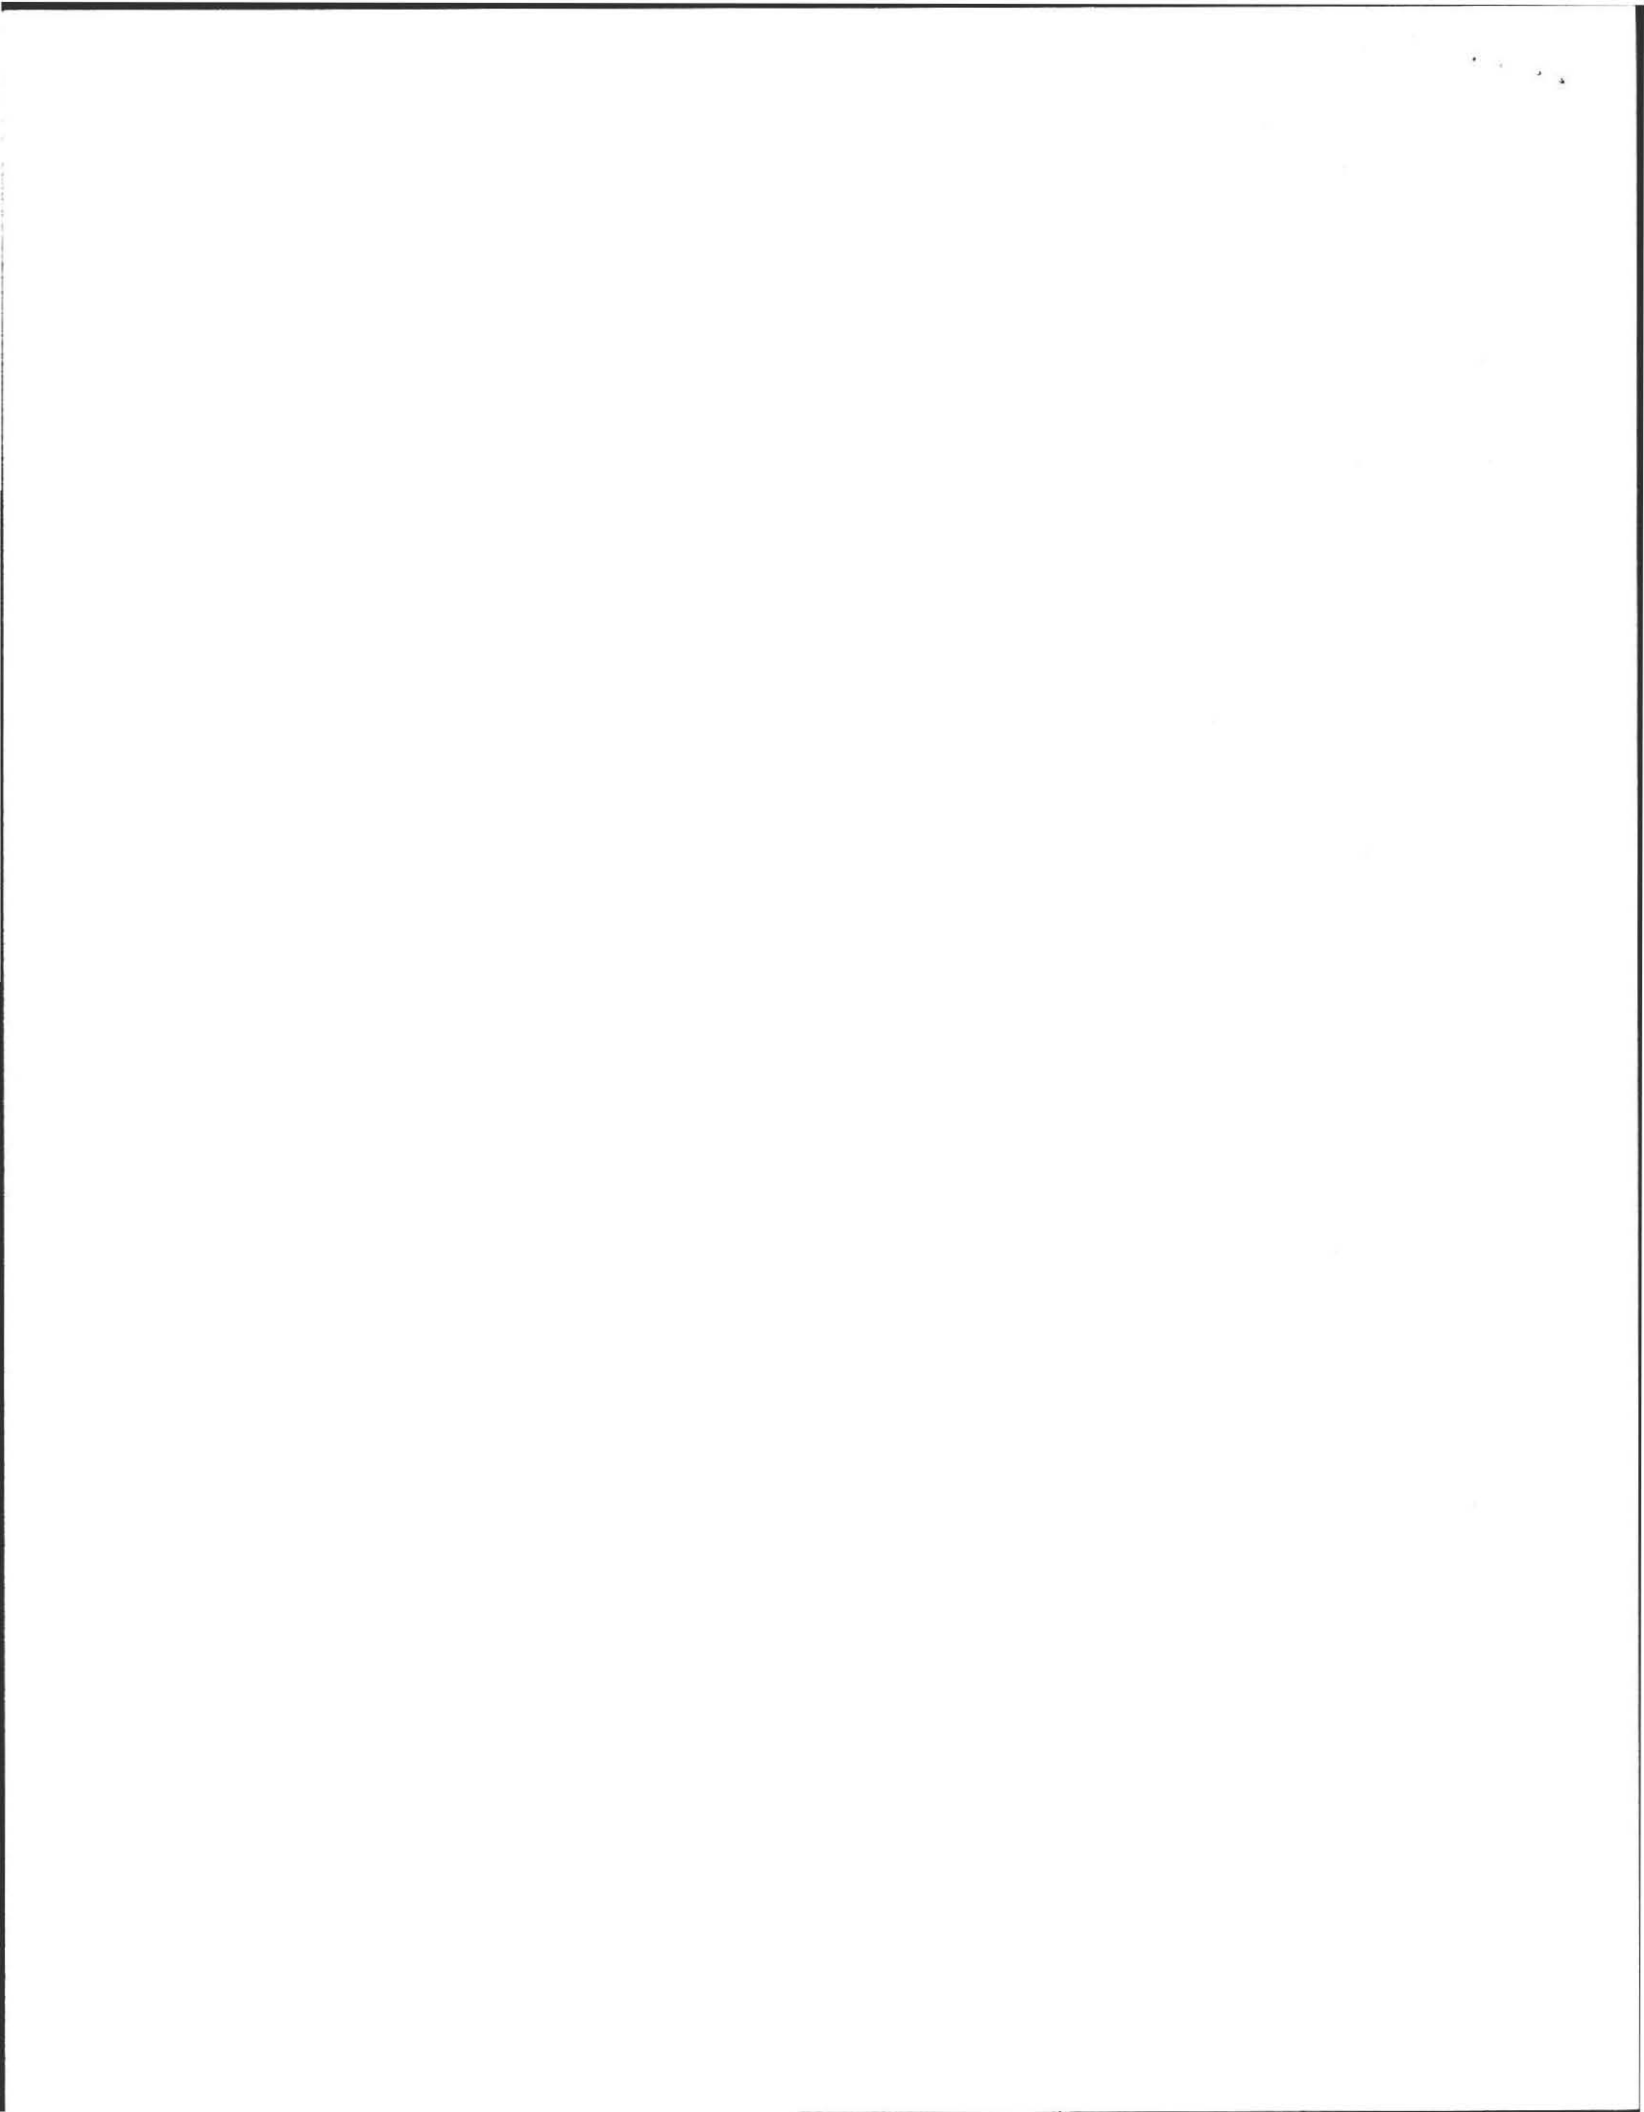

OFFICIAL INSPECTION FORM - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION (continued)

Property Address: 343 Montague Rd.


Owner: Hallman

Date of Inspection: 7/13/01

SKETCH OF SEWAGE DISPOSAL SYSTEM

Provide a sketch of the sewage disposal system including ties to at least two permanent reference landmarks or benchmarks. Locate all wells within 100 feet. Locate where public water supply enters the building.

See attached S. tank replacement plan (1998)

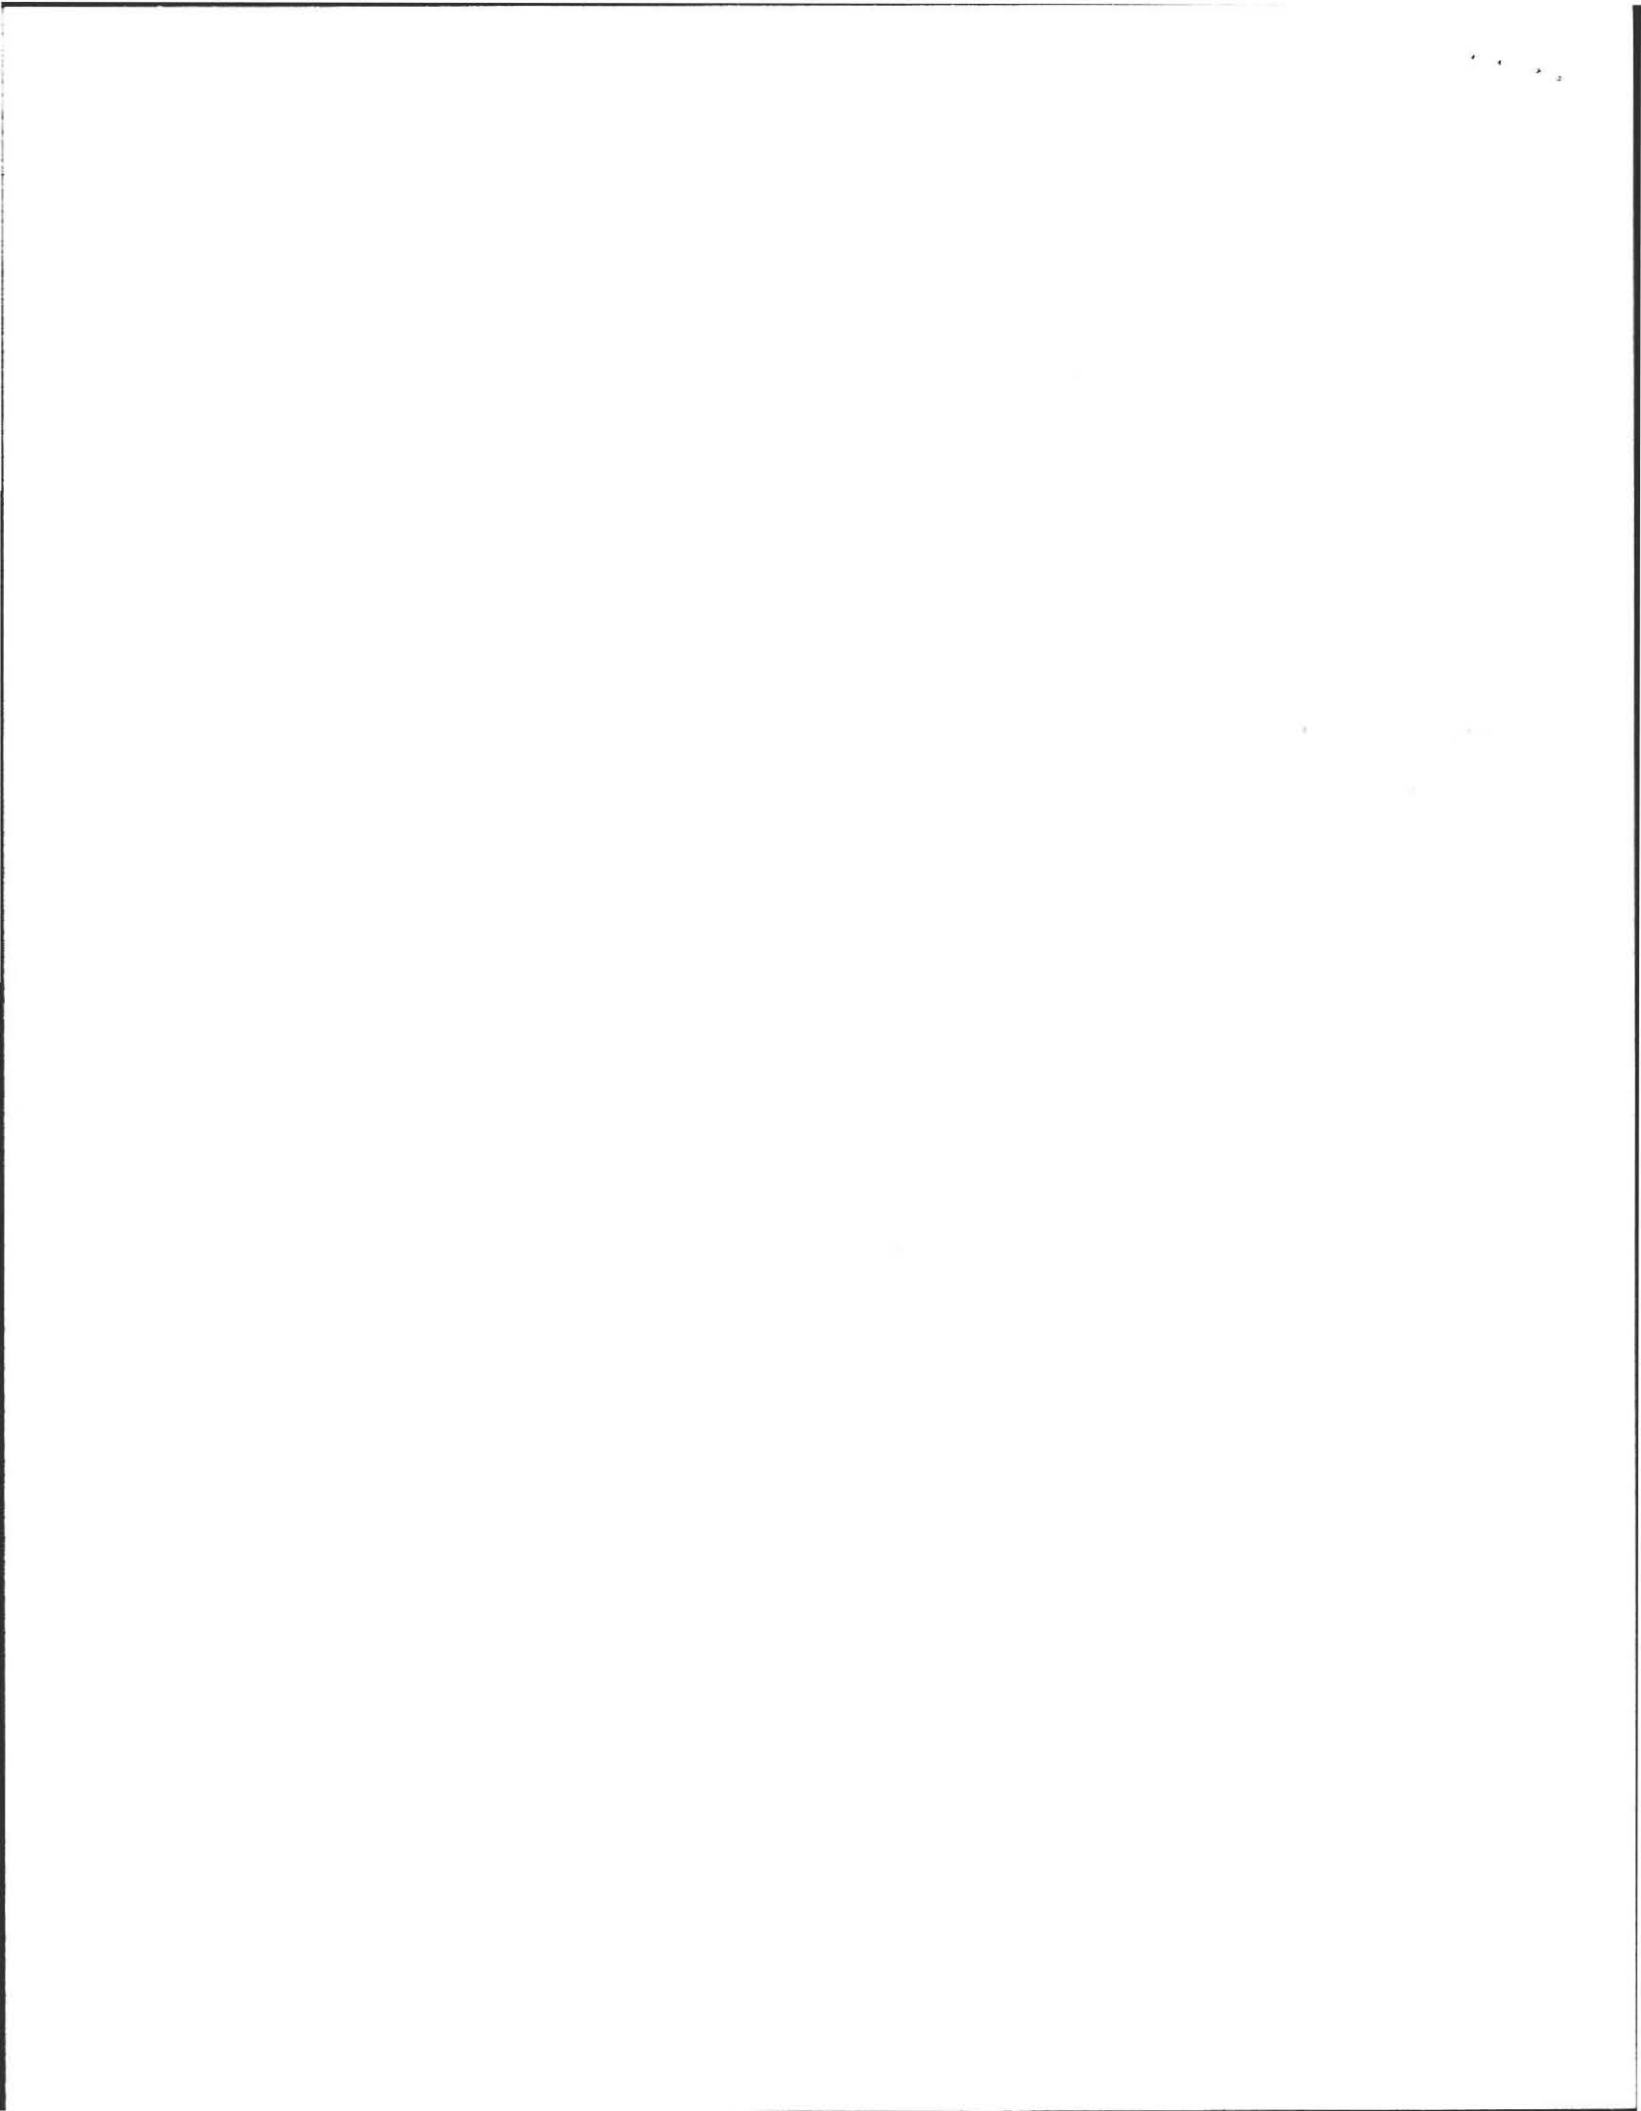

OFFICIAL INSPECTION FORM - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C

SYSTEM INFORMATION (continued)

Property Address: 345 Montague rd

Owner: Hawes

Date of Inspection: 7/18/01

SITE EXAM

Slope

Surface water

Check cellar

Shallow wells


Estimated depth to ground water 8^{1/2} feet



Please indicate (check) all methods used to determine the high ground water elevation:

- Obtained from system design plans on record - If checked, date of design plan reviewed: _____
- Observed site (abutting property/observation hole within 150 feet of SAS)
- Checked with local Board of Health-explain: _____
- Checked with local excavators, installers- (attach documentation)
- Accessed USGS database-explain: _____

You must describe how you established the high ground water elevation:

Nearby / Adjacent Deepholes

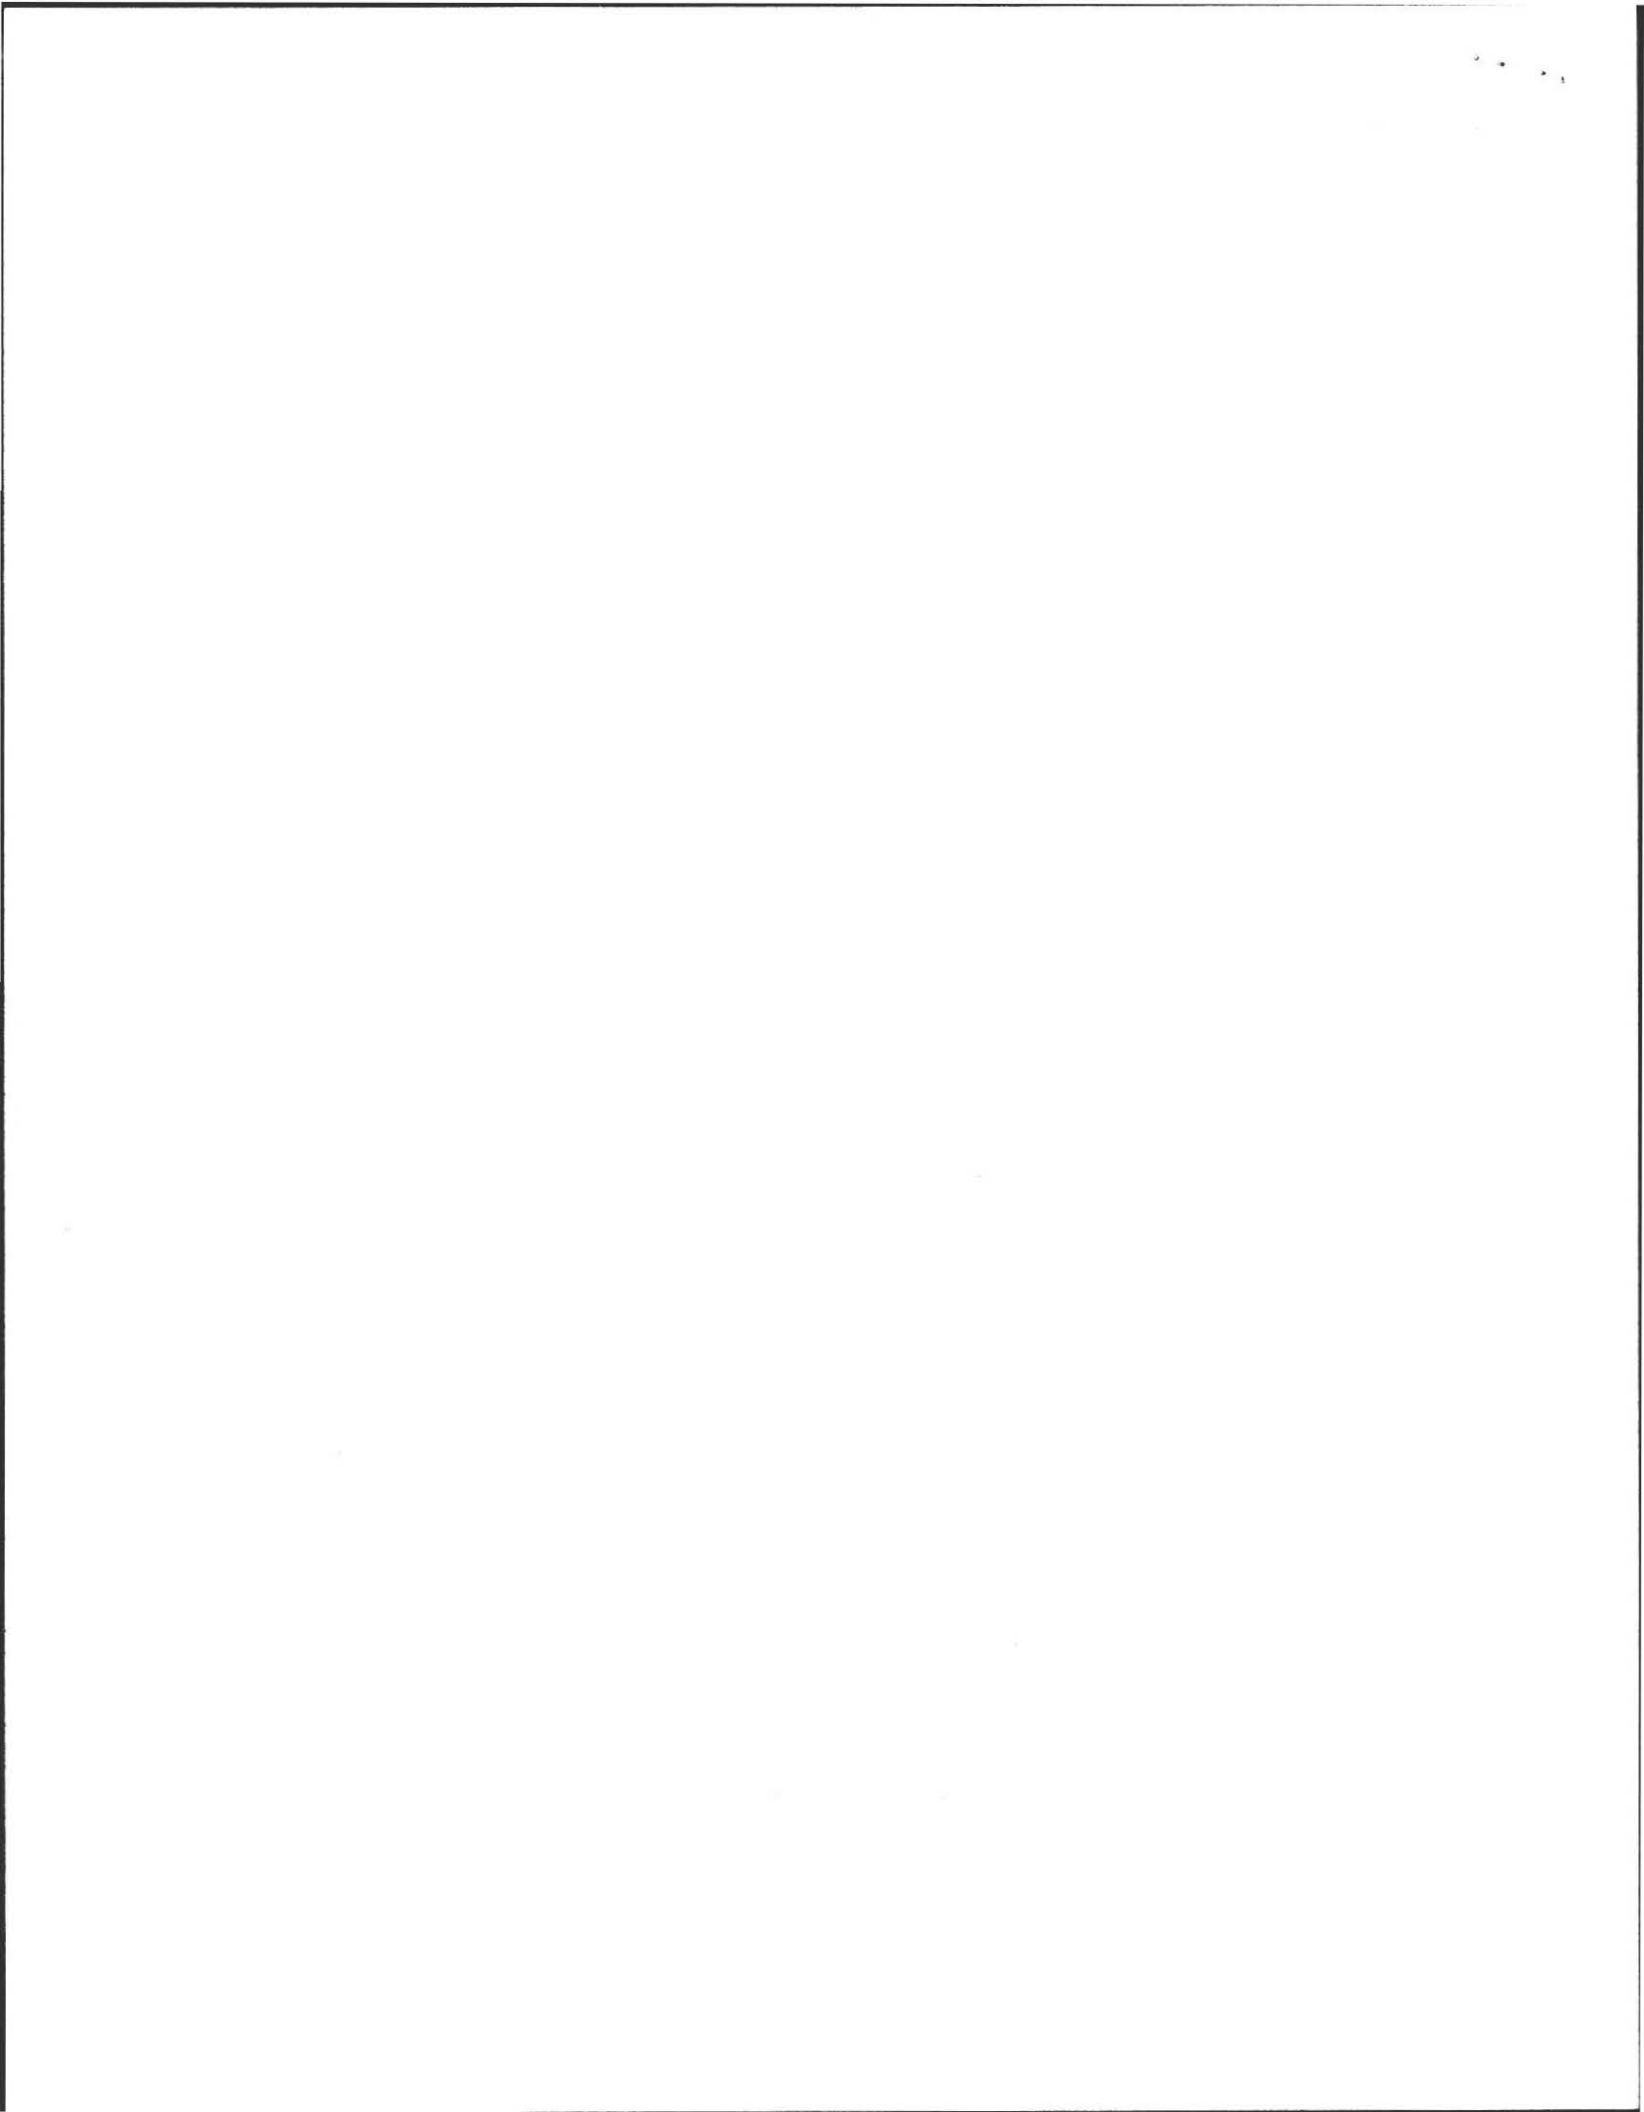

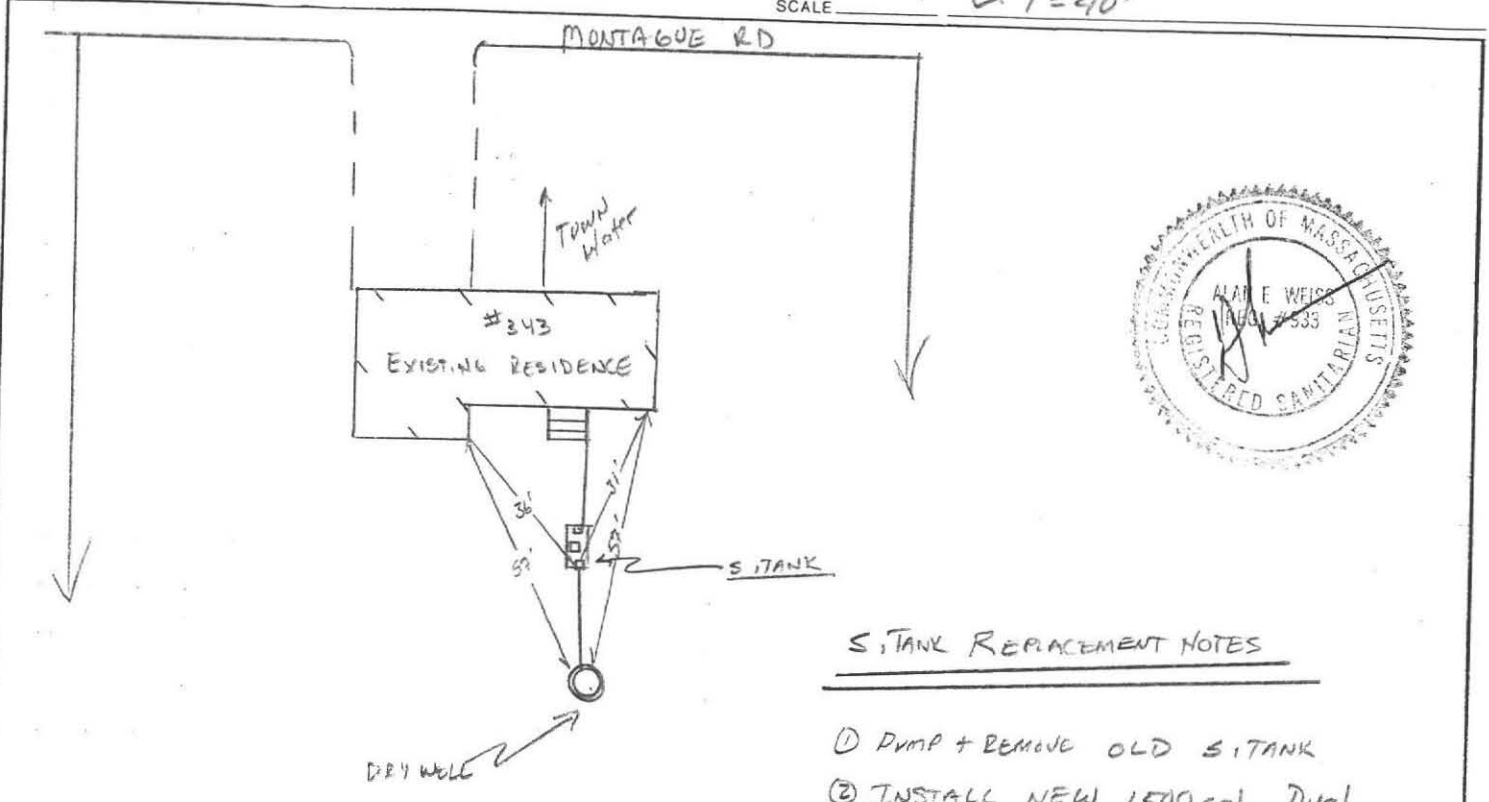



SITANK REPLACEMENT NOTES

- ① PUMP + REMOVE OLD SITANK
- ② INSTALL NEW 1500 gal. Dual chamber SITANK.
* INSTALL ON LEVEL base w/ 6" of 3/4" stone
- ③ Refill SITANK w/ H₂O, Run H₂O
- ④ Engineer + BOH TO Reinspect SITANK AND drywell.

* SITANK Elevation (Same as prior SITANK).
- INLET PIPE 0.02 pitch (MIN), OUTLET PIPE 0.005 pitch (MIN)

TYPICAL 2 CHAMBER S. TANK OR EQUIV.

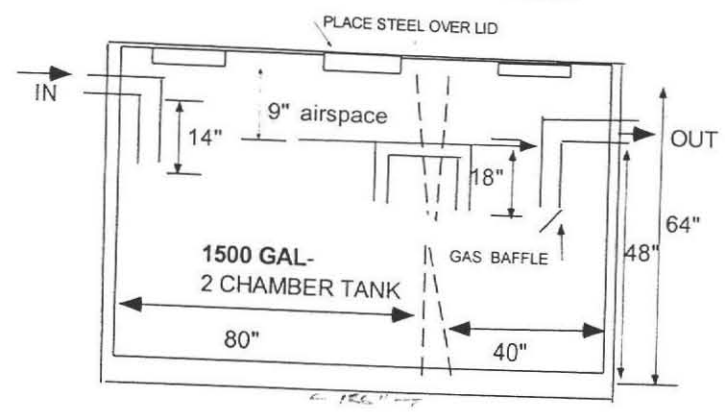

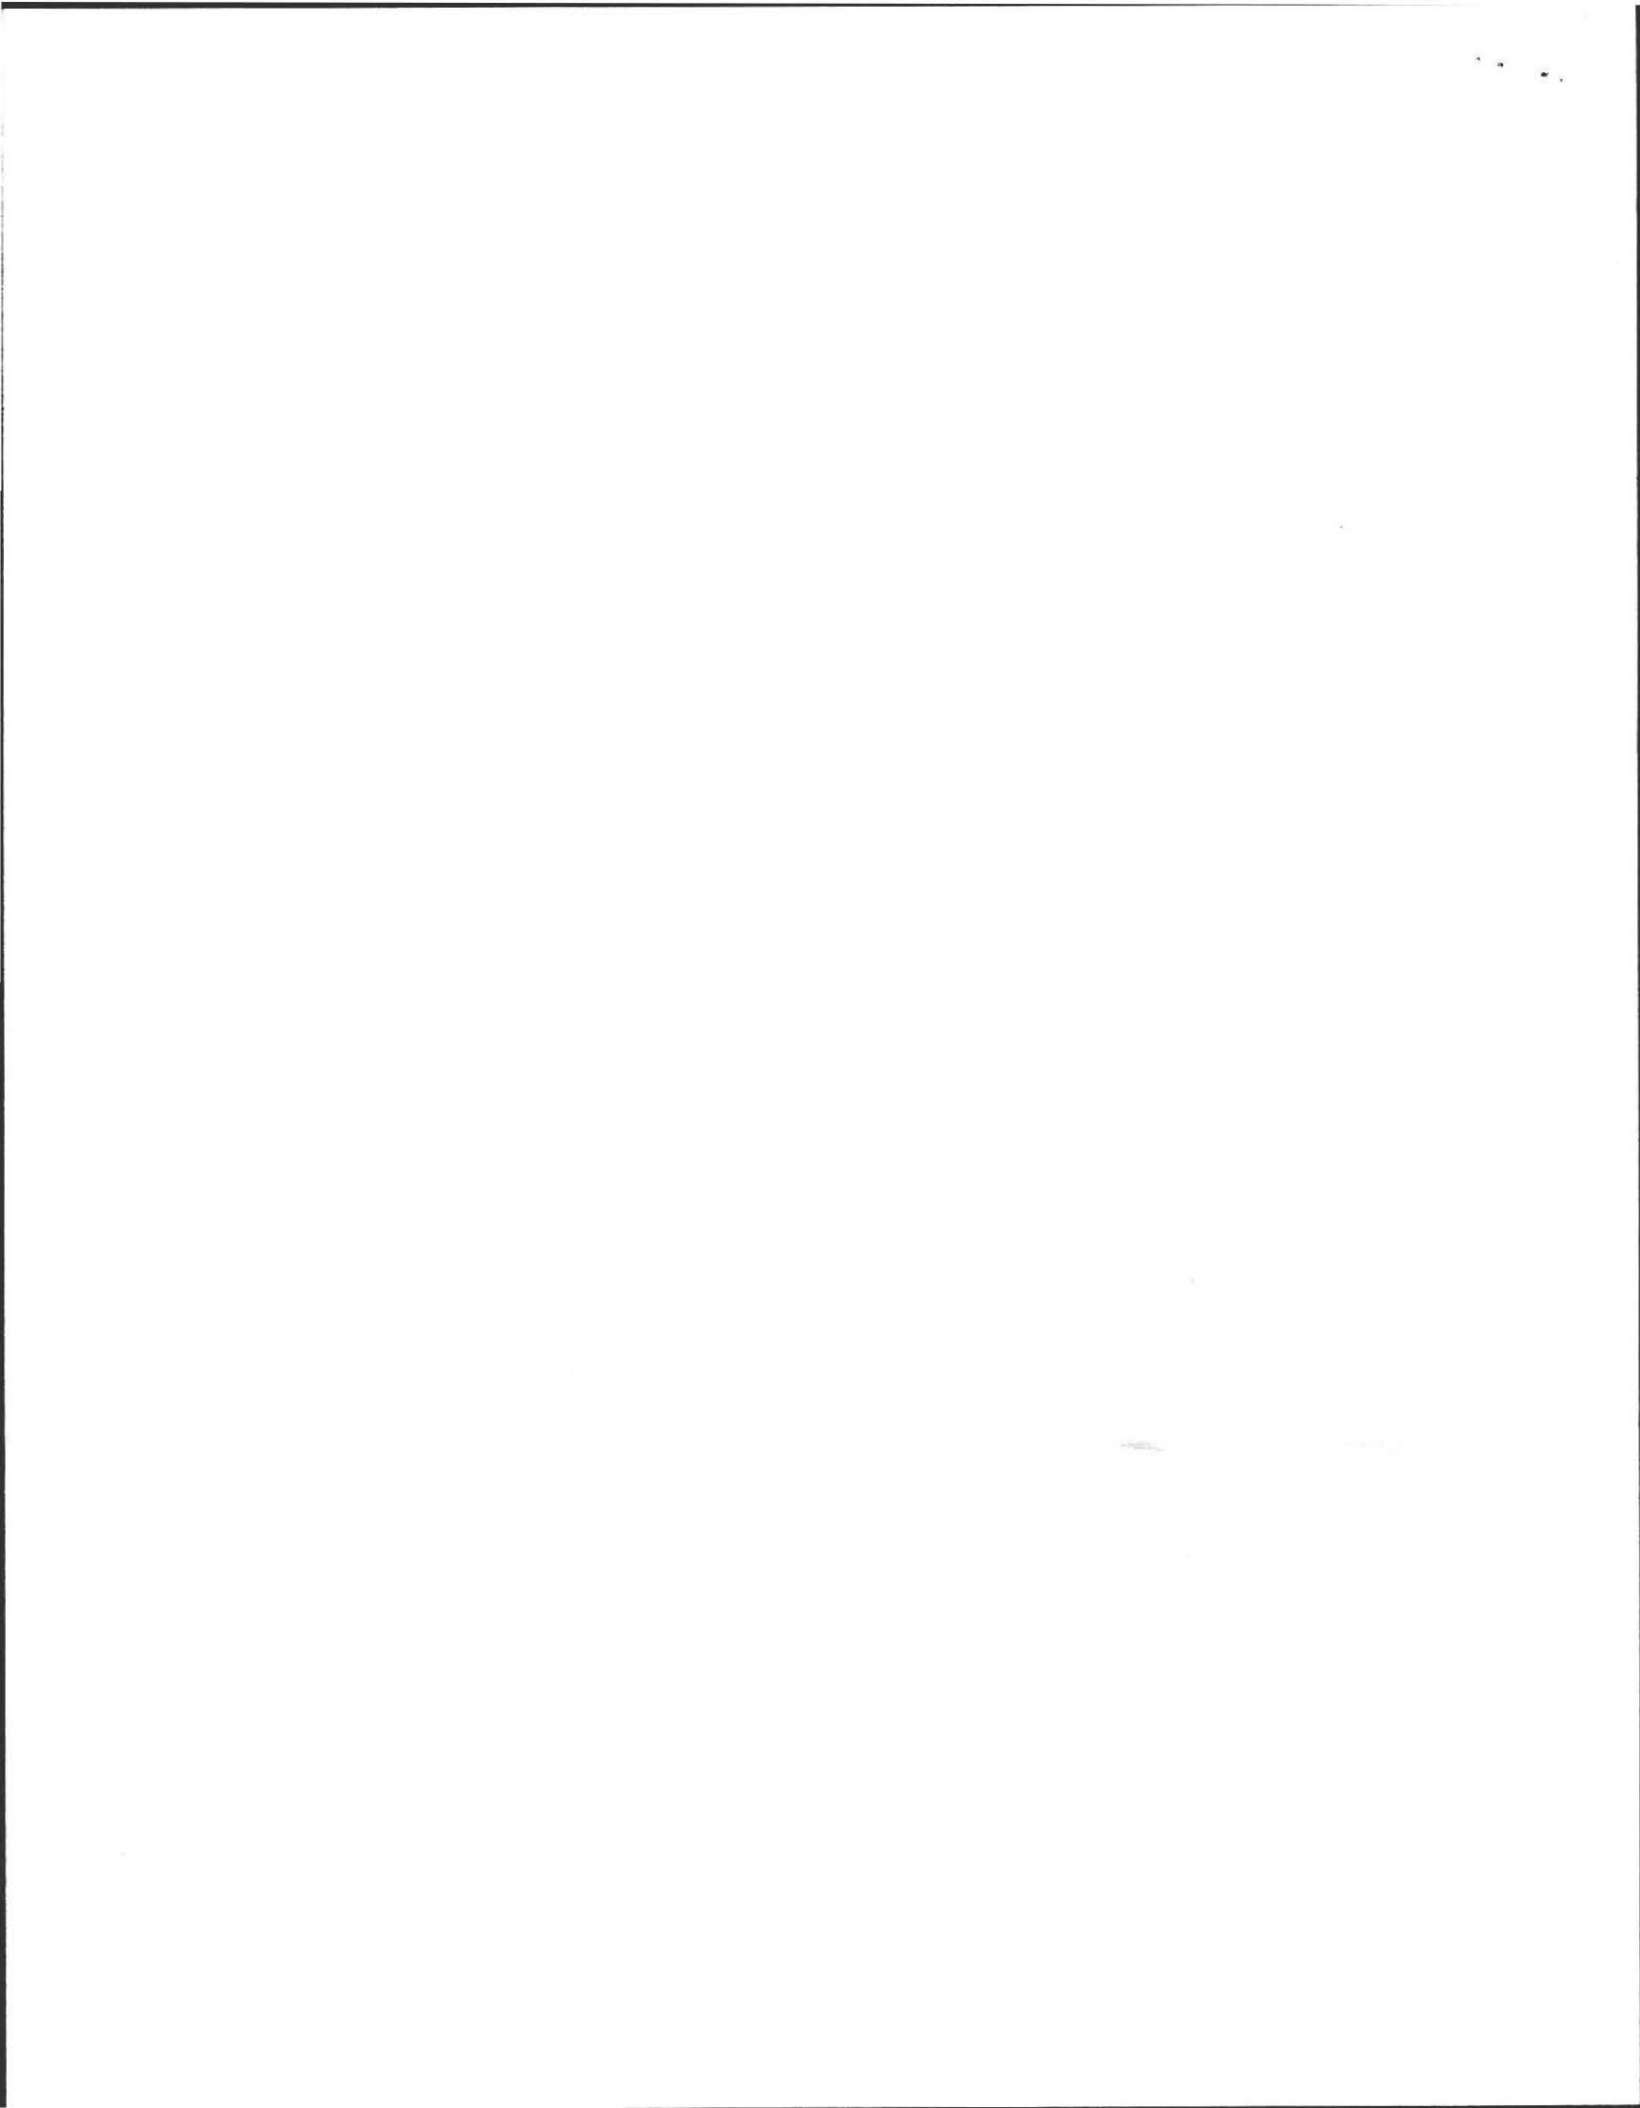

8/1/01
12:04:56 PM

**PAYMENT HISTORY FOR CASE
SPT2002-00004**

343
Montague

Fee Type: PERC **Description:** Perc Test Fee **Total Fee:** **\$150.00**

Date Paid	Receipt#	Check#	Recorded By	Amount Paid		
7/27/01	1783	0326	DDC	\$150.00		
			Total Paid:	\$150.00	Due:	\$0.00

Fee Type: PLAN **Description:** Plan Review Fee (1) **Total Fee:** **\$75.00**

Date Paid	Receipt#	Check#	Recorded By	Amount Paid		
7/27/01	1783	0326	DDC	\$75.00		
			Total Paid:	\$75.00	Due:	\$0.00

Totals for SPT2002-00004:

Fees: **\$225.00** **Paid:** **\$225.00** **Due:** **\$0.00**

8/30 no-certificate of compliance - yet
- add cert. of compliance


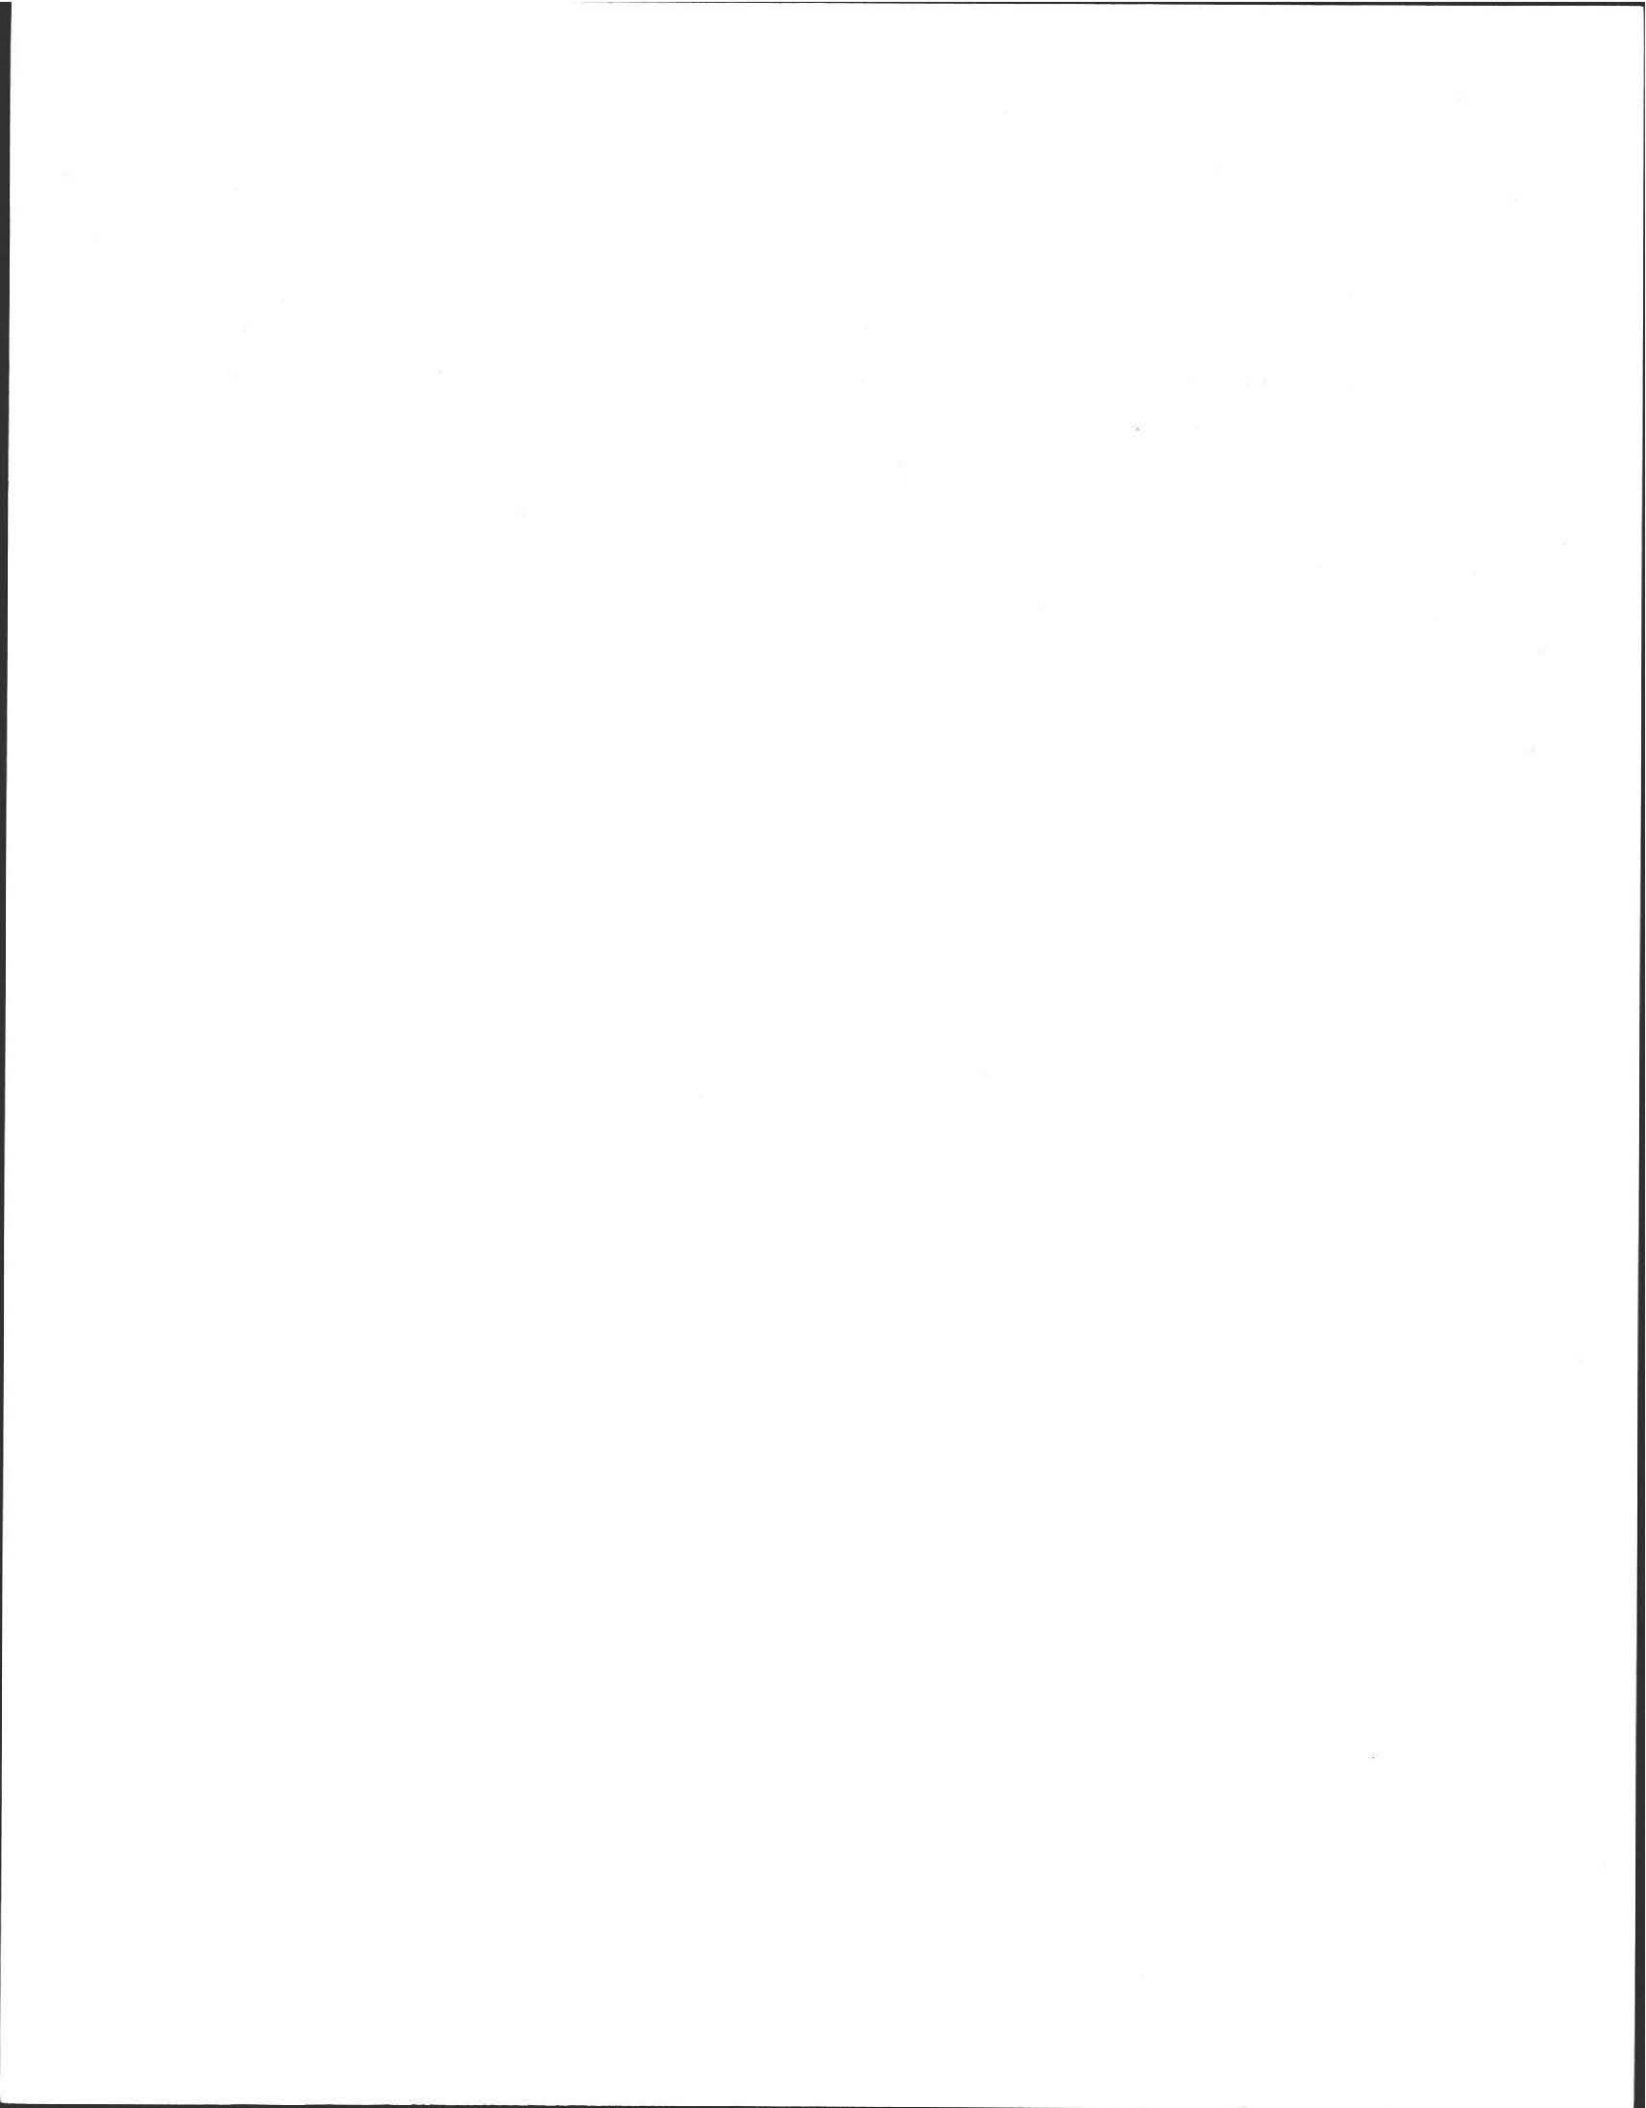


FIGURE 1: SITE LOCUS

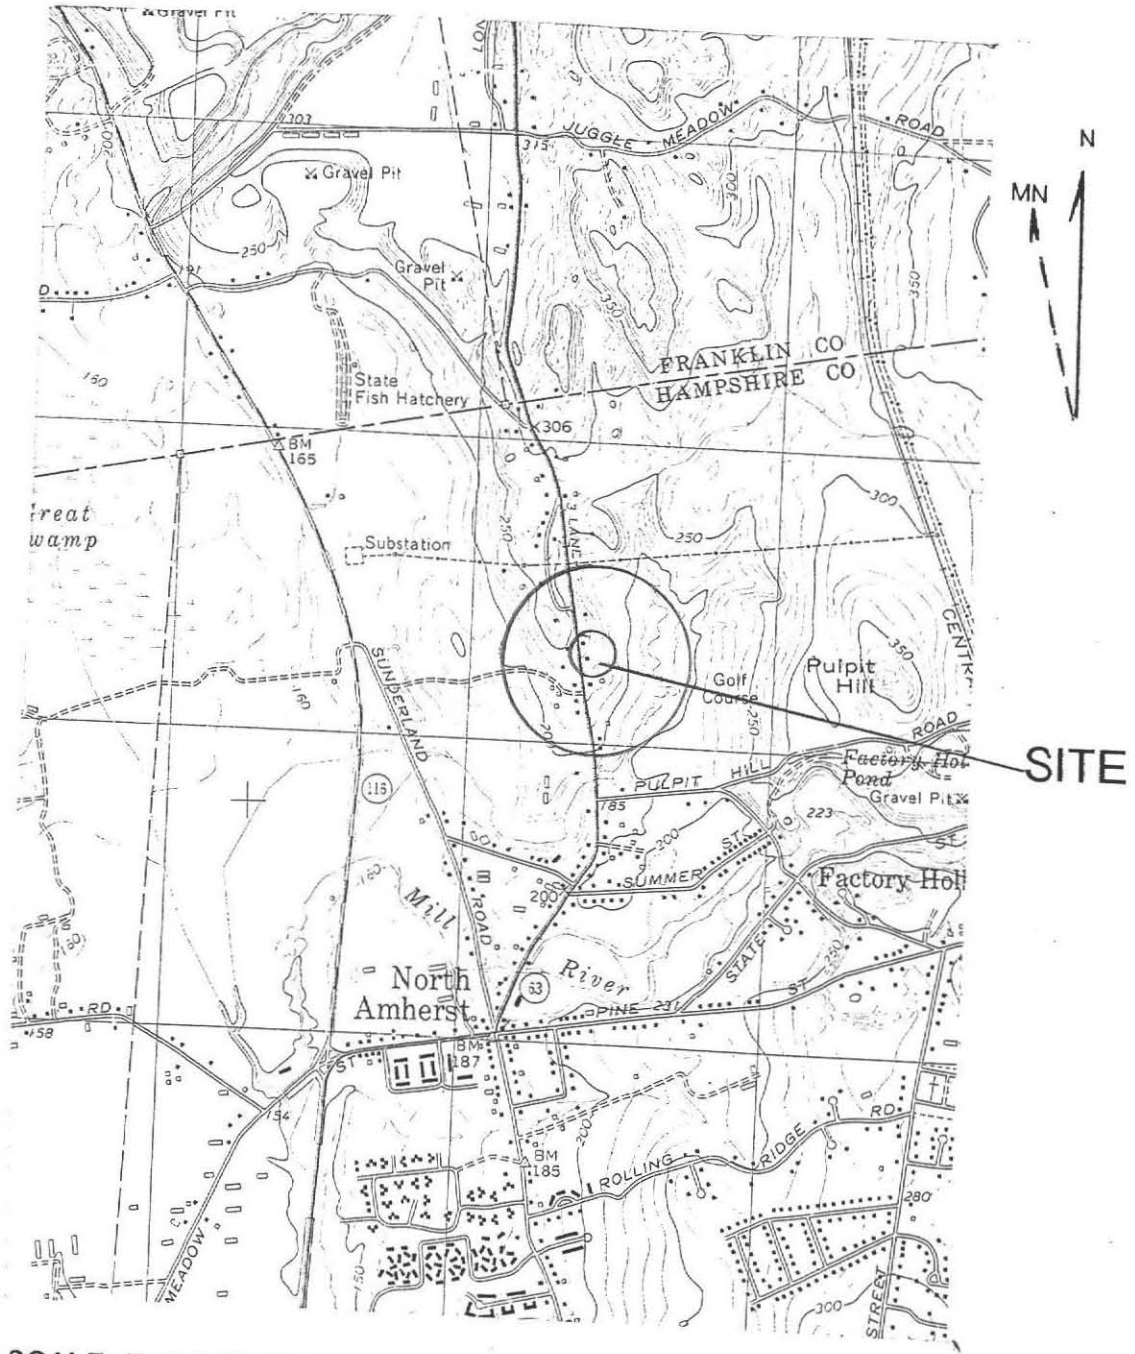

SCALE: 1"=2,083 FT.

USGS 7.5 MIN. QUAD.

0 FEET 2000

COLD SPRING ENVIRONMENTAL INC.

