

751 NORTHEAST STREET
TOLZDORF

PLAN REVIEWED



APP. - 15788
Batch - 2249

October 2012 INVOICE

AMHERST PUBLIC HEALTH DEPARTMENT

Bangs Community Center
70 Boltwood Walk
Amherst, MA 01002

DATE: October 16, 2012

TO Robert Krakower & Rosalie Burrows Jtwros
751 North East Street
Amherst, MA 01002

RE: Invoice for Septic Title V witness

Services provided by Edmund Smith


PAYMENT TERMS: Due Upon Receipt

QUANTITY	DESCRIPTION	UNIT PRICE	LINE TOTAL
1.00	Septic Title V witness - performed 10/16/12	\$ 200.00	\$ 200.00
	this invoice is due - please send check to address above		
	thank you		

SUBTOTAL	\$ 200.00
SALES TAX	
TOTAL	\$ 200.00

*My apologies -
fee is \$200 not \$300.
Please send a replacement
check for \$200 instead of the \$300
check (enclosed) you gave me today.*

*thanks!
Ed Smith
259-3153*

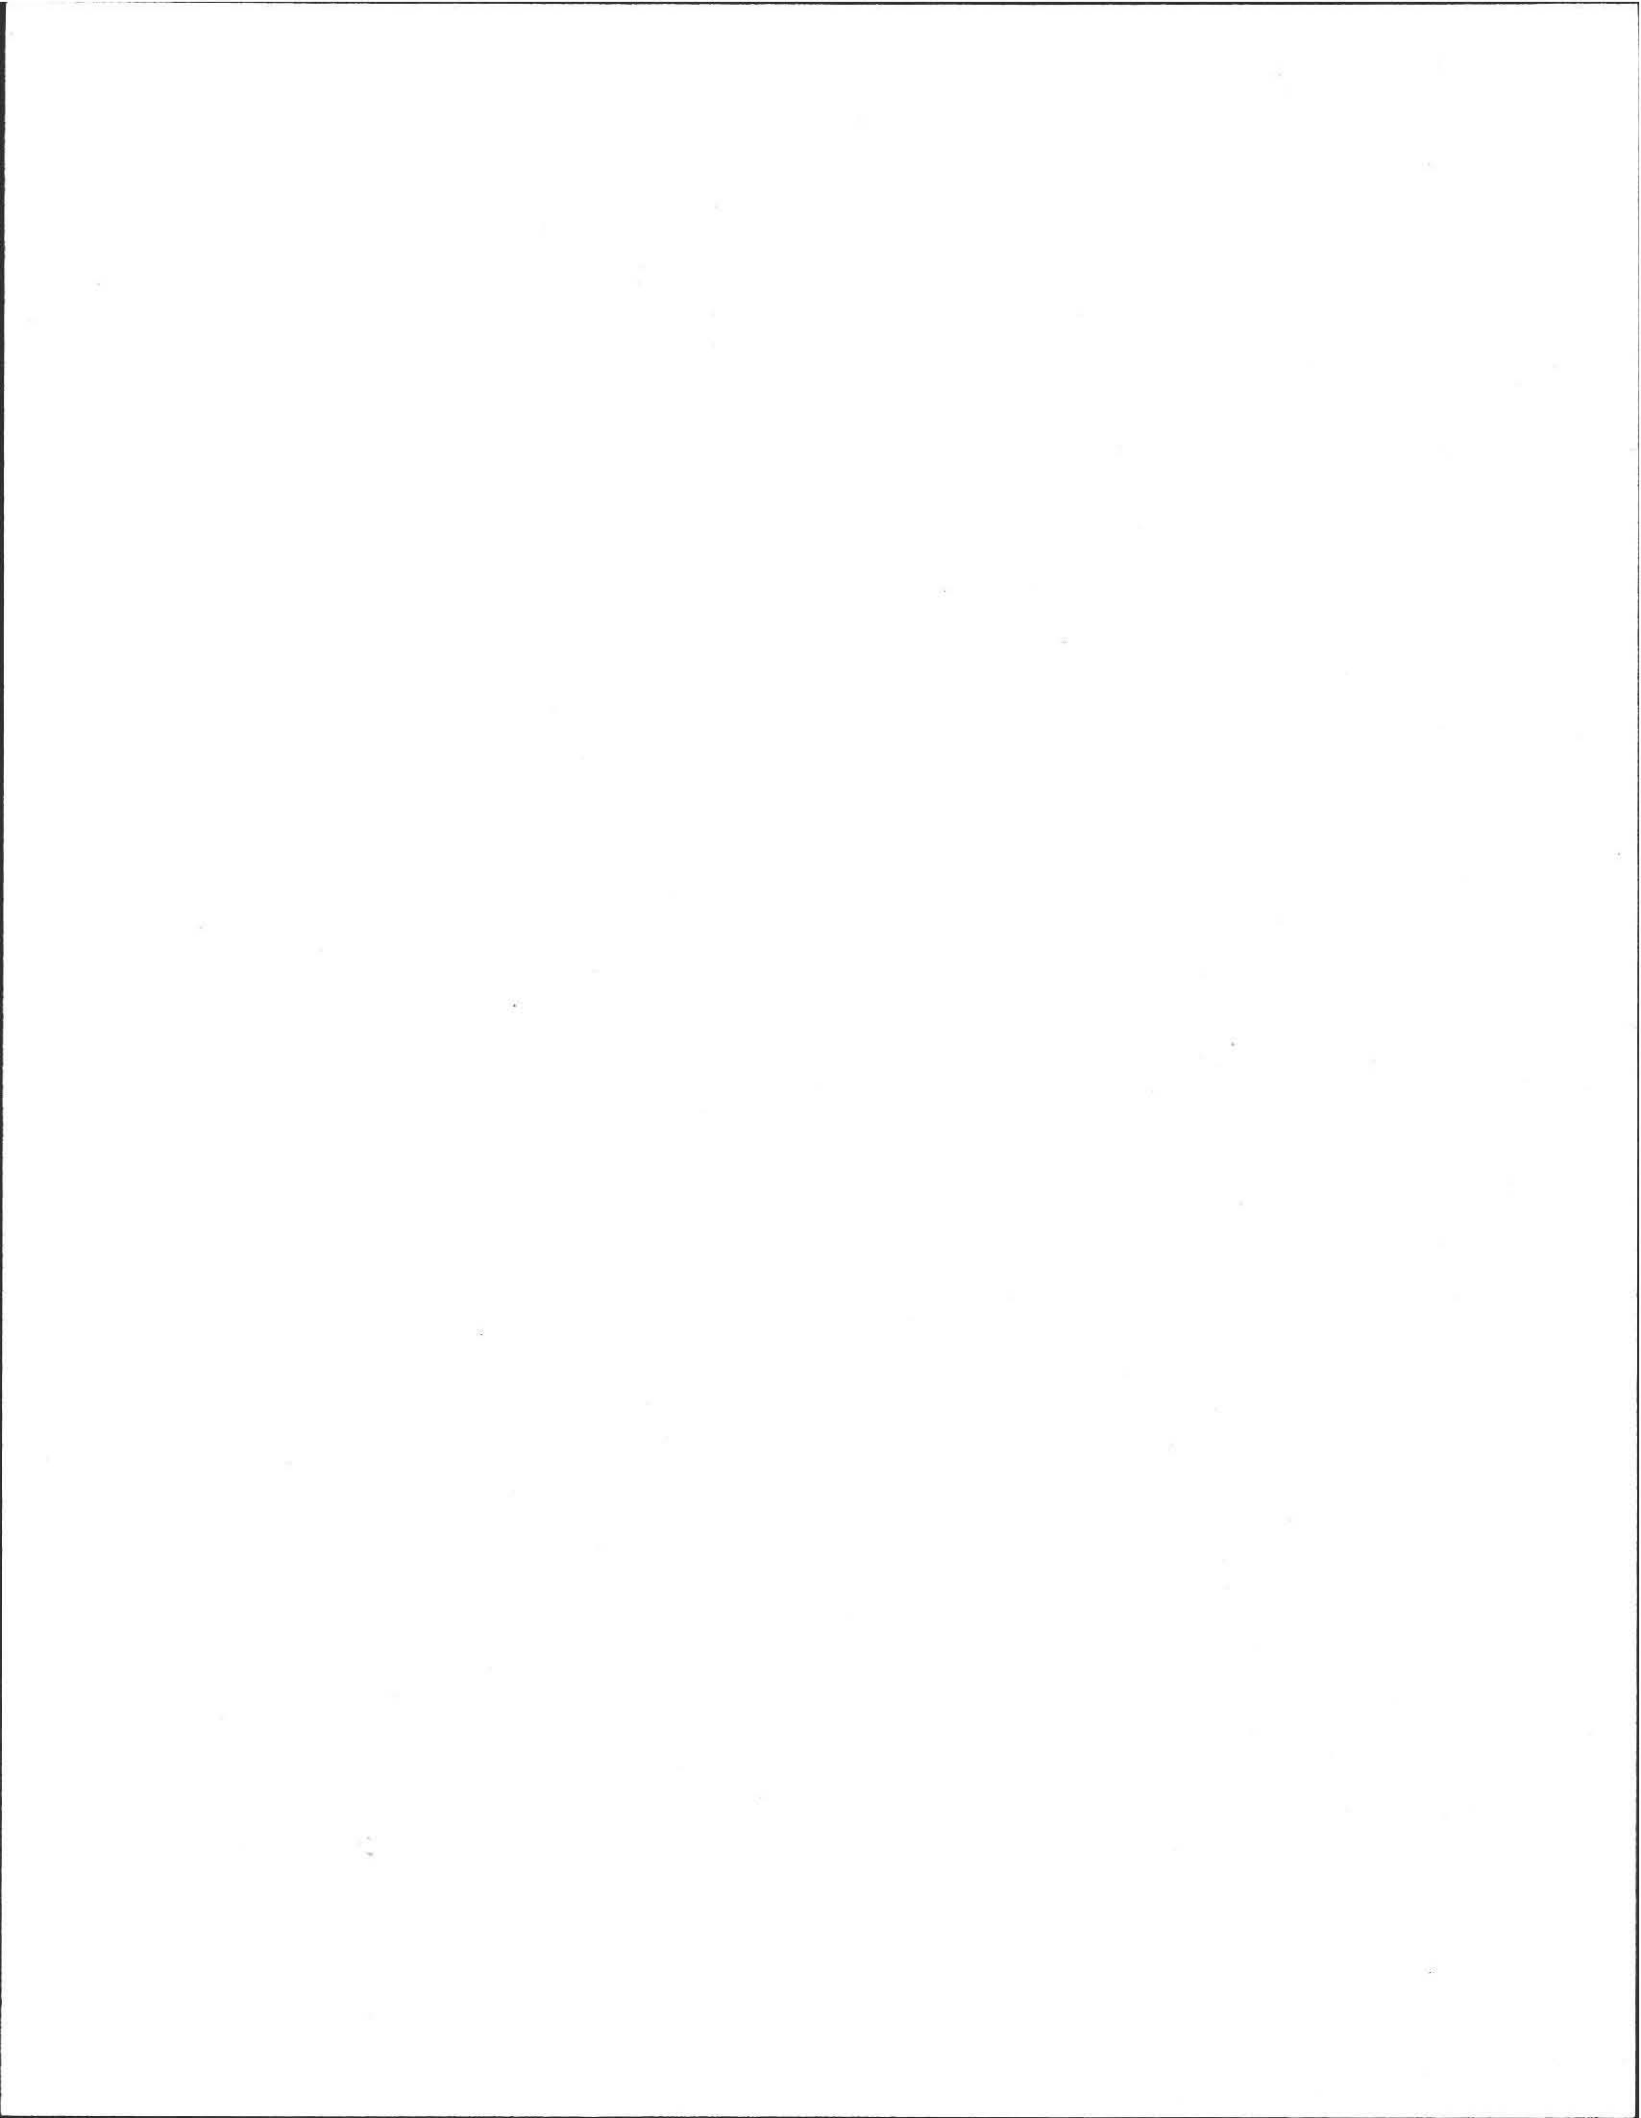

CUST NAME
4 BOLTWOOD AVENUE
10/24/12
CITY, ST, ZIP

***TOWN OF A TOWN HAL
AMHERST M REFERENCE
DATE/TIME 07:19

CUST NAME

0
DEPT

DE HEA058

TITLE V WI


200.

RECPT TOTAL

200.00
ROSALIE BU QUA CHECK

869

AMOUNT

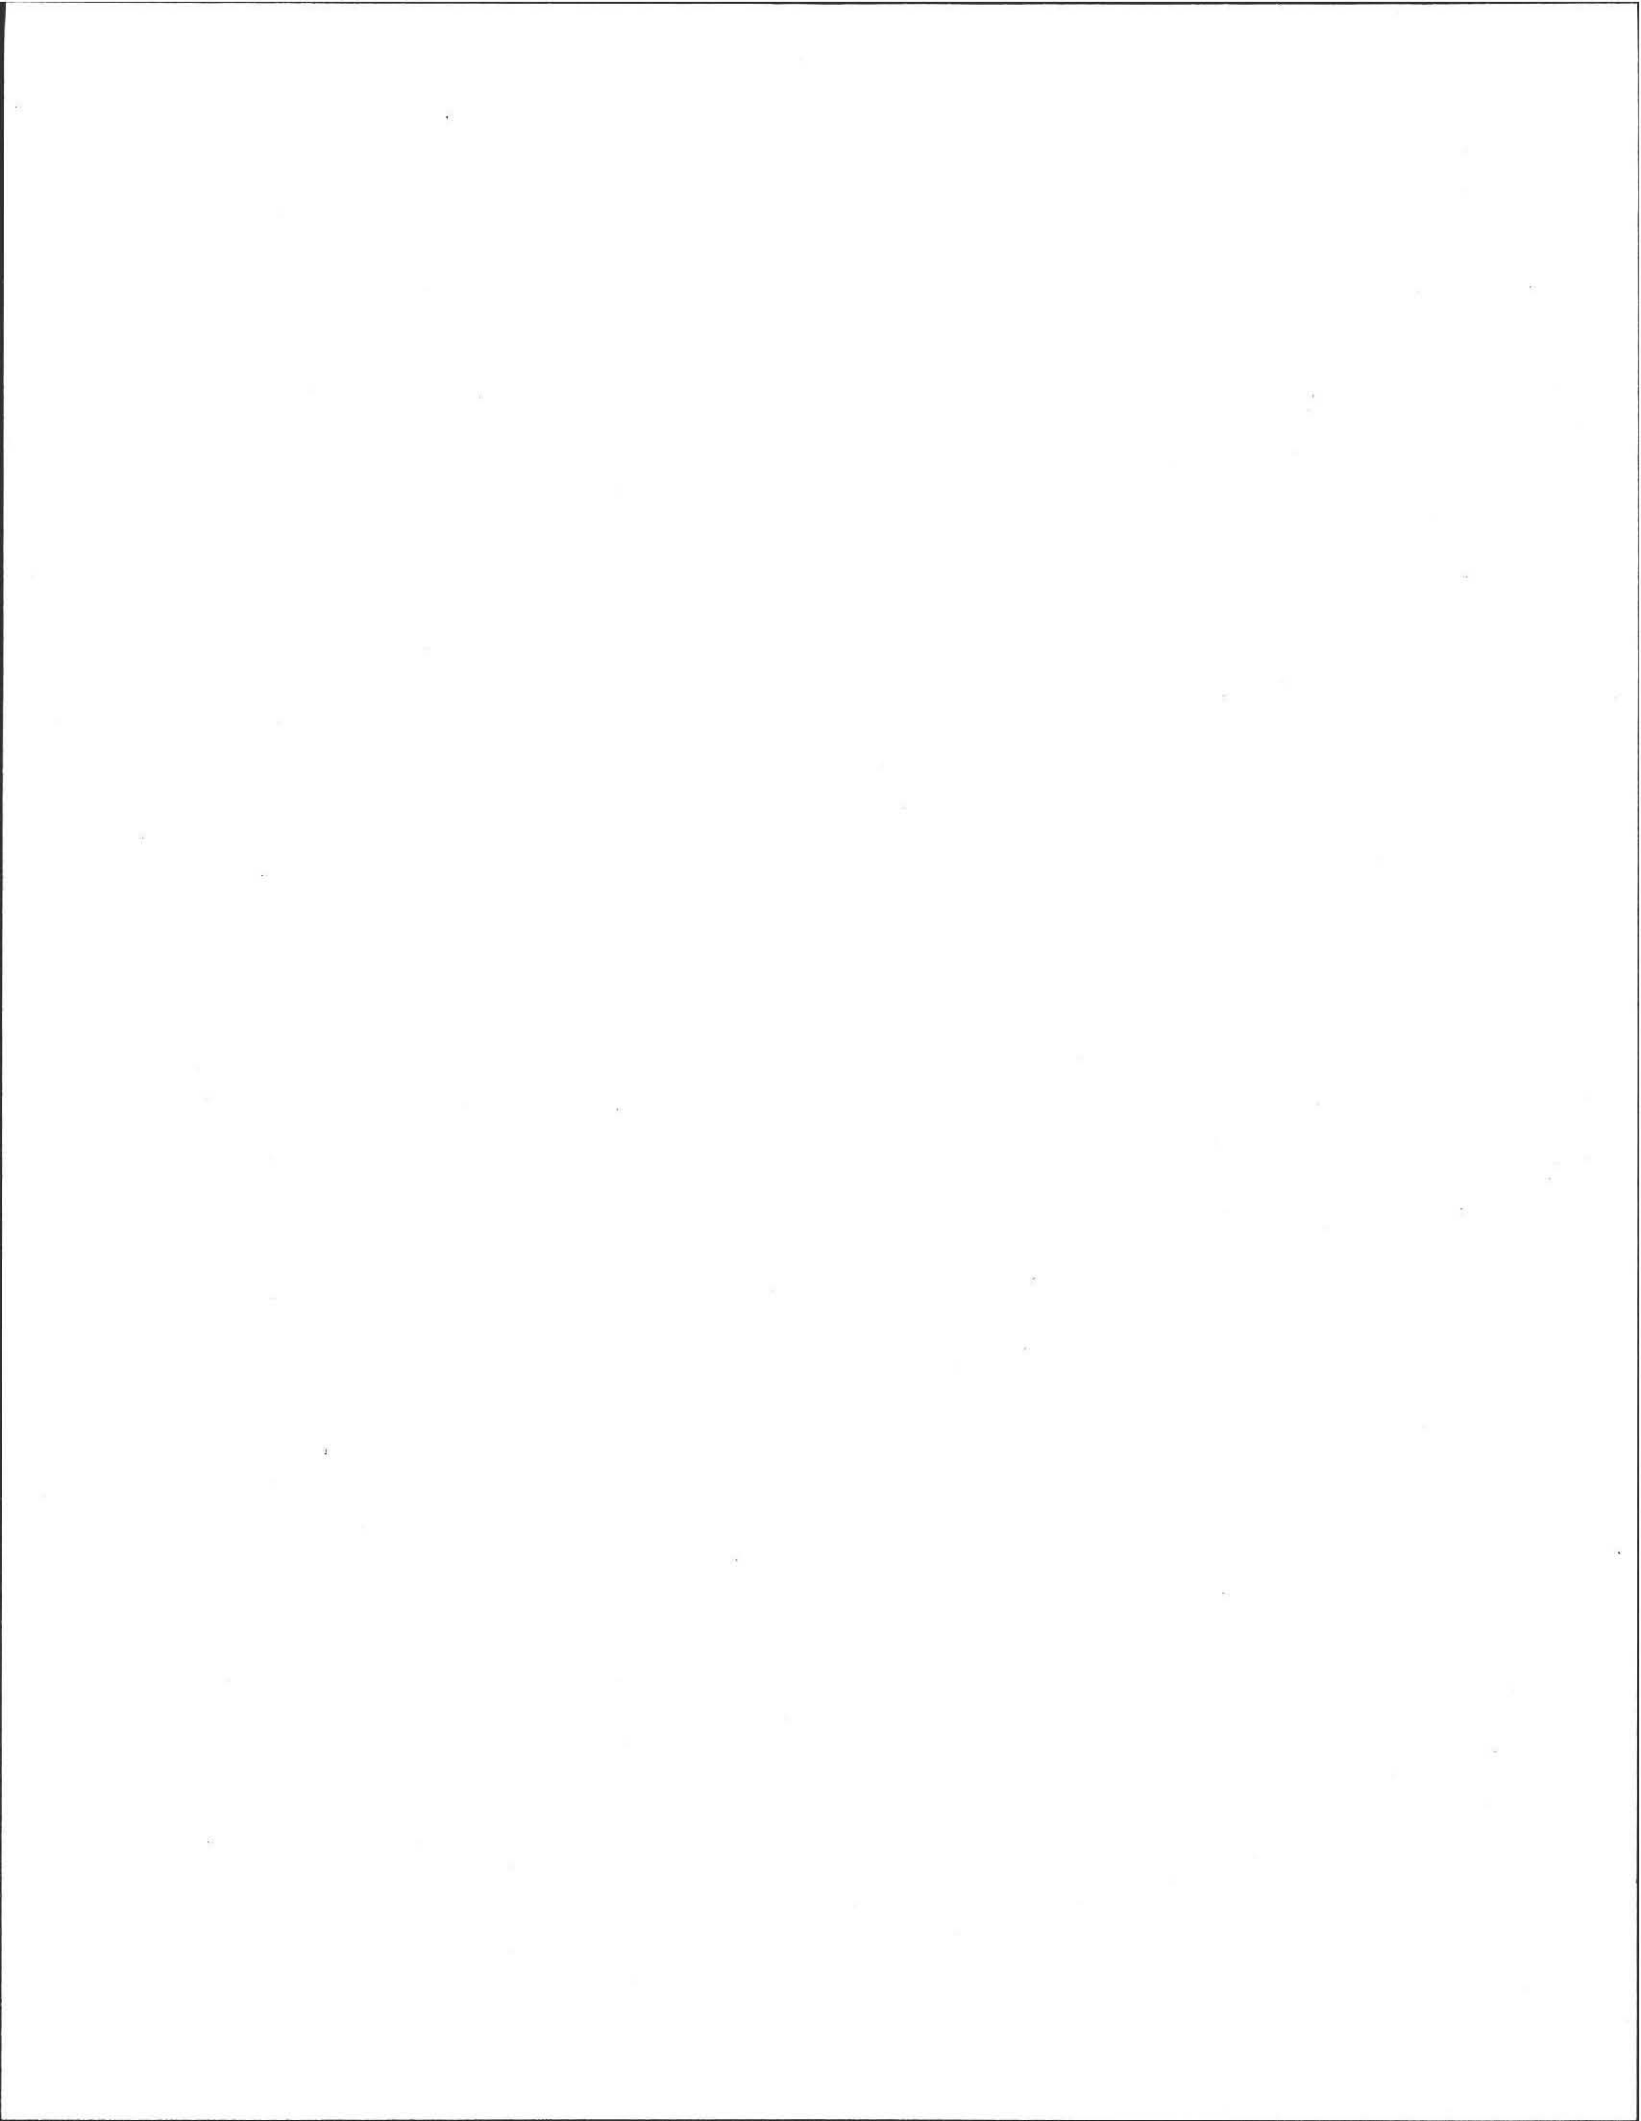

TITLE 5
OFFICIAL INSPECTION FOR - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM FORM
PART A
CERTIFICATION

Property Address: 751 Northeast Street, Amherst, MA
Owner's Name: Steve Founds C/O Jacqui Zuzgo
Owner's Address: 99 Main St Jones Town and Country Real Estate
Shelburne, MA 01370

COPY

Date of Inspection: December 02, 2003

Name of Inspector: Alan E. Weiss, R.S # 933
Company Name: Cold Spring Environmental Inc.
Mailing Address: 350 Old Enfield Road
Belchertown, Massachusetts 01007
Telephone Number: (413) 323-5957 fax: 413-323-4916

CERTIFICATION STATEMENT

I certify that I have personally inspected the sewage disposal system at this address and that the information reported below is true, accurate and complete as of the time of the inspection. The inspection was performed based on my training and experience in the proper function and maintenance of on site sewage disposal systems. **I am a DEP approved system inspector pursuant to Section 15.340 of Title 5 (310 CMR 15.000).** The system:

- XX Passes
- Conditionally Passes
- Needs Further Evaluation by the Local Approving Authority
- Fails

Inspector's Signature:  Date: **December 02, 2003**


The system inspector shall submit a copy of this inspection report to the Approving Authority (Board of Health or DEP) within 30 days of completing this inspection. If the system is a shared system or has a design flow of 10,000 gpd or greater, the inspector and the system owner shall submit the report to the appropriate regional office of the DEP. The original should be sent to the system owner and copies sent to the buyer, if applicable, and the approving authority.

Notes and Comments:

Septic Tank was in good condition upon inspection. System appears to be functional All Stains, alarms & levels were ok at tank and chamber. SAS is 2+/- years old and had no standing liquid. Outlet & inlet baffles were in place. Tank was pumped. No evidence of failure (Pump tank every other year, or more).

******This report only describes conditions at the time of inspection and under the conditions of use at that time. This inspection does not address how the system will perform in the future under the same different conditions of use.**



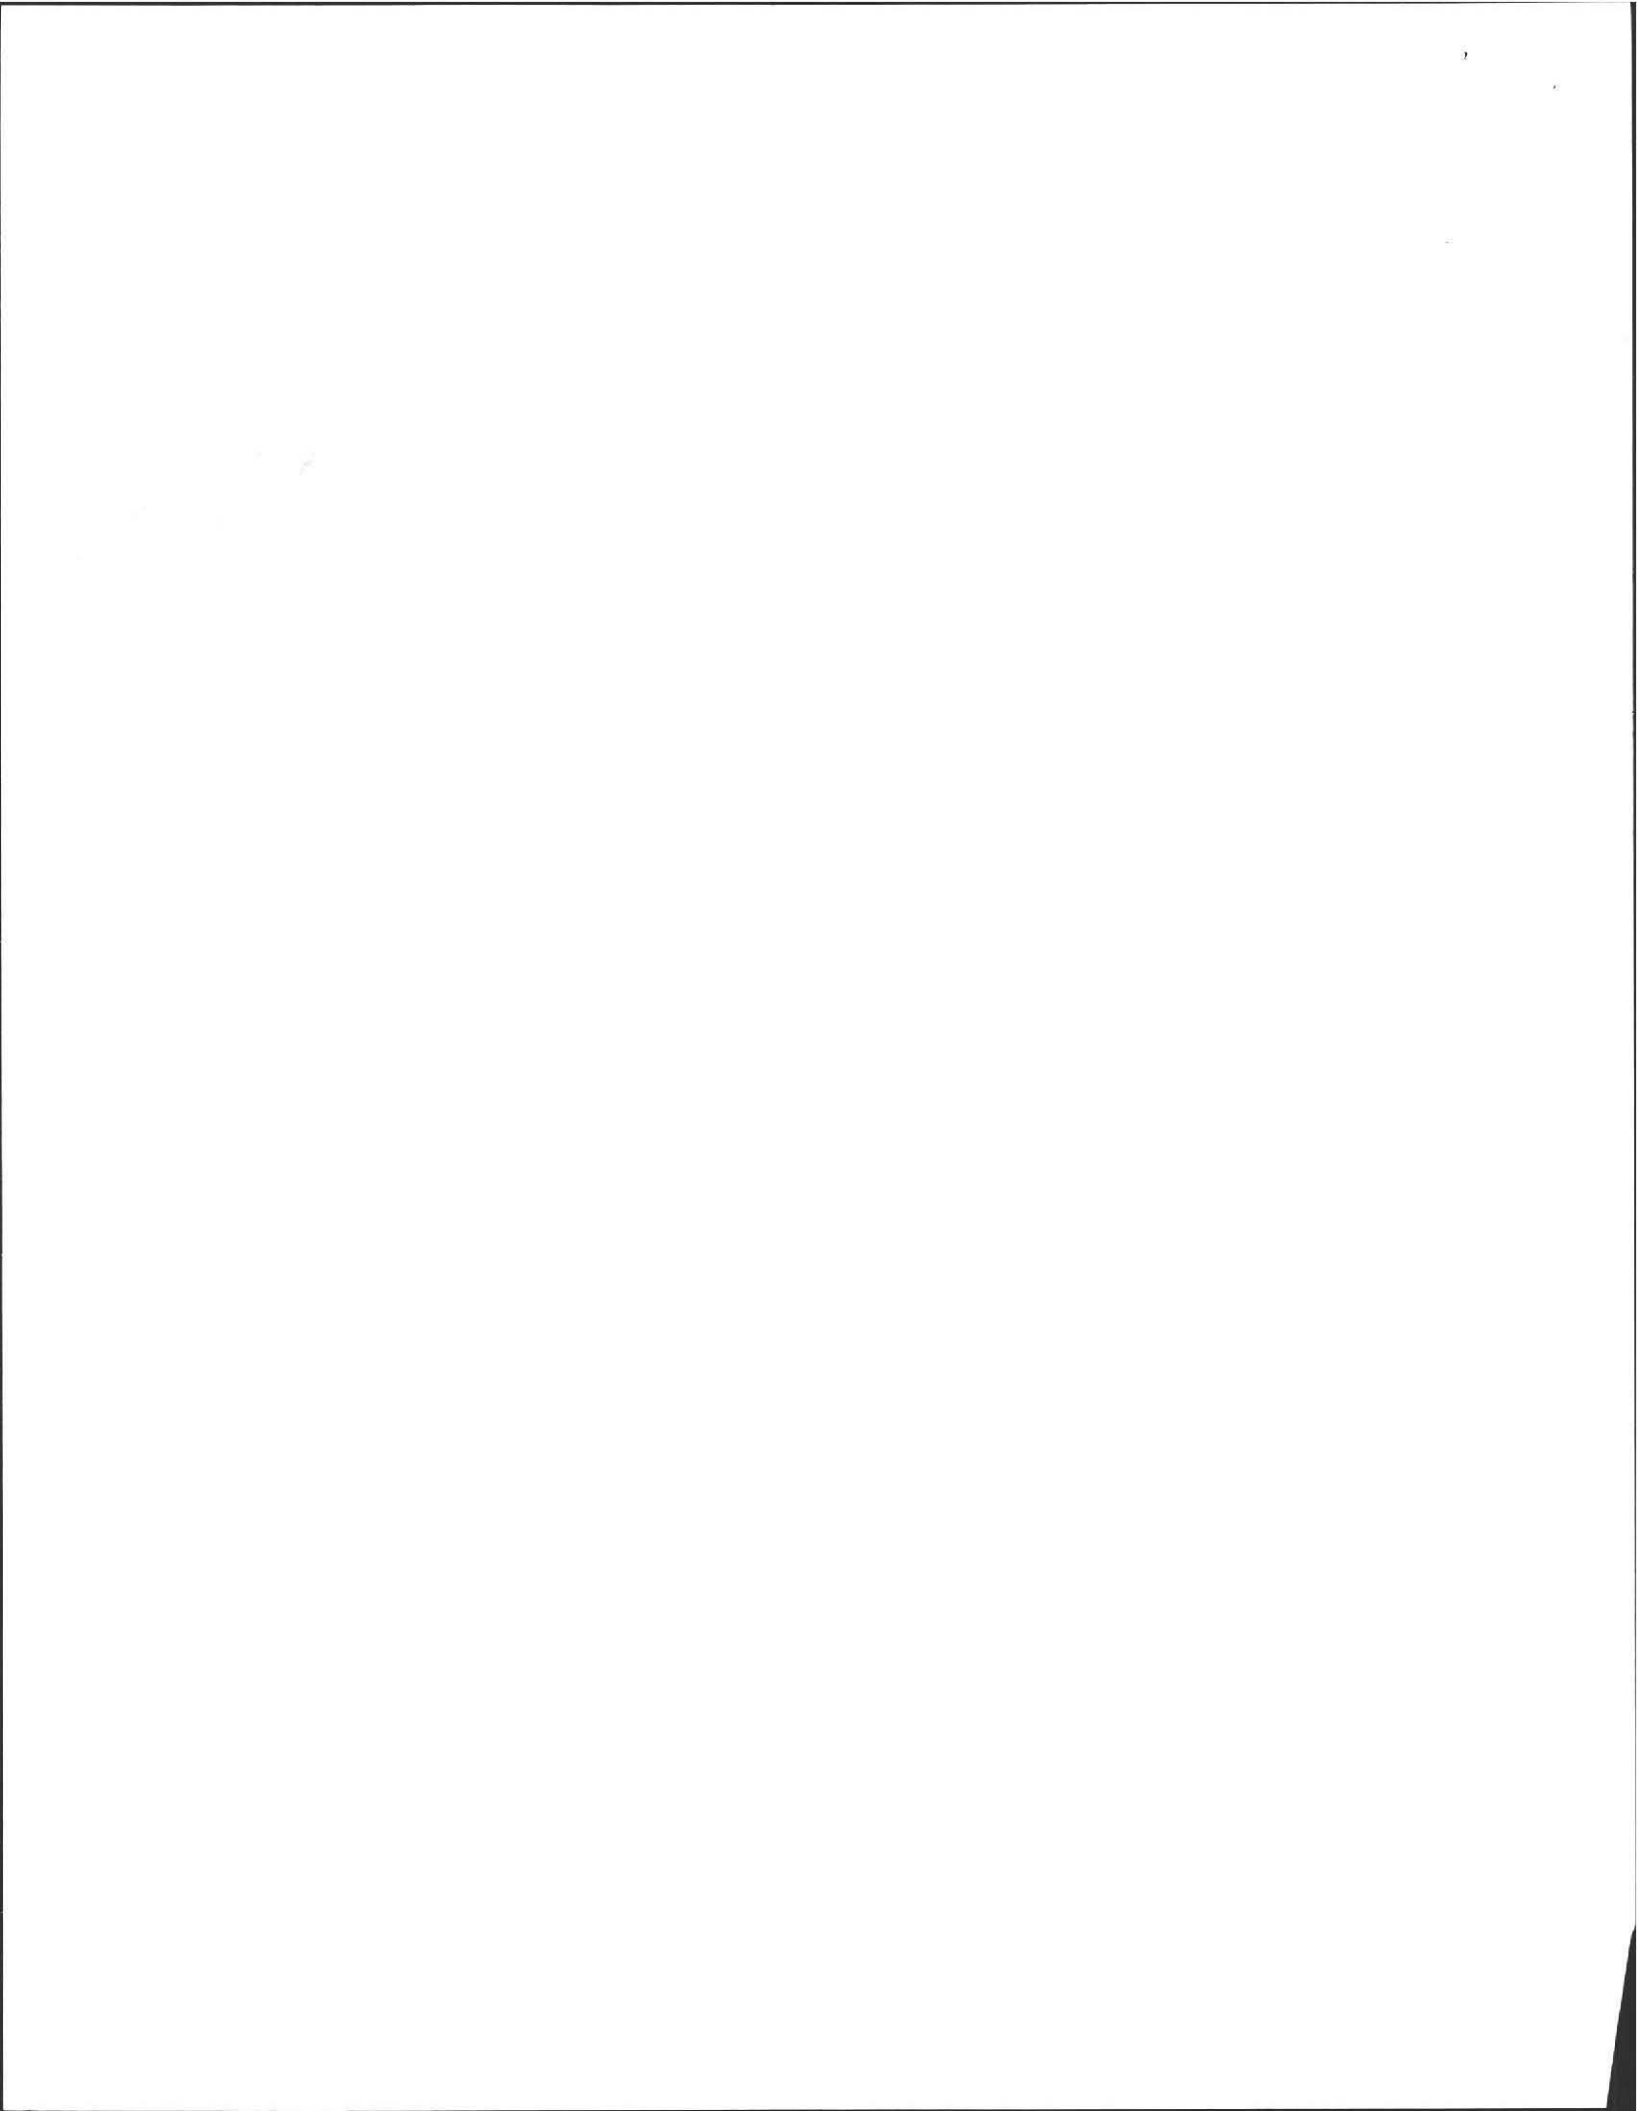

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM

PART A
CERTIFICATION (continued)

Property Address: 751 NE ST

Owner: Found S

Date of Inspection: 12/2/03

Inspection Summary: Check A,B,C,D or E / ALWAYS complete all of Section D

A. System Passes:

Yes I have not found any information which indicates that any of the failure criteria described in 310 CMR 15.303 or in 310 CMR 15.304 exist. Any failure criteria not evaluated are indicated below.

Comments:

B. System Conditionally Passes:

No One or more system components as described in the "Conditional Pass" section need to be replaced or repaired. The system, upon completion of the replacement or repair, as approved by the Board of Health, will pass.

Answer yes, no or not determined (Y,N,ND) in the ____ for the following statements. If "not determined" please explain.

____ The septic tank is metal and over 20 years old* or the septic tank (whether metal or not) is structurally unsound, exhibits substantial infiltration or exfiltration or tank failure is imminent. System will pass inspection if the existing tank is replaced with a complying septic tank as approved by the Board of Health.

*A metal septic tank will pass inspection if it is structurally sound, not leaking and if a Certificate of Compliance indicating that the tank is less than 20 years old is available.

ND explain:

____ Observation of sewage backup or break out or high static water level in the distribution box due to broken or obstructed pipe(s) or due to a broken, settled or uneven distribution box. System will pass inspection if (with approval of Board of Health):


- ____ broken pipe(s) are replaced
- ____ obstruction is removed
- ____ distribution box is leveled or replaced

ND explain:

____ The system required pumping more than 4 times a year due to broken or obstructed pipe(s). The system will pass inspection if (with approval of the Board of Health):

- ____ broken pipe(s) are replaced
- ____ obstruction is removed

ND explain:

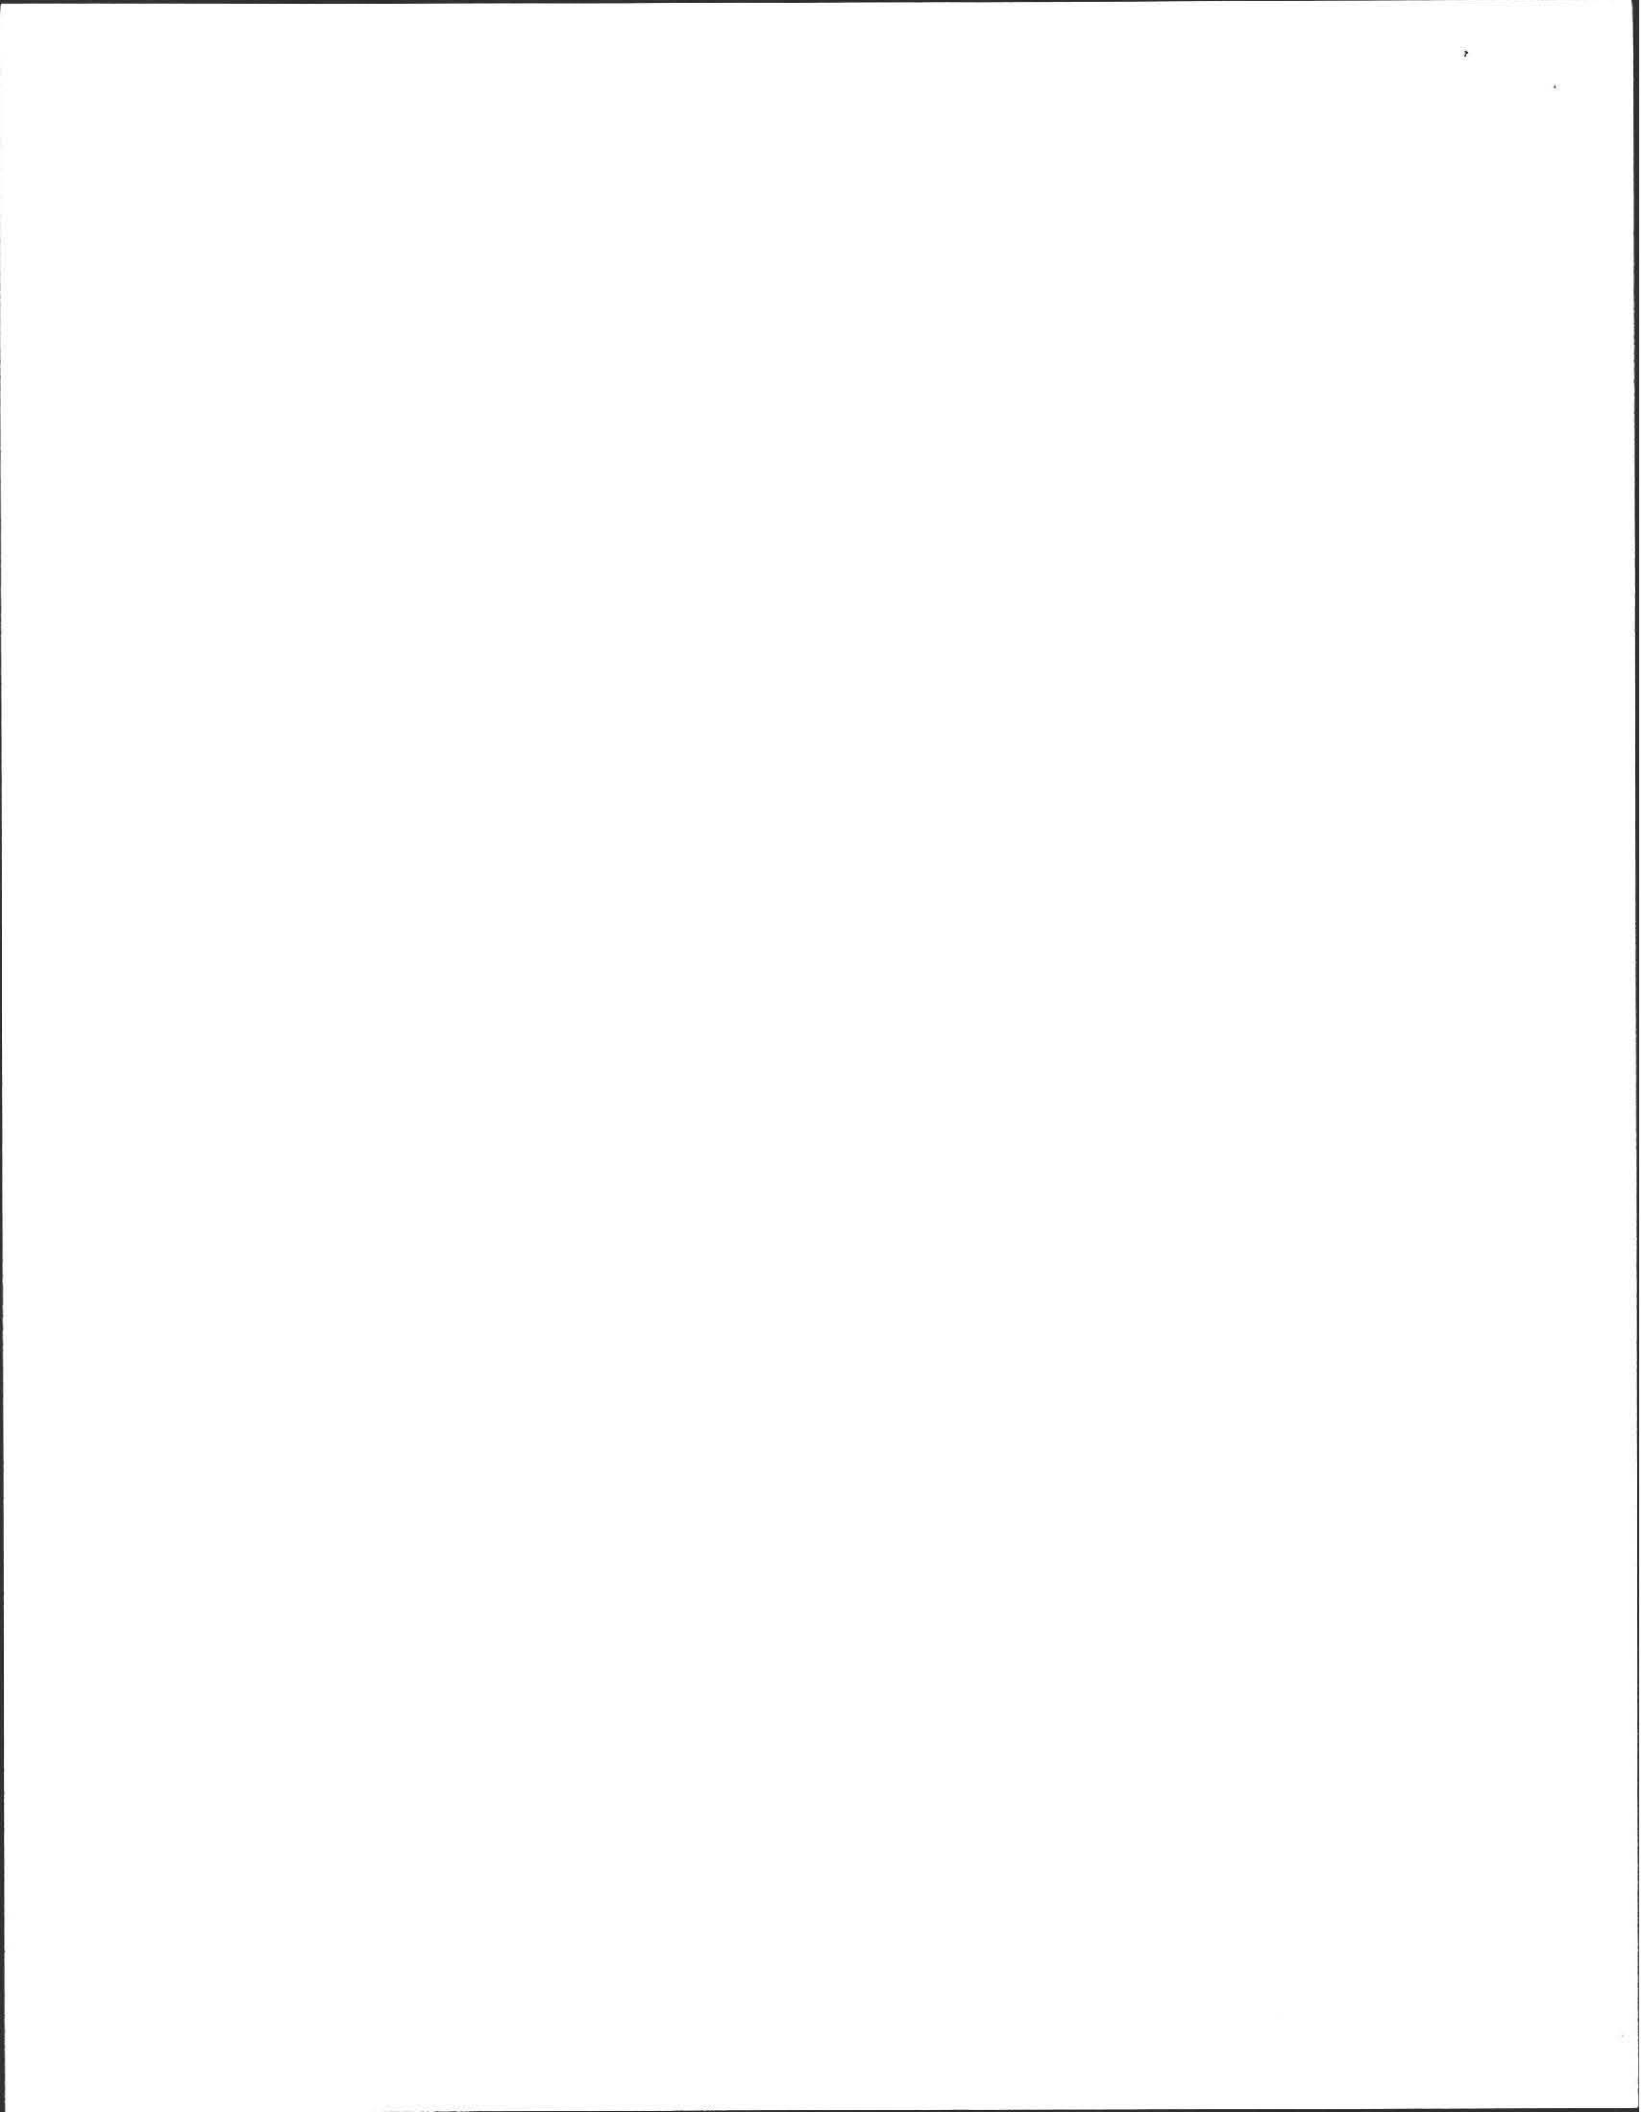

OFFICIAL INSPECTION FORM - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM

PART A
CERTIFICATION (continued)

Property Address: 751 NE ST

Owner: FRUNDS

Date of Inspection: 12/2/03

C. Further Evaluation is Required by the Board of Health:

No Conditions exist which require further evaluation by the Board of Health in order to determine if the system is failing to protect public health, safety or the environment.

1. System will pass unless Board of Health determines in accordance with 310 CMR 15.303(1)(b) that the system is not functioning in a manner which will protect public health, safety and the environment:


- Cesspool or privy is within 50 feet of a surface water
- Cesspool or privy is within 50 feet of a bordering vegetated wetland or a salt marsh

2. System will fail unless the Board of Health (and Public Water Supplier, if any) determines that the system is functioning in a manner that protects the public health, safety and environment:

- The system has a septic tank and soil absorption system (SAS) and the SAS is within 100 feet of a surface water supply or tributary to a surface water supply.
- The system has a septic tank and SAS and the SAS is within a Zone 1 of a public water supply.
- The system has a septic tank and SAS and the SAS is within 50 feet of a private water supply well.
- The system has a septic tank and SAS and the SAS is less than 100 feet but 50 feet or more from a private water supply well**. Method used to determine distance _____

**This system passes if the well water analysis, performed at a DEP certified laboratory, for coliform bacteria and volatile organic compounds indicates that the well is free from pollution from that facility and the presence of ammonia nitrogen and nitrate nitrogen is equal to or less than 5 ppm, provided that no other failure criteria are triggered. A copy of the analysis must be attached to this form.

3. Other:

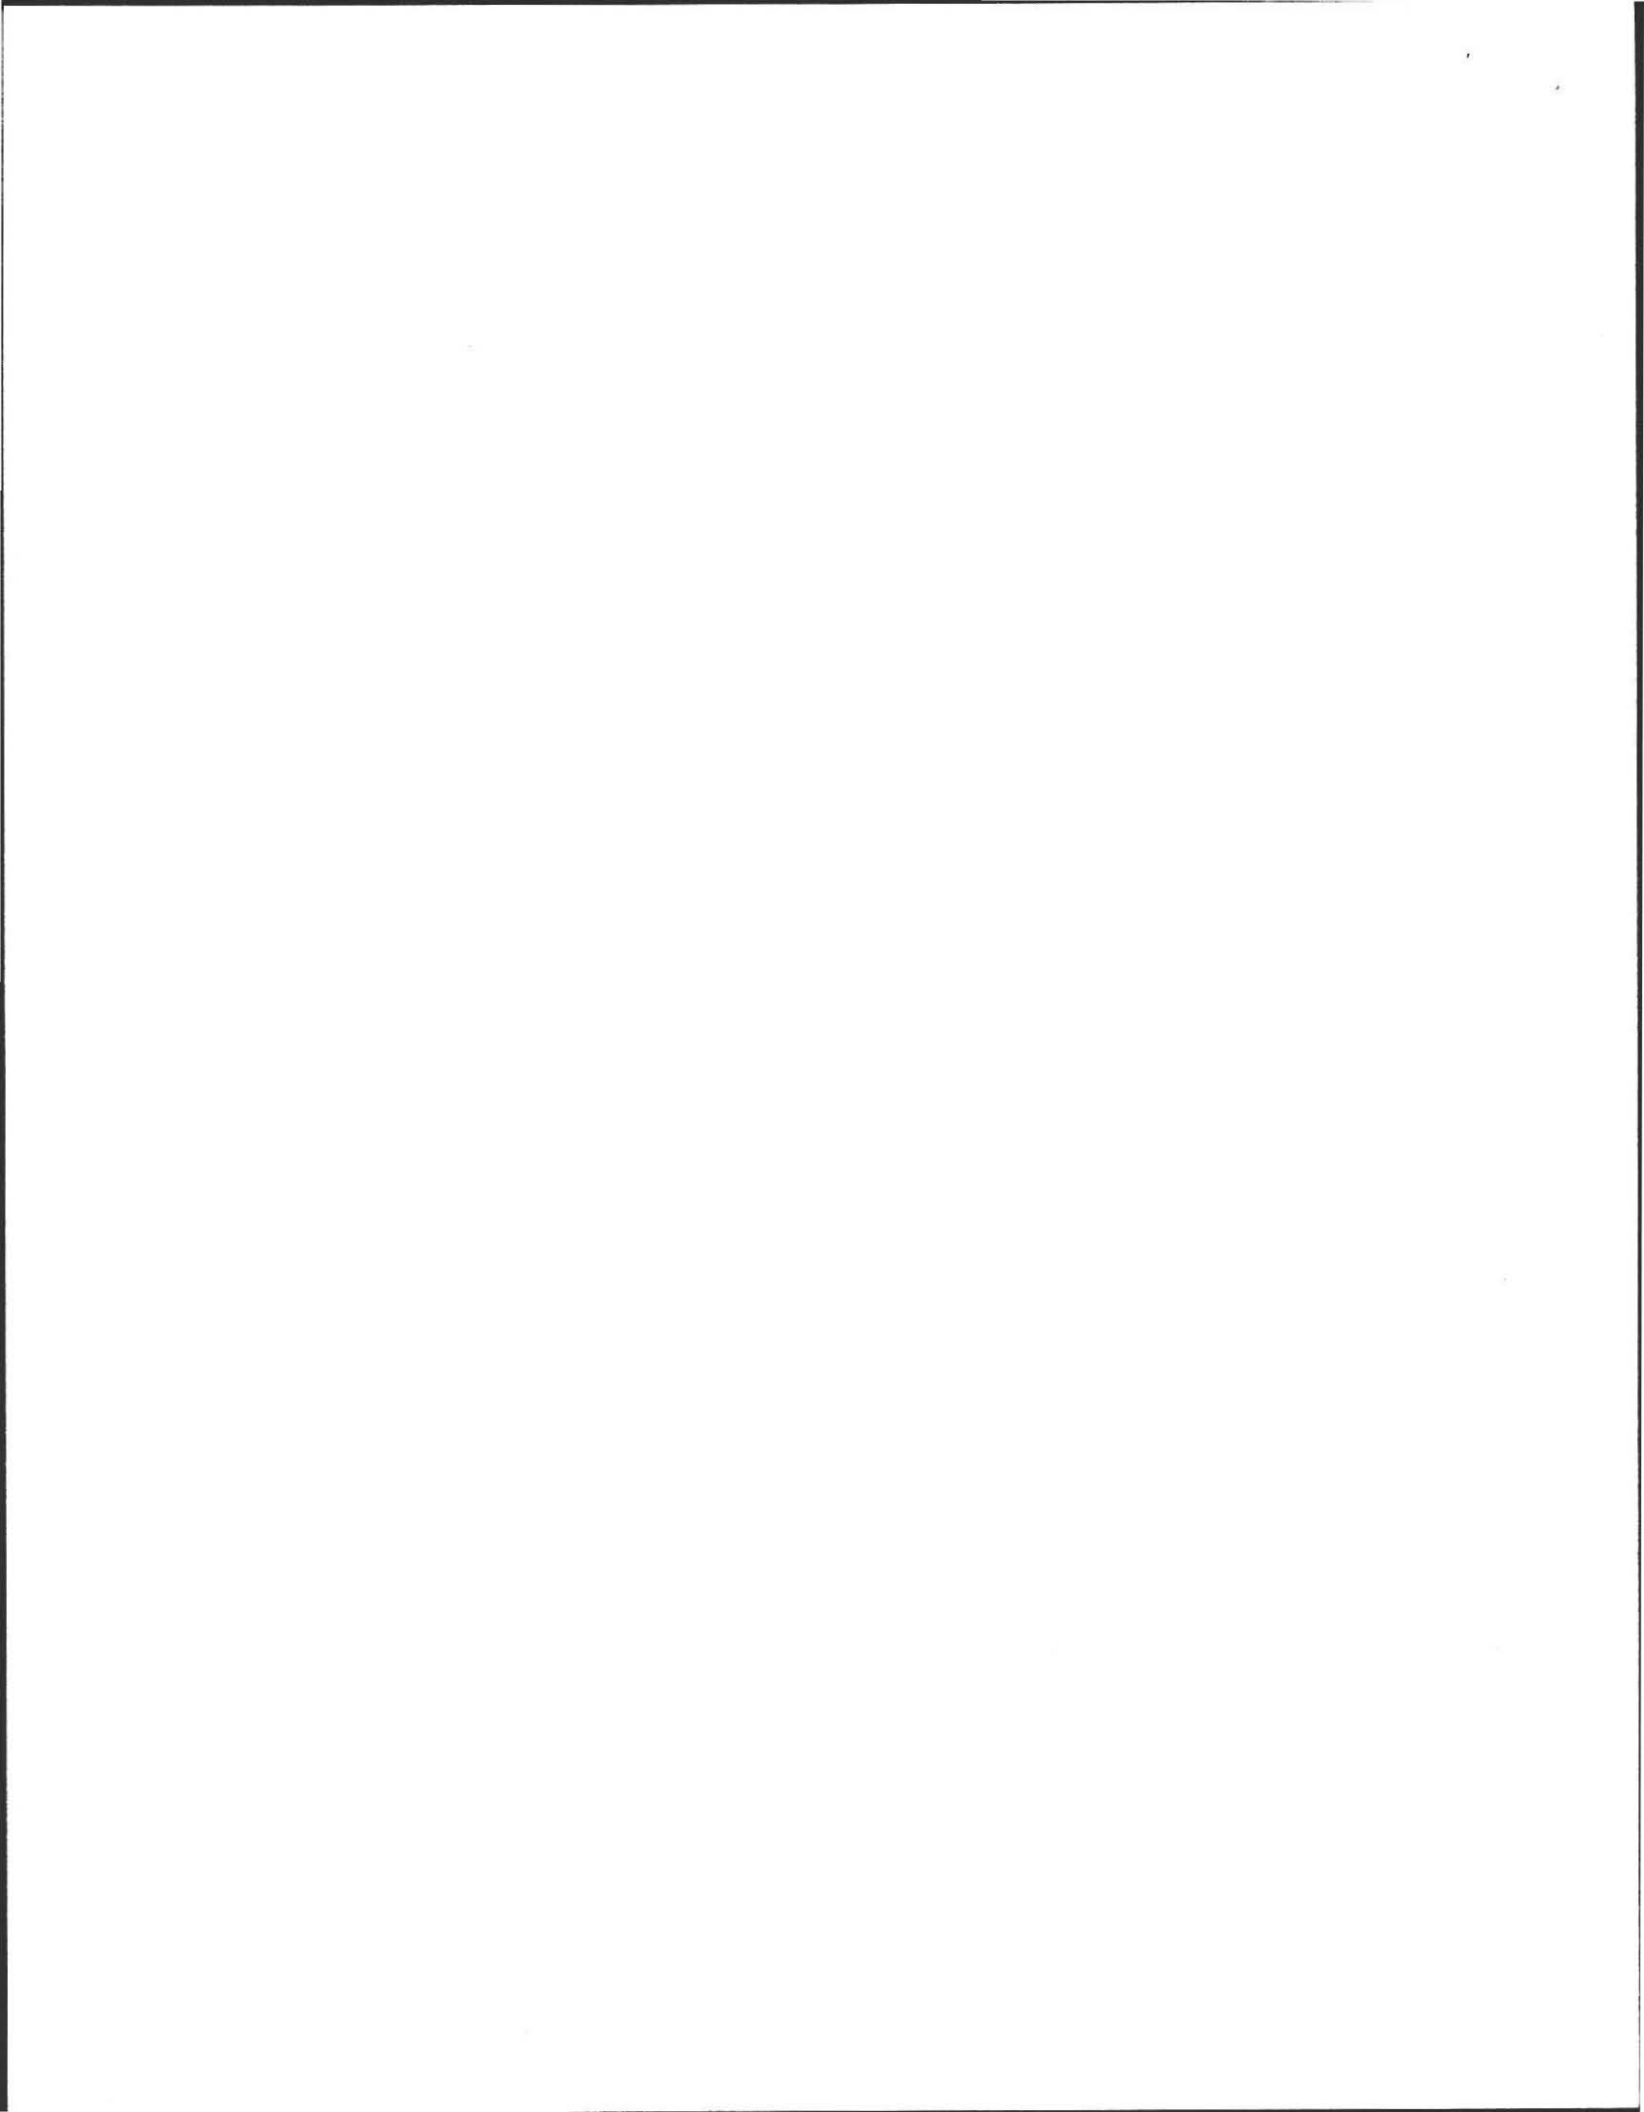

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM

PART A
CERTIFICATION (continued)

Property Address: 751 NE ST.

Owner: Foinds

Date of Inspection: 12/26/03

D. System Failure Criteria applicable to all systems:

You **must** indicate "yes" or "no" to each of the following for **all** inspections:

- Yes No
 No Backup of sewage into facility or system component due to overloaded or clogged SAS or cesspool
- No Discharge or ponding of effluent to the surface of the ground or surface waters due to an overloaded or clogged SAS or cesspool
- No Static liquid level in the distribution box above outlet invert due to an overloaded or clogged SAS or cesspool
- No Liquid depth in cesspool is less than 6" below invert or available volume is less than 1/2 day flow
- No Required pumping more than 4 times in the last year **NOT** due to clogged or obstructed pipe(s). Number of times pumped .
- No Any portion of the SAS, cesspool or privy is below high ground water elevation.
- No Any portion of cesspool or privy is within 100 feet of a surface water supply or tributary to a surface water supply.
- No Any portion of a cesspool or privy is within a Zone 1 of a public well.
- No Any portion of a cesspool or privy is within 50 feet of a private water supply well.
- No Any portion of a cesspool or privy is less than 100 feet but greater than 50 feet from a private water supply well with no acceptable water quality analysis. [This system passes if the well water analysis, performed at a DEP certified laboratory, for coliform bacteria and volatile organic compounds indicates that the well is free from pollution from that facility and the presence of ammonia nitrogen and nitrate nitrogen is equal to or less than 5 ppm, provided that no other failure criteria are triggered. A copy of the analysis must be attached to this form.]

No (Yes/No) The system **fails**. I have determined that one or more of the above failure criteria exist as described in 310 CMR 15.303, therefore the system fails. The system owner should contact the Board of Health to determine what will be necessary to correct the failure.

E. Large Systems:


To be considered a large system the system must serve a facility with a design flow of 10,000 gpd to 15,000 gpd.

You must indicate either "yes" or "no" to each of the following:

(The following criteria apply to large systems in addition to the criteria above)

- yes no
 the system is within 400 feet of a surface drinking water supply
- the system is within 200 feet of a tributary to a surface drinking water supply
- the system is located in a nitrogen sensitive area (Interim Wellhead Protection Area – IWPA) or a mapped Zone II of a public water supply well

If you have answered "yes" to any question in Section E the system is considered a significant threat, or answered "yes" in Section D above the large system has failed. The owner or operator of any large system considered a significant threat under Section E or failed under Section D shall upgrade the system in accordance with 310 CMR 15.304. The system owner should contact the appropriate regional office of the Department.

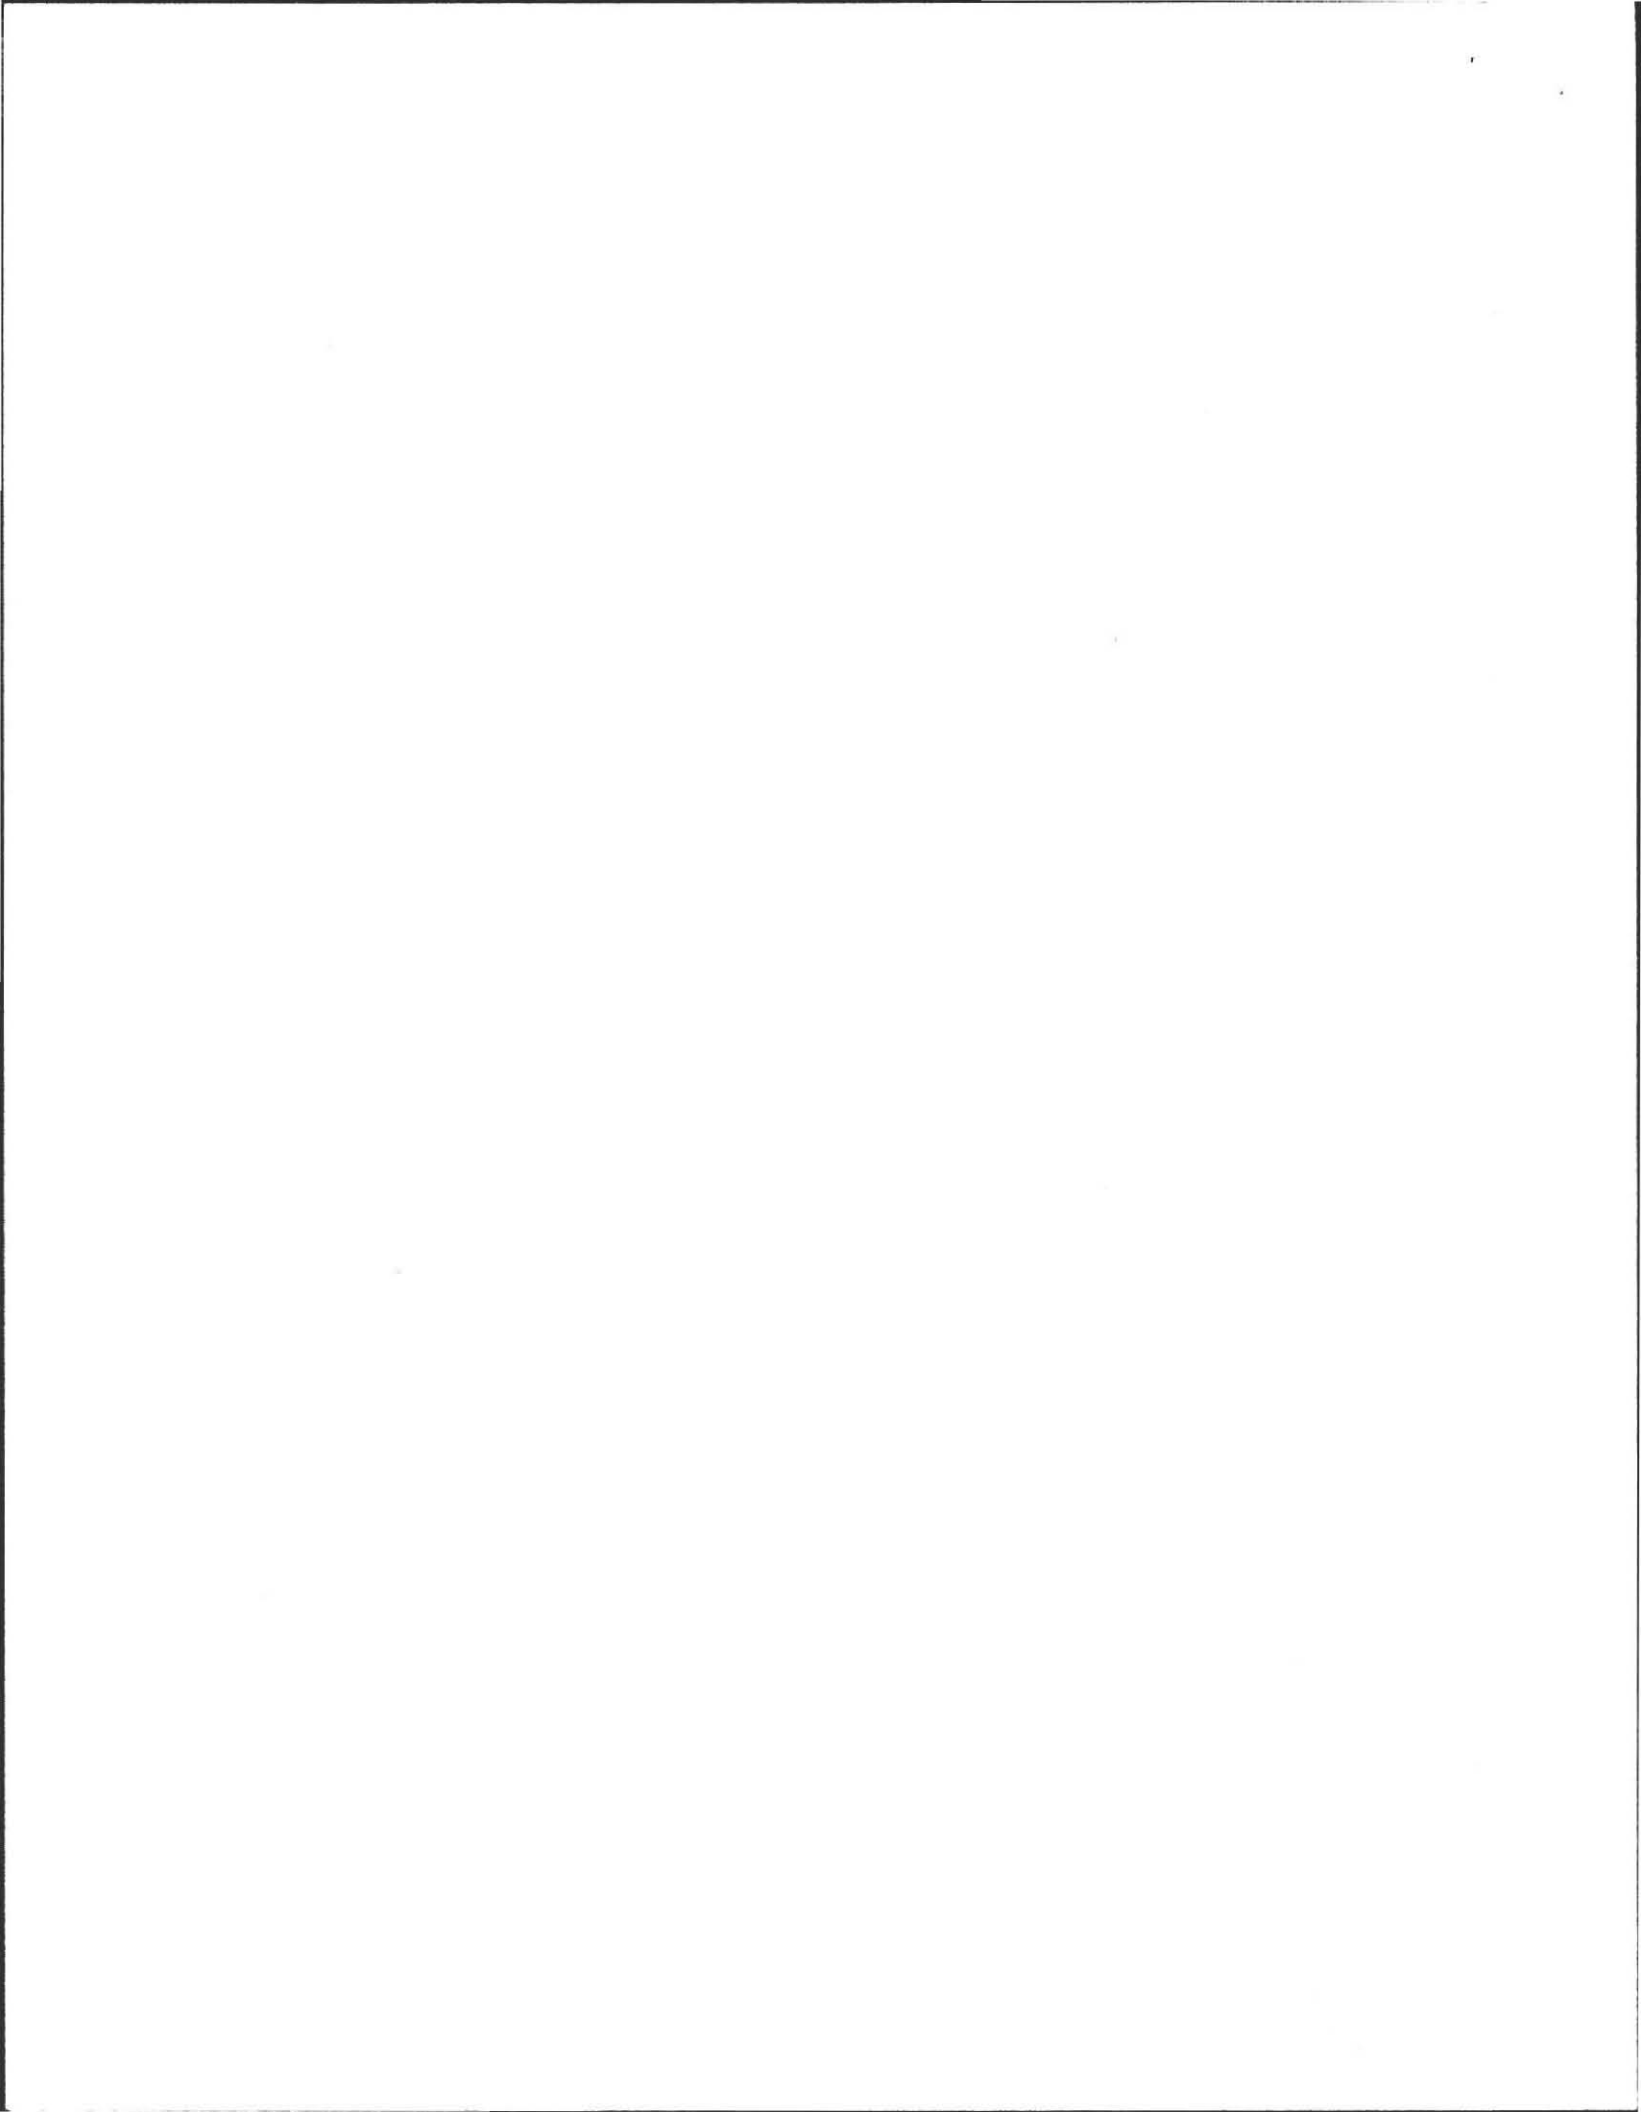

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART B
CHECKLIST

Property Address: 751 NE ST.

Owner: Frends


Date of Inspection: 12/2/03

Check if the following have been done. You must indicate "yes" or "no" as to each of the following:

- Yes No
- yes ___ Pumping information was provided by the owner, occupant, or Board of Health
 - ___ No ___ Were any of the system components pumped out in the previous two weeks ?
 - ___ No ___ Has the system received normal flows in the previous two week period ? (OCTOBER)
 - ___ No ___ Have large volumes of water been introduced to the system recently or as part of this inspection ?
 - yes ___ Were as built plans of the system obtained and examined? (If they were not available note as N/A)
 - yes ___ Was the facility or dwelling inspected for signs of sewage back up ?
 - yes ___ Was the site inspected for signs of break out ?
 - yes ___ Were all system components, excluding the SAS, located on site ?
 - yes ___ Were the septic tank manholes uncovered, opened, and the interior of the tank inspected for the condition of the baffles or tees, material of construction, dimensions, depth of liquid, depth of sludge and depth of scum ?
 - yes ___ Was the facility owner (and occupants if different from owner) provided with information on the proper maintenance of subsurface sewage disposal systems ?

The size and location of the Soil Absorption System (SAS) on the site has been determined based on:

- Yes no
- yes ___ Existing information. For example, a plan at the Board of Health.
 - yes ___ Determined in the field (if any of the failure criteria related to Part C is at issue approximation of distance is unacceptable) [310 CMR 15.302(3)(b)]

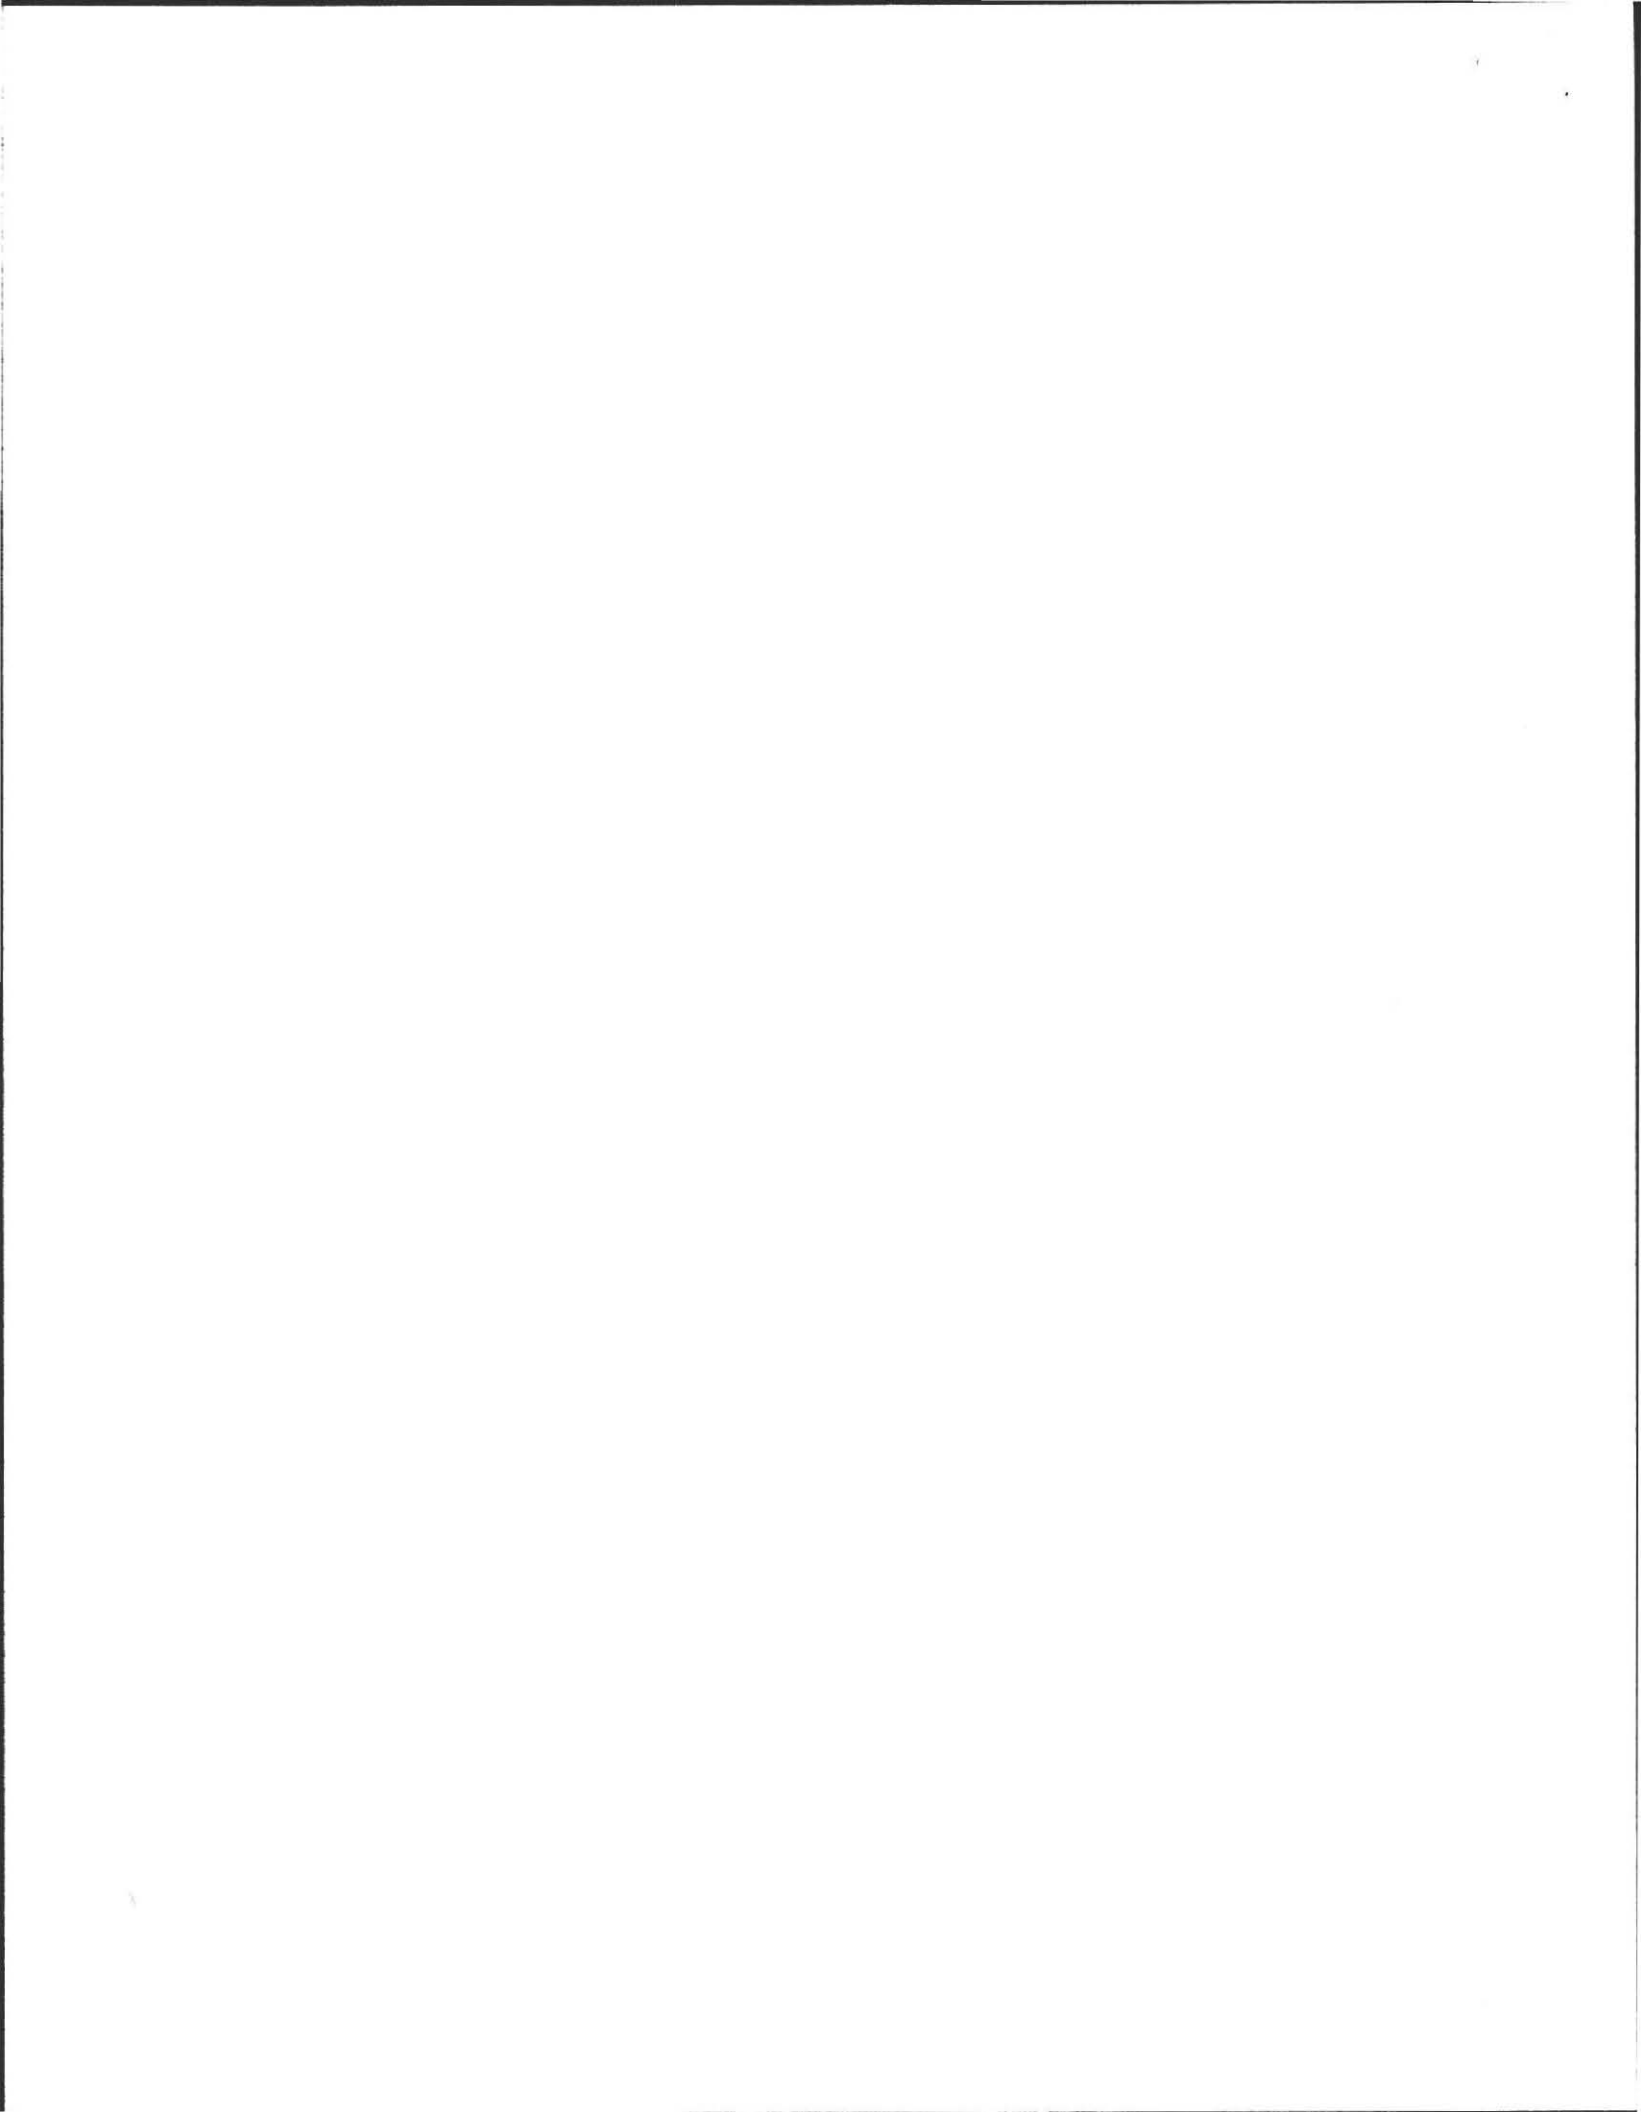

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION

Property Address: 751 NE ST.

Owner: FORDIS

Date of Inspection: 12/2/03

FLOW CONDITIONS

RESIDENTIAL

Number of bedrooms (design): 7 Number of bedrooms (actual): 7

DESIGN flow based on 310 CMR 15.203 (for example: 110 gpd x # of bedrooms): 770

Number of current residents: 0 (4 in October)

Does residence have a garbage grinder (yes or no): no

Is laundry on a separate sewage system (yes or no): no [if yes separate inspection required]

Laundry system inspected (yes or no): no

Seasonal use: (yes or no): no

Water meter readings, if available (last 2 years usage (gpd)): N/A.

Sump pump (yes or no): no

Last date of occupancy: Oct. 03

COMMERCIAL/INDUSTRIAL

Type of establishment: N/A

Design flow (based on 310 CMR 15.203): _____ gpd

Basis of design flow (seats/persons/sqft, etc.): _____

Grease trap present (yes or no): _____

Industrial waste holding tank present (yes or no): _____

Non-sanitary waste discharged to the Title 5 system (yes or no): _____

Water meter readings, if available: _____

Last date of occupancy/use: _____

OTHER (describe): _____

GENERAL INFORMATION

Pumping Records

Source of information: _____

Was system pumped as part of the inspection (yes or no): yes

If yes, volume pumped: 1000 gallons -- How was quantity pumped determined? _____

Reason for pumping: _____

TYPE OF SYSTEM

Septic tank, distribution box, soil absorption system

Single cesspool

Overflow cesspool

Privy

Shared system (yes or no) (if yes, attach previous inspection records, if any)


Innovative/Alternative technology. Attach a copy of the current operation and maintenance contract (to be obtained from system owner)

Tight tank Attach a copy of the DEP approval

Other (describe): _____

Approximate age of all components, date installed (if known) and source of information:
2001.

Were sewage odors detected when arriving at the site (yes or no): No

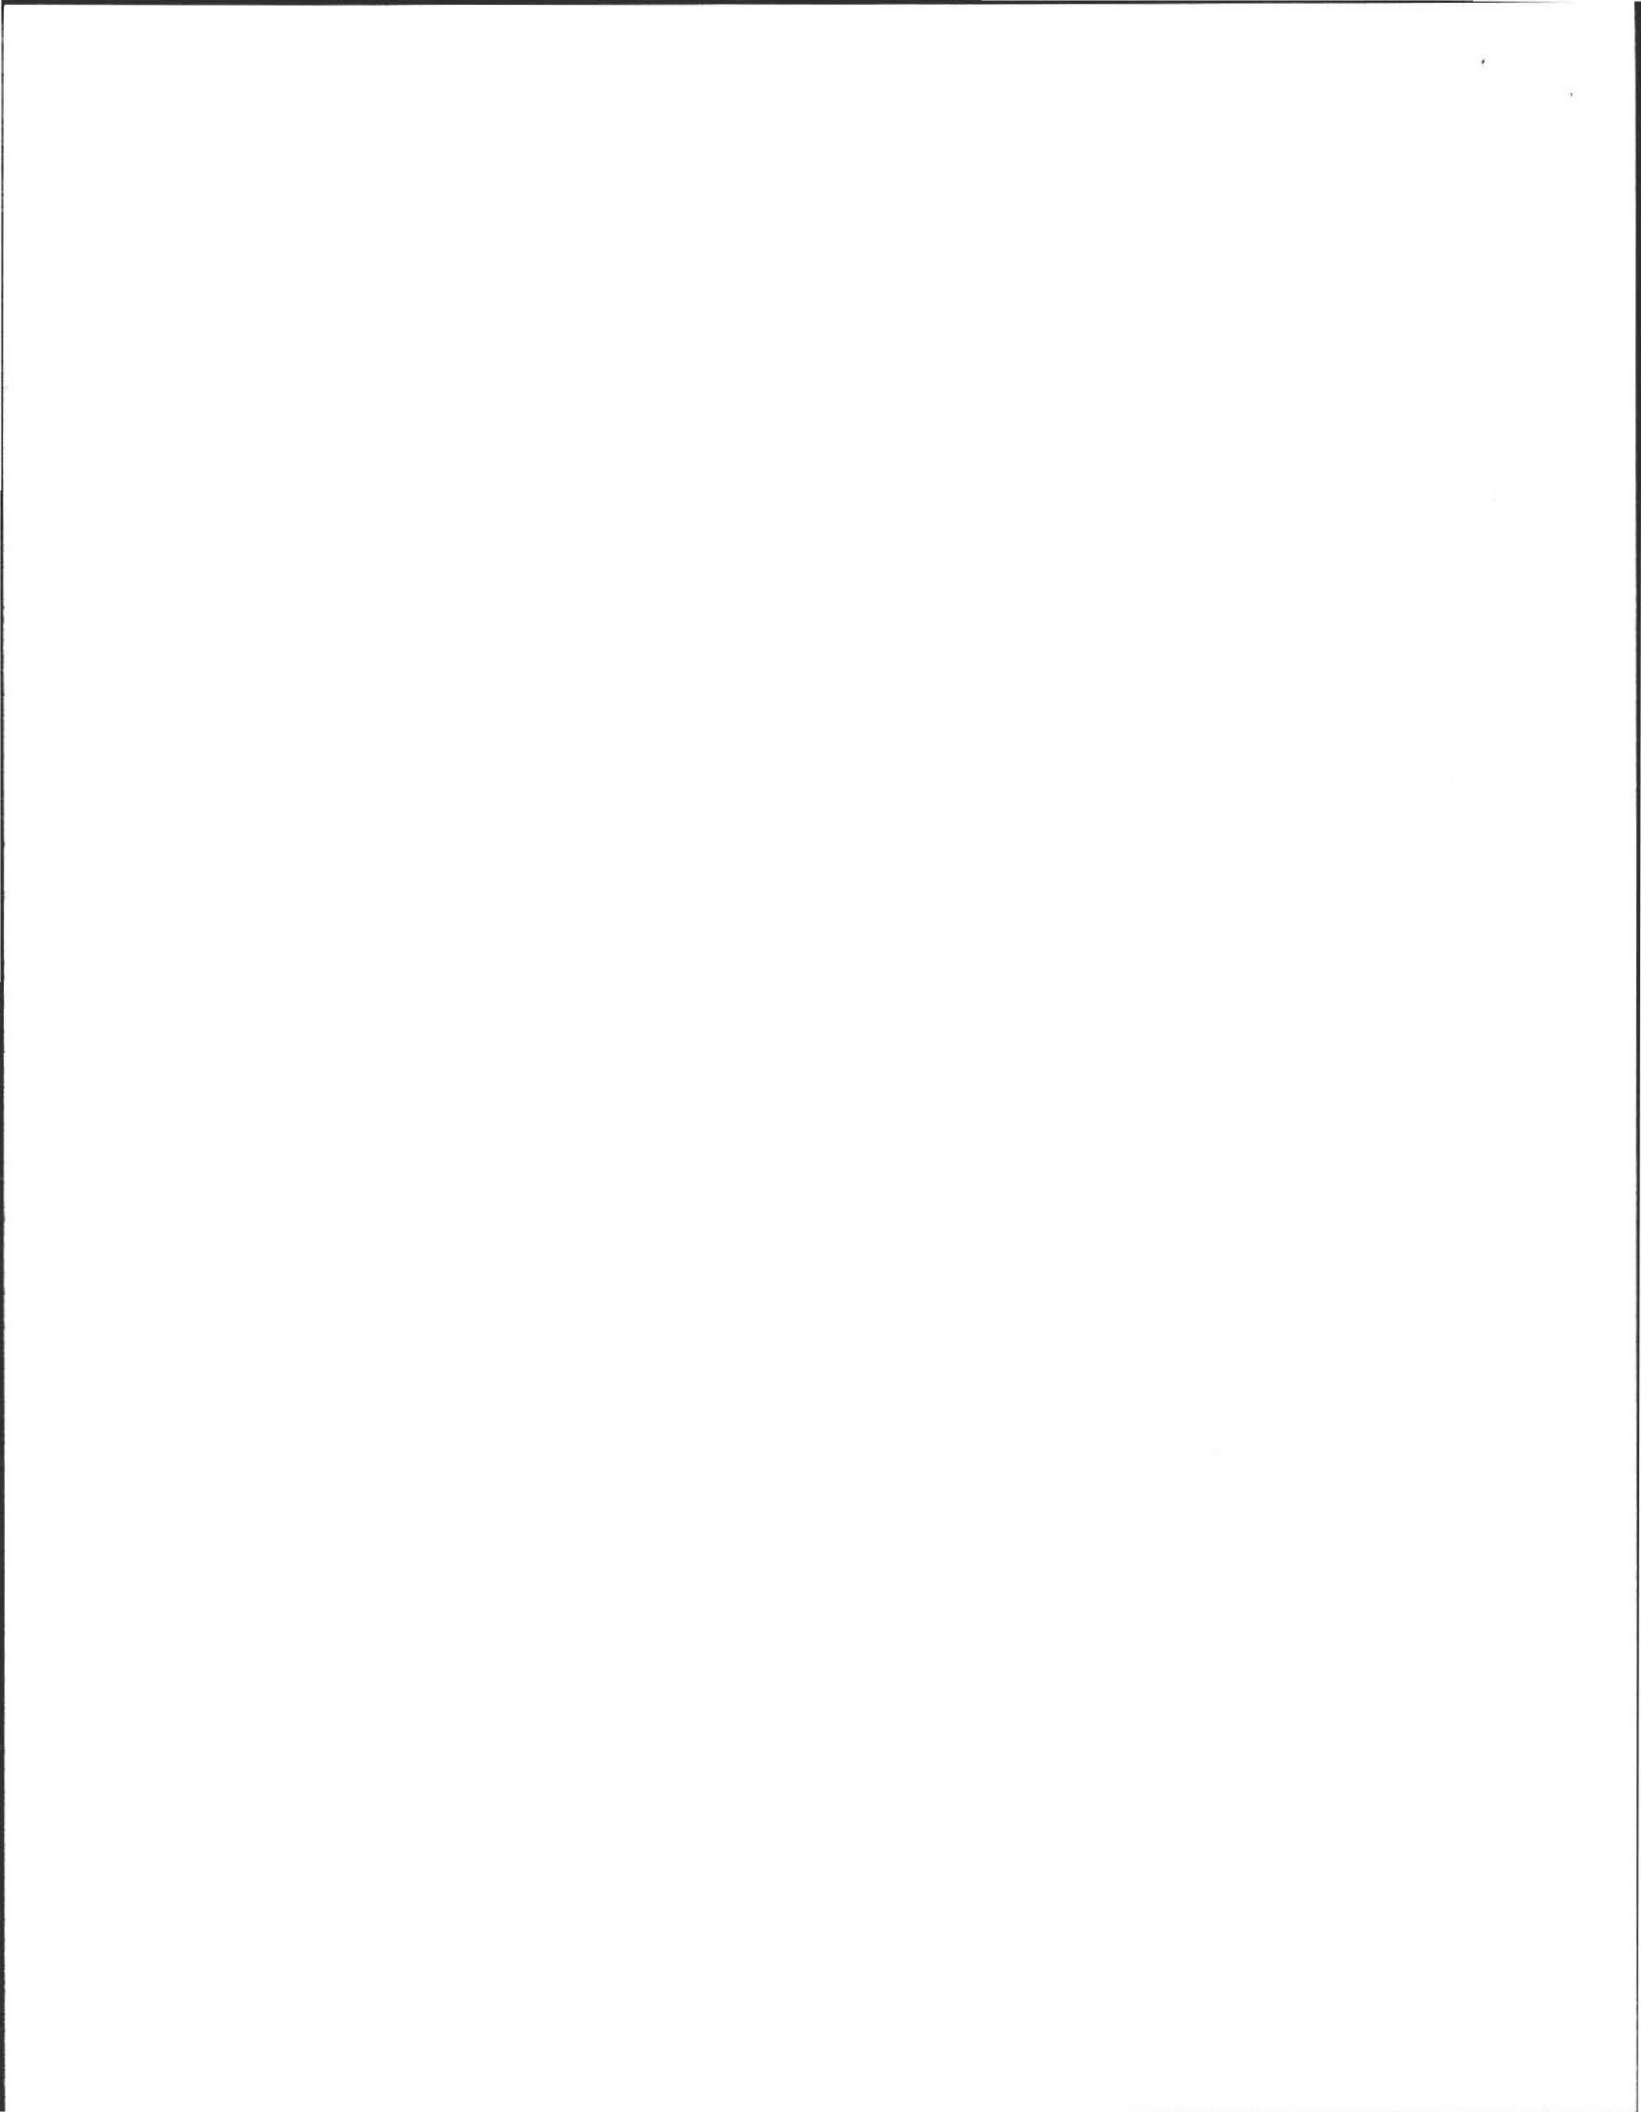

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION (continued)

Property Address: 751 NE ST

Owner: Founds

Date of Inspection: 12/2/03

BUILDING SEWER (locate on site plan)


Depth below grade: 14"
Materials of construction: cast iron 40 PVC other (explain): _____
Distance from private water supply well or suction line: 10' +
Comments (on condition of joints, venting, evidence of leakage, etc.):
OK

SEPTIC TANK: 45' (locate on site plan)

Depth below grade: 26'
Material of construction: concrete metal fiberglass polyethylene
 other(explain) _____
If tank is metal list age: ___ Is age confirmed by a Certificate of Compliance (yes or no): ___ (attach a copy of certificate)
Dimensions: 8.5' x 4.5' x 4.5'
Sludge depth: 3"
Distance from top of sludge to bottom of outlet tee or baffle: 40"
Scum thickness: 1"
Distance from top of scum to top of outlet tee or baffle: 6"
Distance from bottom of scum to bottom of outlet tee or baffle: 10"
How were dimensions determined: MEAS.
Comments (on pumping recommendations, inlet and outlet tee or baffle condition, structural integrity, liquid levels as related to outlet invert, evidence of leakage, etc.):
BUILT IN - BAFFLES, OK.

GREASE TRAP: N/A (locate on site plan)

Depth below grade: ___
Material of construction: ___ concrete ___ metal ___ fiberglass ___ polyethylene ___ other (explain): _____
Dimensions: _____
Scum thickness: _____
Distance from top of scum to top of outlet tee or baffle: _____
Distance from bottom of scum to bottom of outlet tee or baffle: _____
Date of last pumping: _____
Comments (on pumping recommendations, inlet and outlet tee or baffle condition, structural integrity, liquid levels as related to outlet invert, evidence of leakage, etc.):

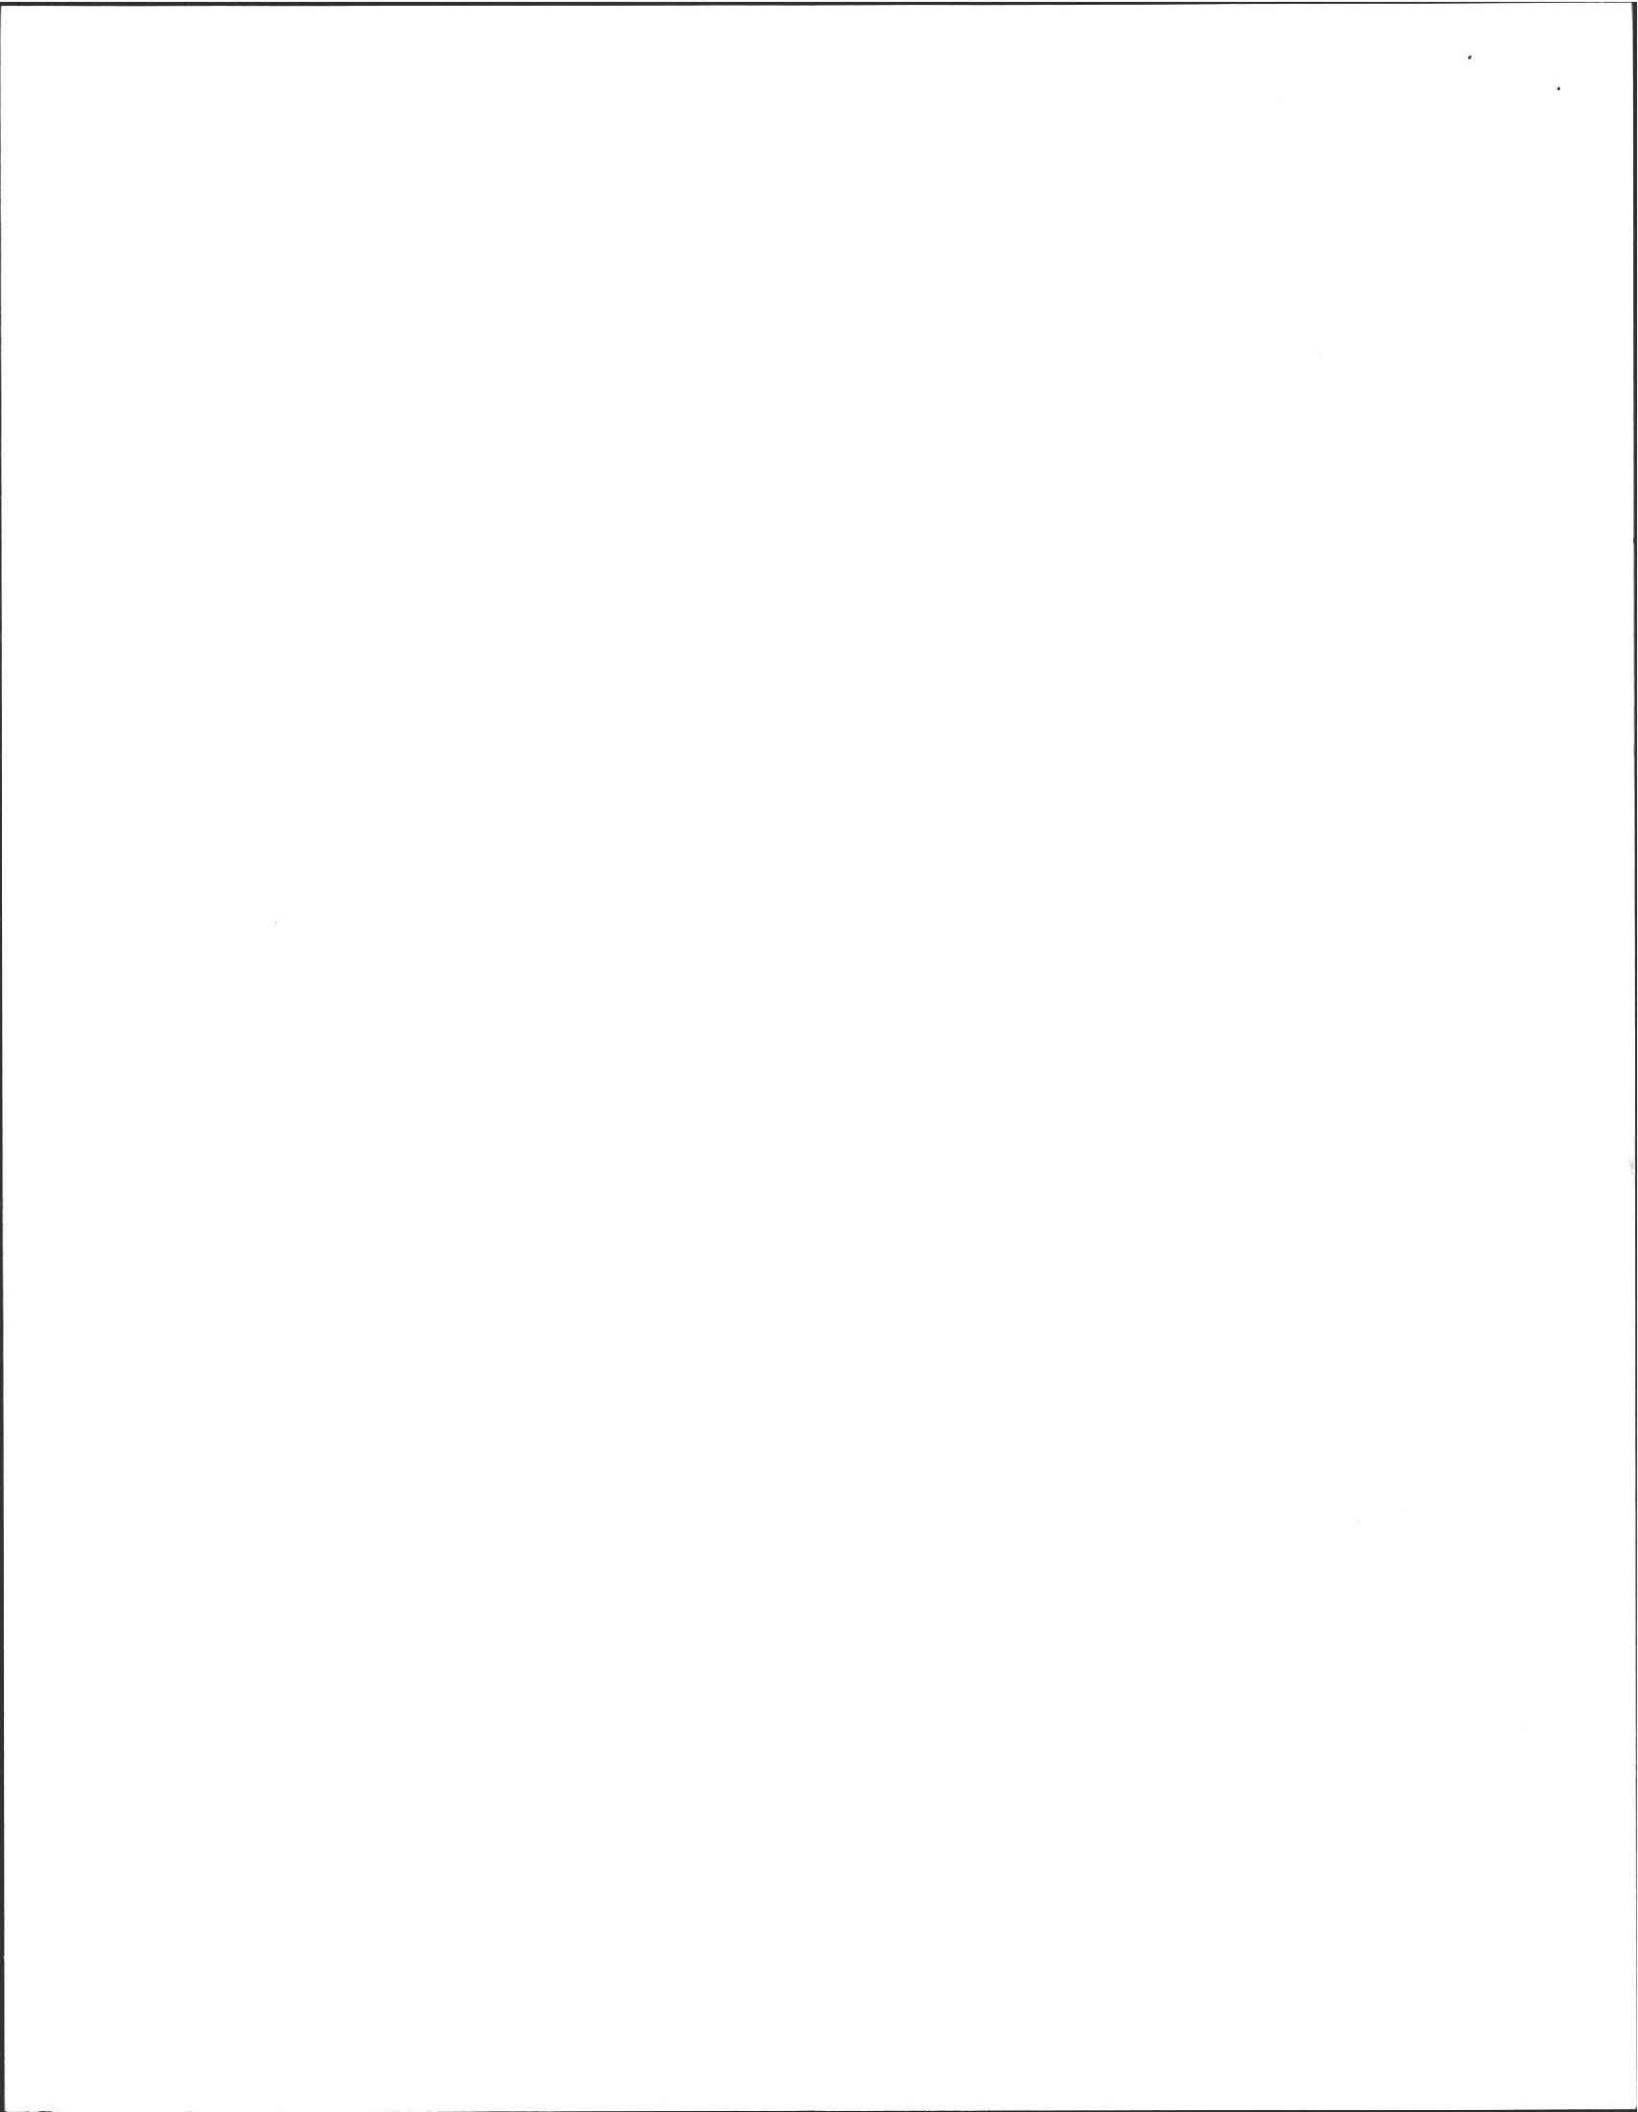

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION (continued)

Property Address: 751 NE ST.

Owner: FARDS

Date of Inspection: 12/2/03

TIGHT or HOLDING TANK: No (tank must be pumped at time of inspection)(locate on site plan)

Depth below grade: _____

Material of construction: ___ concrete ___ metal ___ fiberglass ___ polyethylene ___ other(explain): _____

Dimensions: _____

Capacity: _____ gallons

Design Flow: _____ gallons/day

Alarm present (yes or no): _____

Alarm level: _____ Alarm in working order (yes or no): _____

Date of last pumping: _____

Comments (condition of alarm and float switches, etc.): _____

DISTRIBUTION BOX: yes (if present must be opened)(locate on site plan)

Depth of liquid level above outlet invert: 0 IN.


Comments (note if box is level and distribution to outlets equal, any evidence of solids carryover, any evidence of leakage into or out of box, etc.):
Good condition

PUMP CHAMBER: yes (locate on site plan)

Pumps in working order (yes or no): yes

Alarms in working order (yes or no): yes

Comments (note condition of pump chamber, condition of pumps and appurtenances, etc.): _____

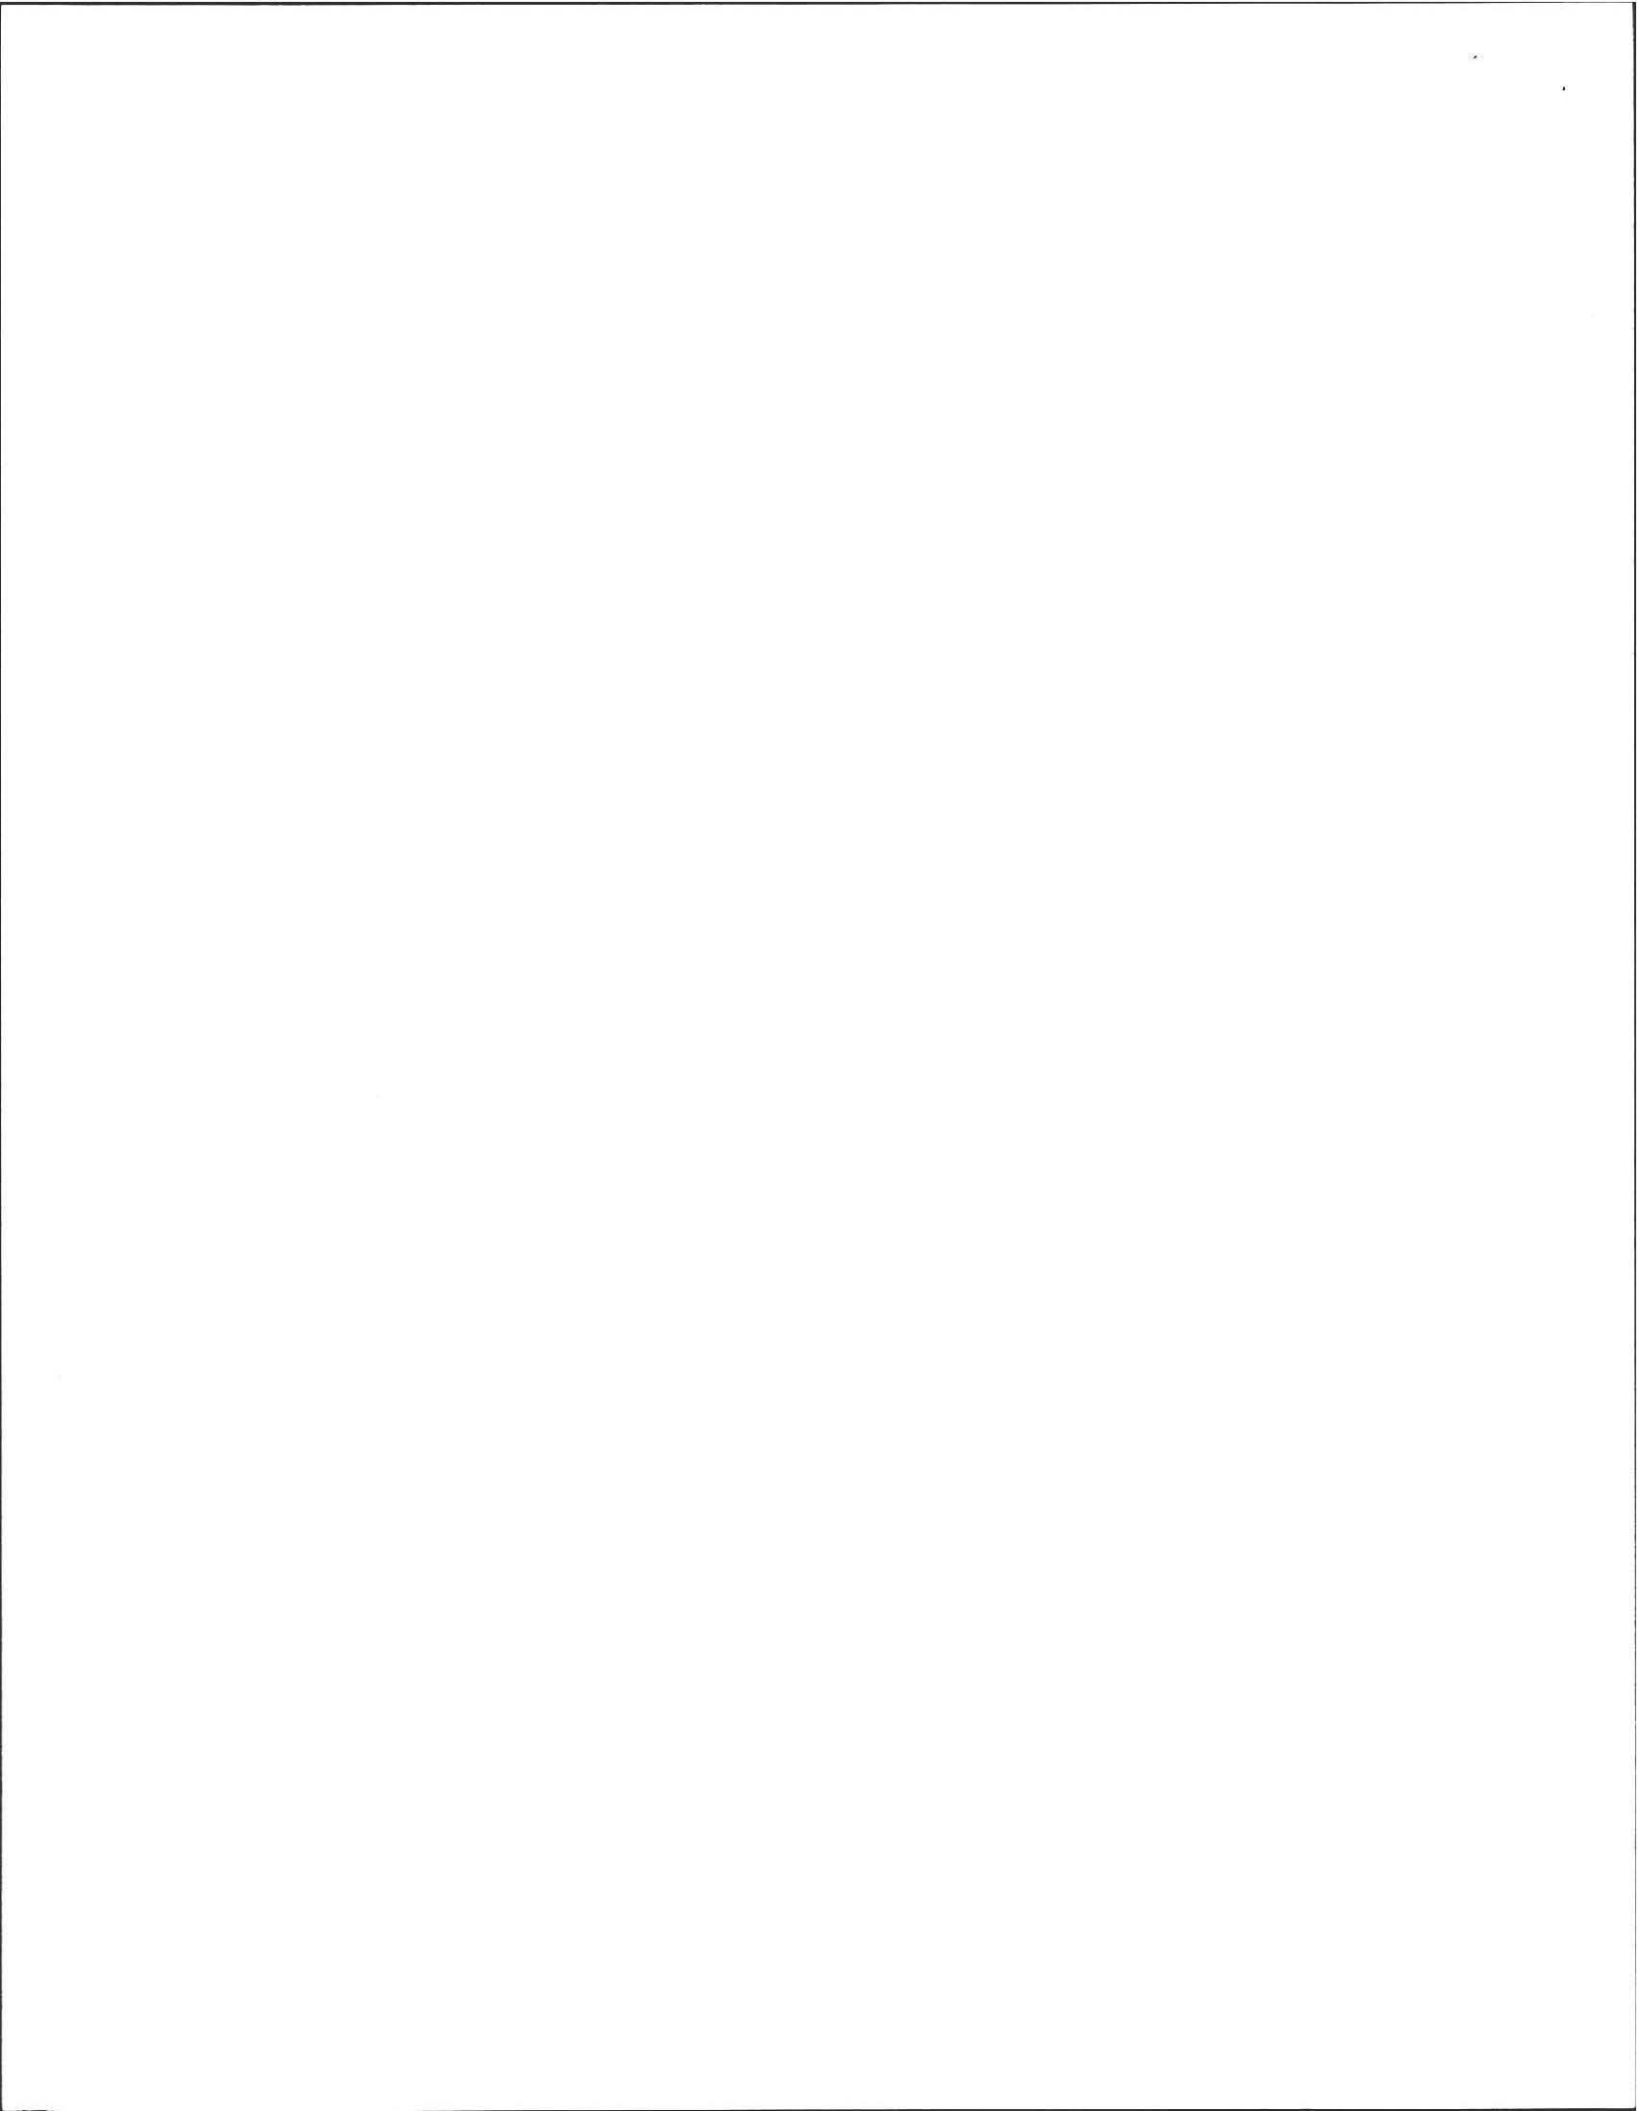

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM

PART C

SYSTEM INFORMATION (continued)

Property Address: 751 NE ST.

Owner: Founds

Date of Inspection: 12/2/03

SOIL ABSORPTION SYSTEM (SAS): Y (locate on site plan, excavation not required)

If SAS not located explain why:

Type

- leaching pits, number: _____
- leaching chambers, number: _____
- leaching galleries, number: _____
- leaching trenches, number, length: _____
- leaching fields, number, dimensions: 60' L x 18' W
- overflow cesspool, number: _____
- innovative/alternative system Type/name of technology: _____

Comments (note condition of soil, signs of hydraulic failure, level of ponding, damp soil, condition of vegetation, etc.):

No Signs of Failure

CESSPOOLS: No (cesspool must be pumped as part of inspection)(locate on site plan)


- Number and configuration: _____
- Depth – top of liquid to inlet invert: _____
- Depth of solids layer: _____
- Depth of scum layer: _____
- Dimensions of cesspool: _____
- Materials of construction: _____
- Indication of groundwater inflow (yes or no): _____

Comments (note condition of soil, signs of hydraulic failure, level of ponding, condition of vegetation, etc.):

PRIVY: N (locate on site plan)

- Materials of construction: _____
- Dimensions: _____
- Depth of solids: _____

Comments (note condition of soil, signs of hydraulic failure, level of ponding, condition of vegetation, etc.):

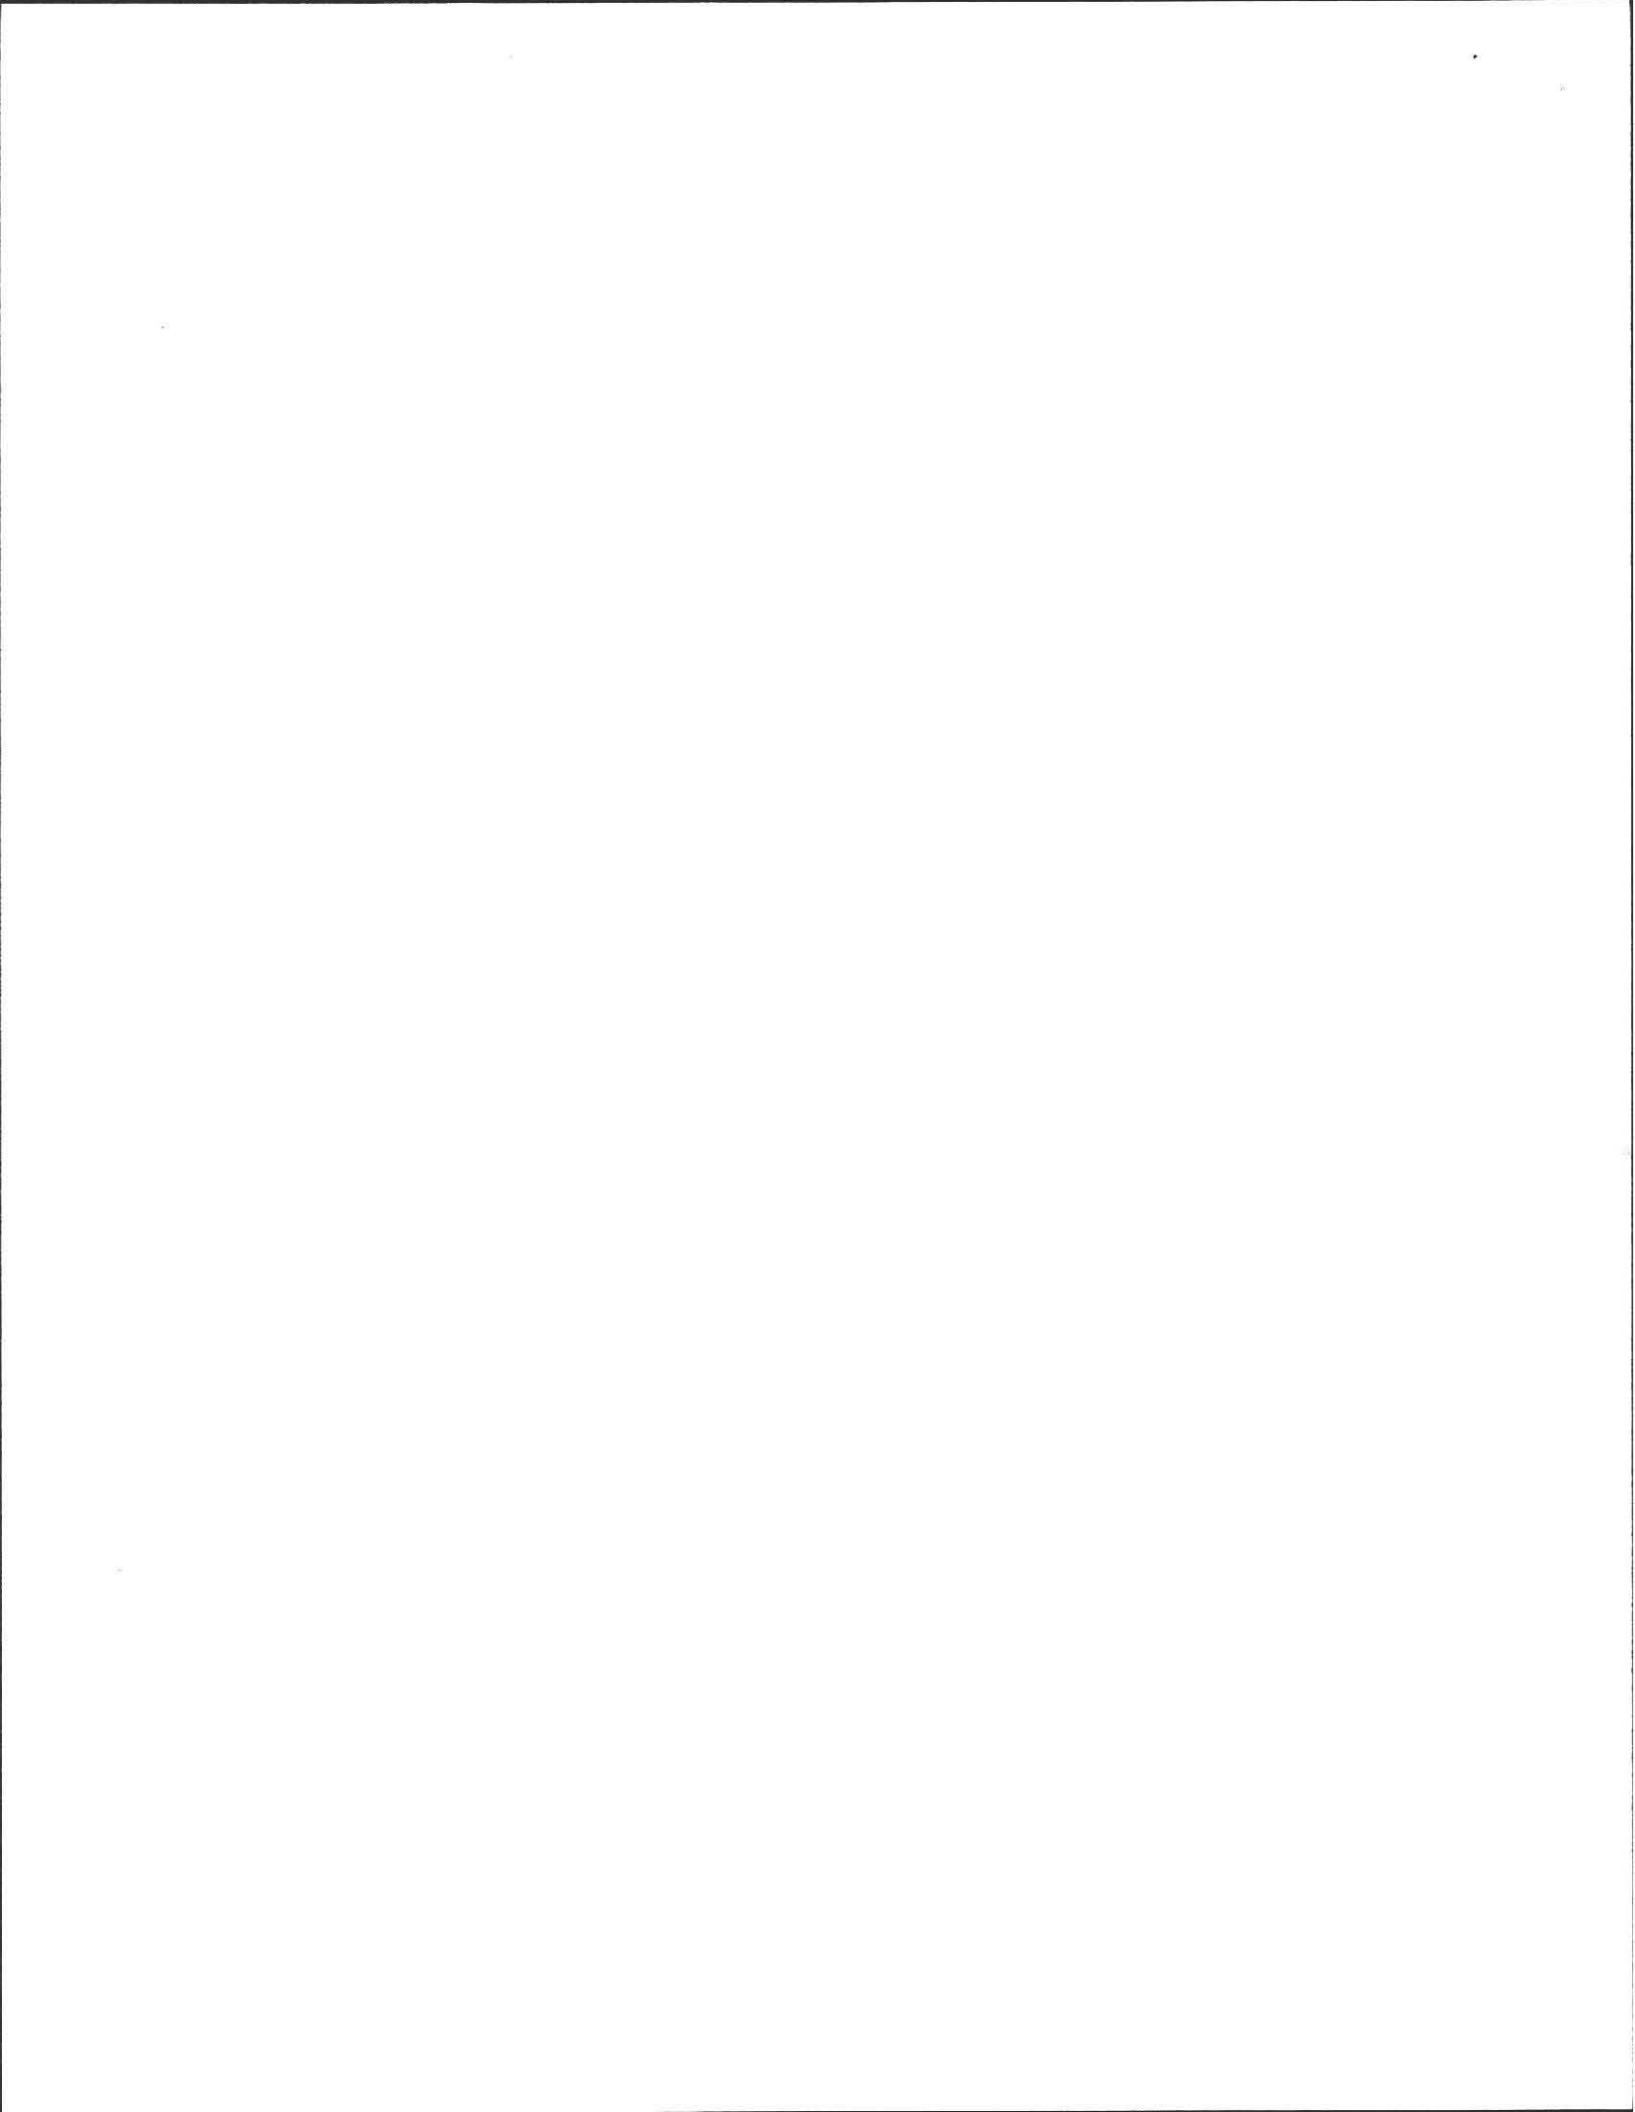

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION (continued)

Property Address: 751 NE ST


Owner: Founds

Date of Inspection: 12/2/03

SKETCH OF SEWAGE DISPOSAL SYSTEM

Provide a sketch of the sewage disposal system including ties to at least two permanent reference landmarks or benchmarks. Locate all wells within 100 feet. Locate where public water supply enters the building.

SEE PLAN ATTACHED

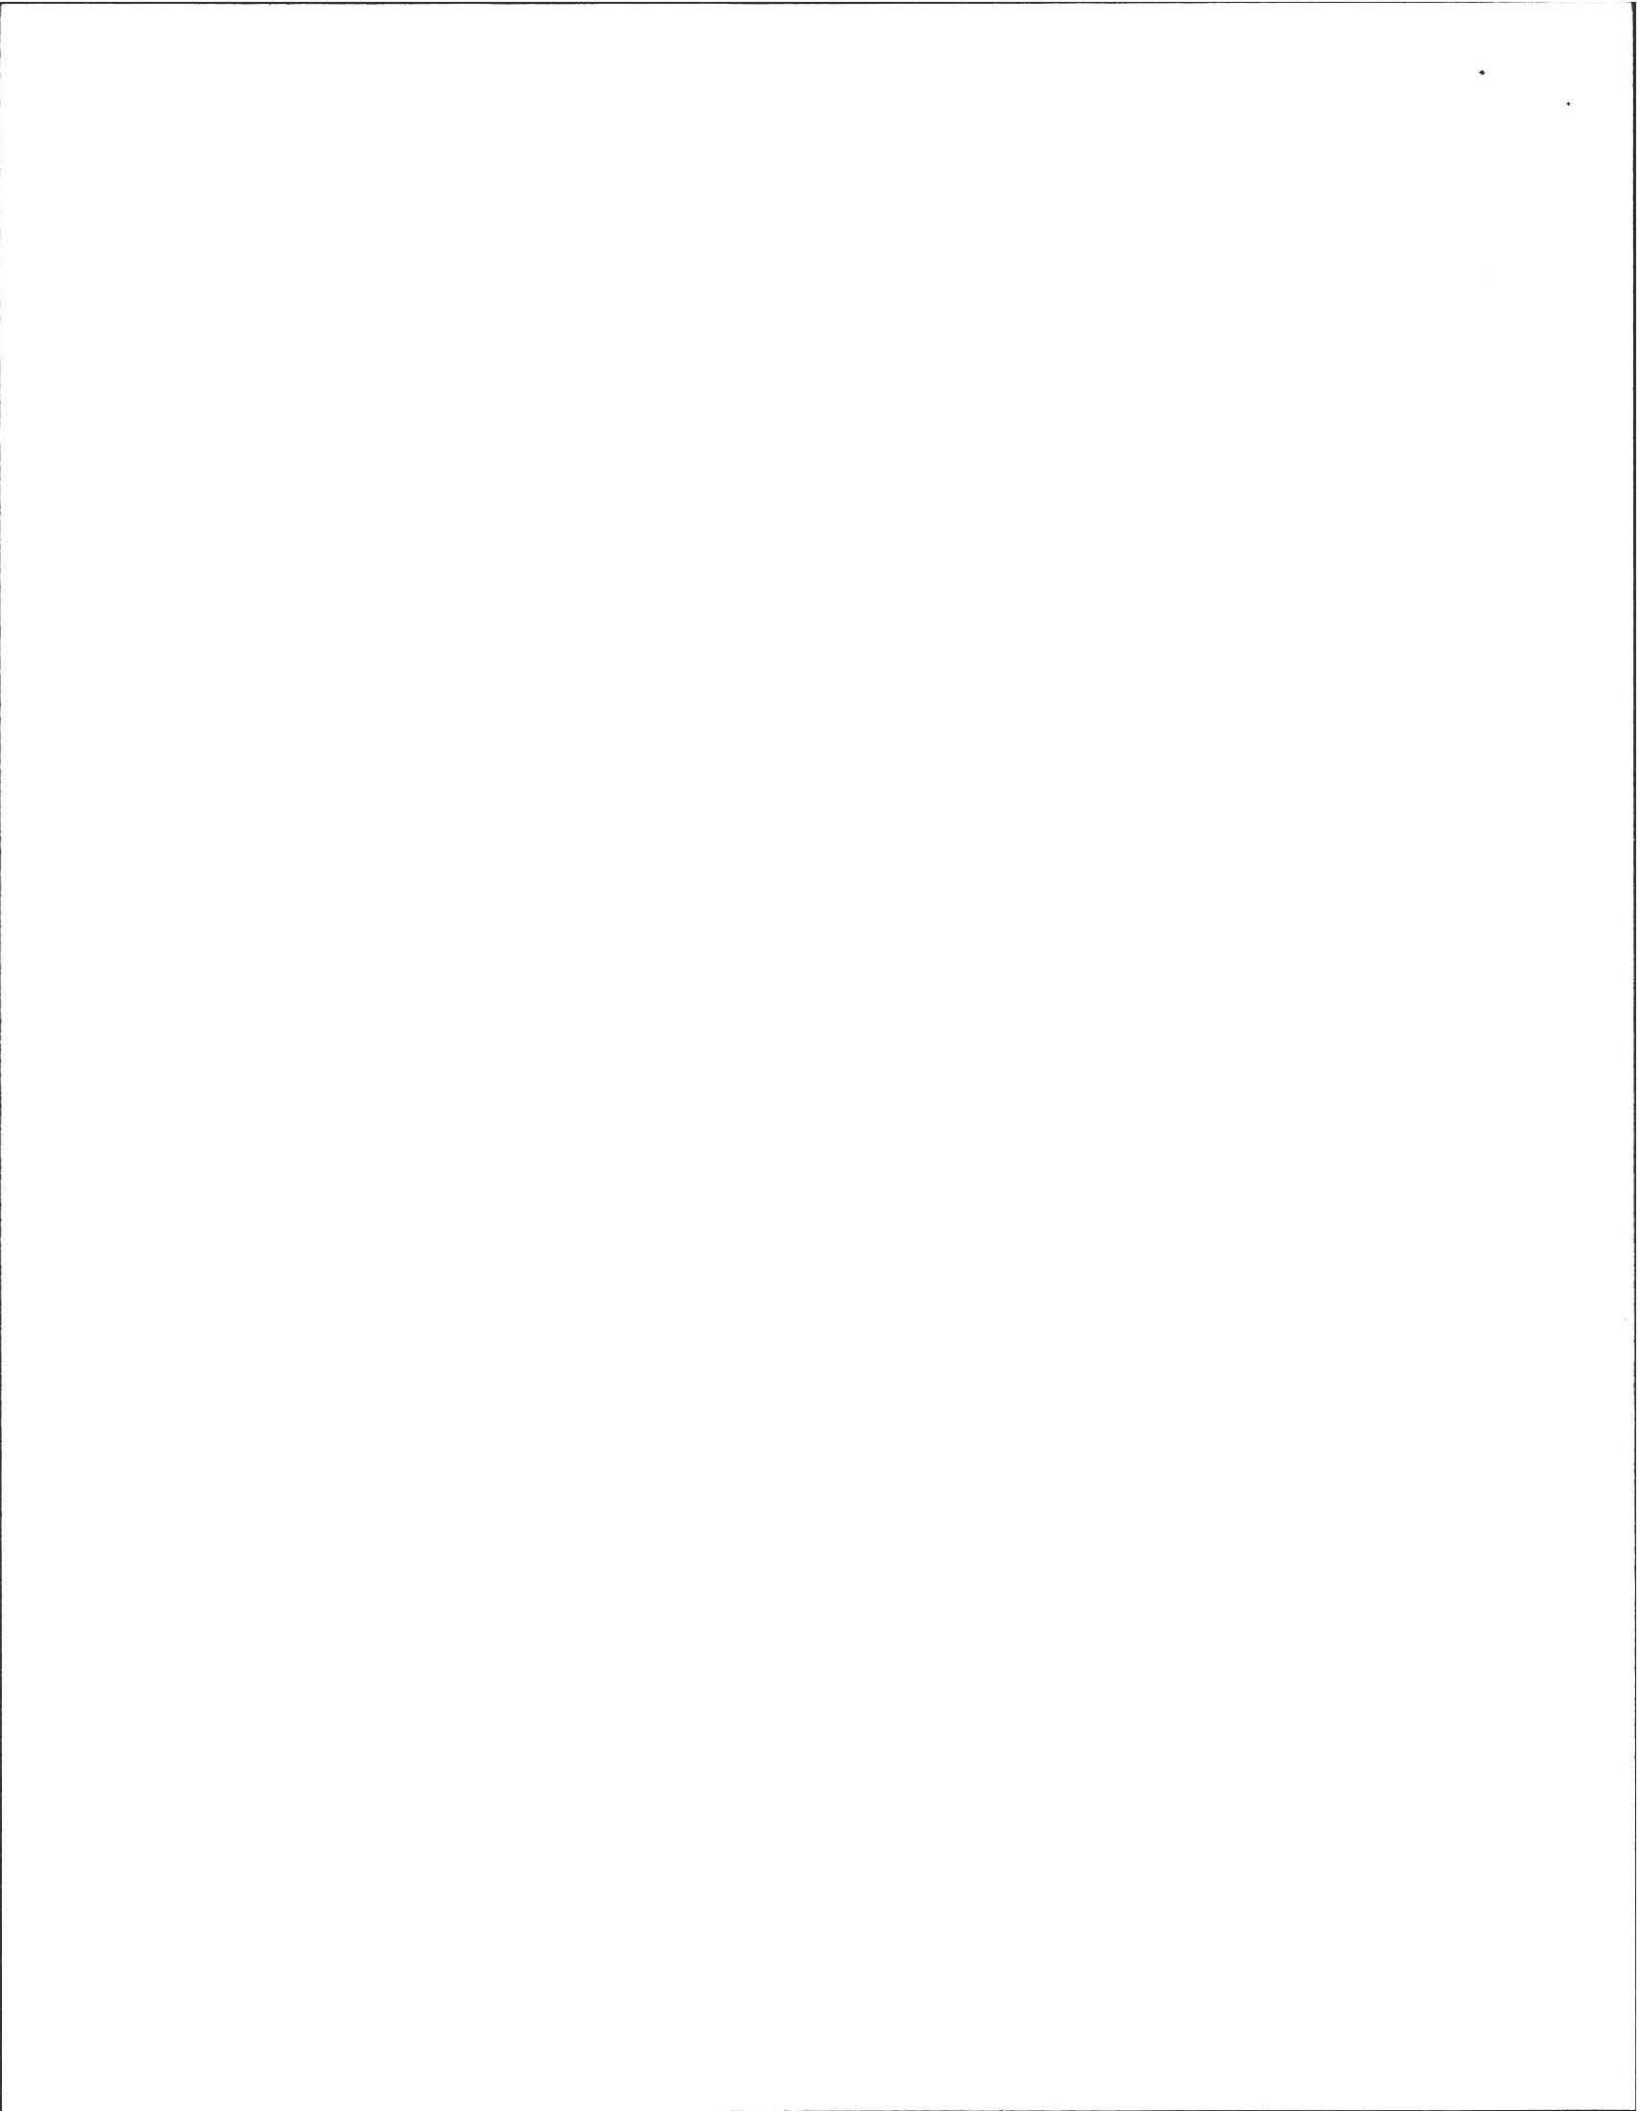

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION (continued)

Property Address: 751 NE ST.

Owner: Founds

Date of Inspection: 12/2/03

SITE EXAM

- Slope
- Surface water
- Check cellar
- Shallow wells


Estimated depth to ground water 4' feet AT SAS. (Elevated)


Please indicate (check) all methods used to determine the high ground water elevation:

- Obtained from system design plans on record - If checked, date of design plan reviewed: 7/13/01
- Observed site (abutting property/observation hole within 150 feet of SAS)
- Checked with local Board of Health-explain: _____
- Checked with local excavators, installers- (attach documentation)
- Accessed USGS database-explain: _____


You must describe how you established the high ground water elevation:

SEE RECORDS.

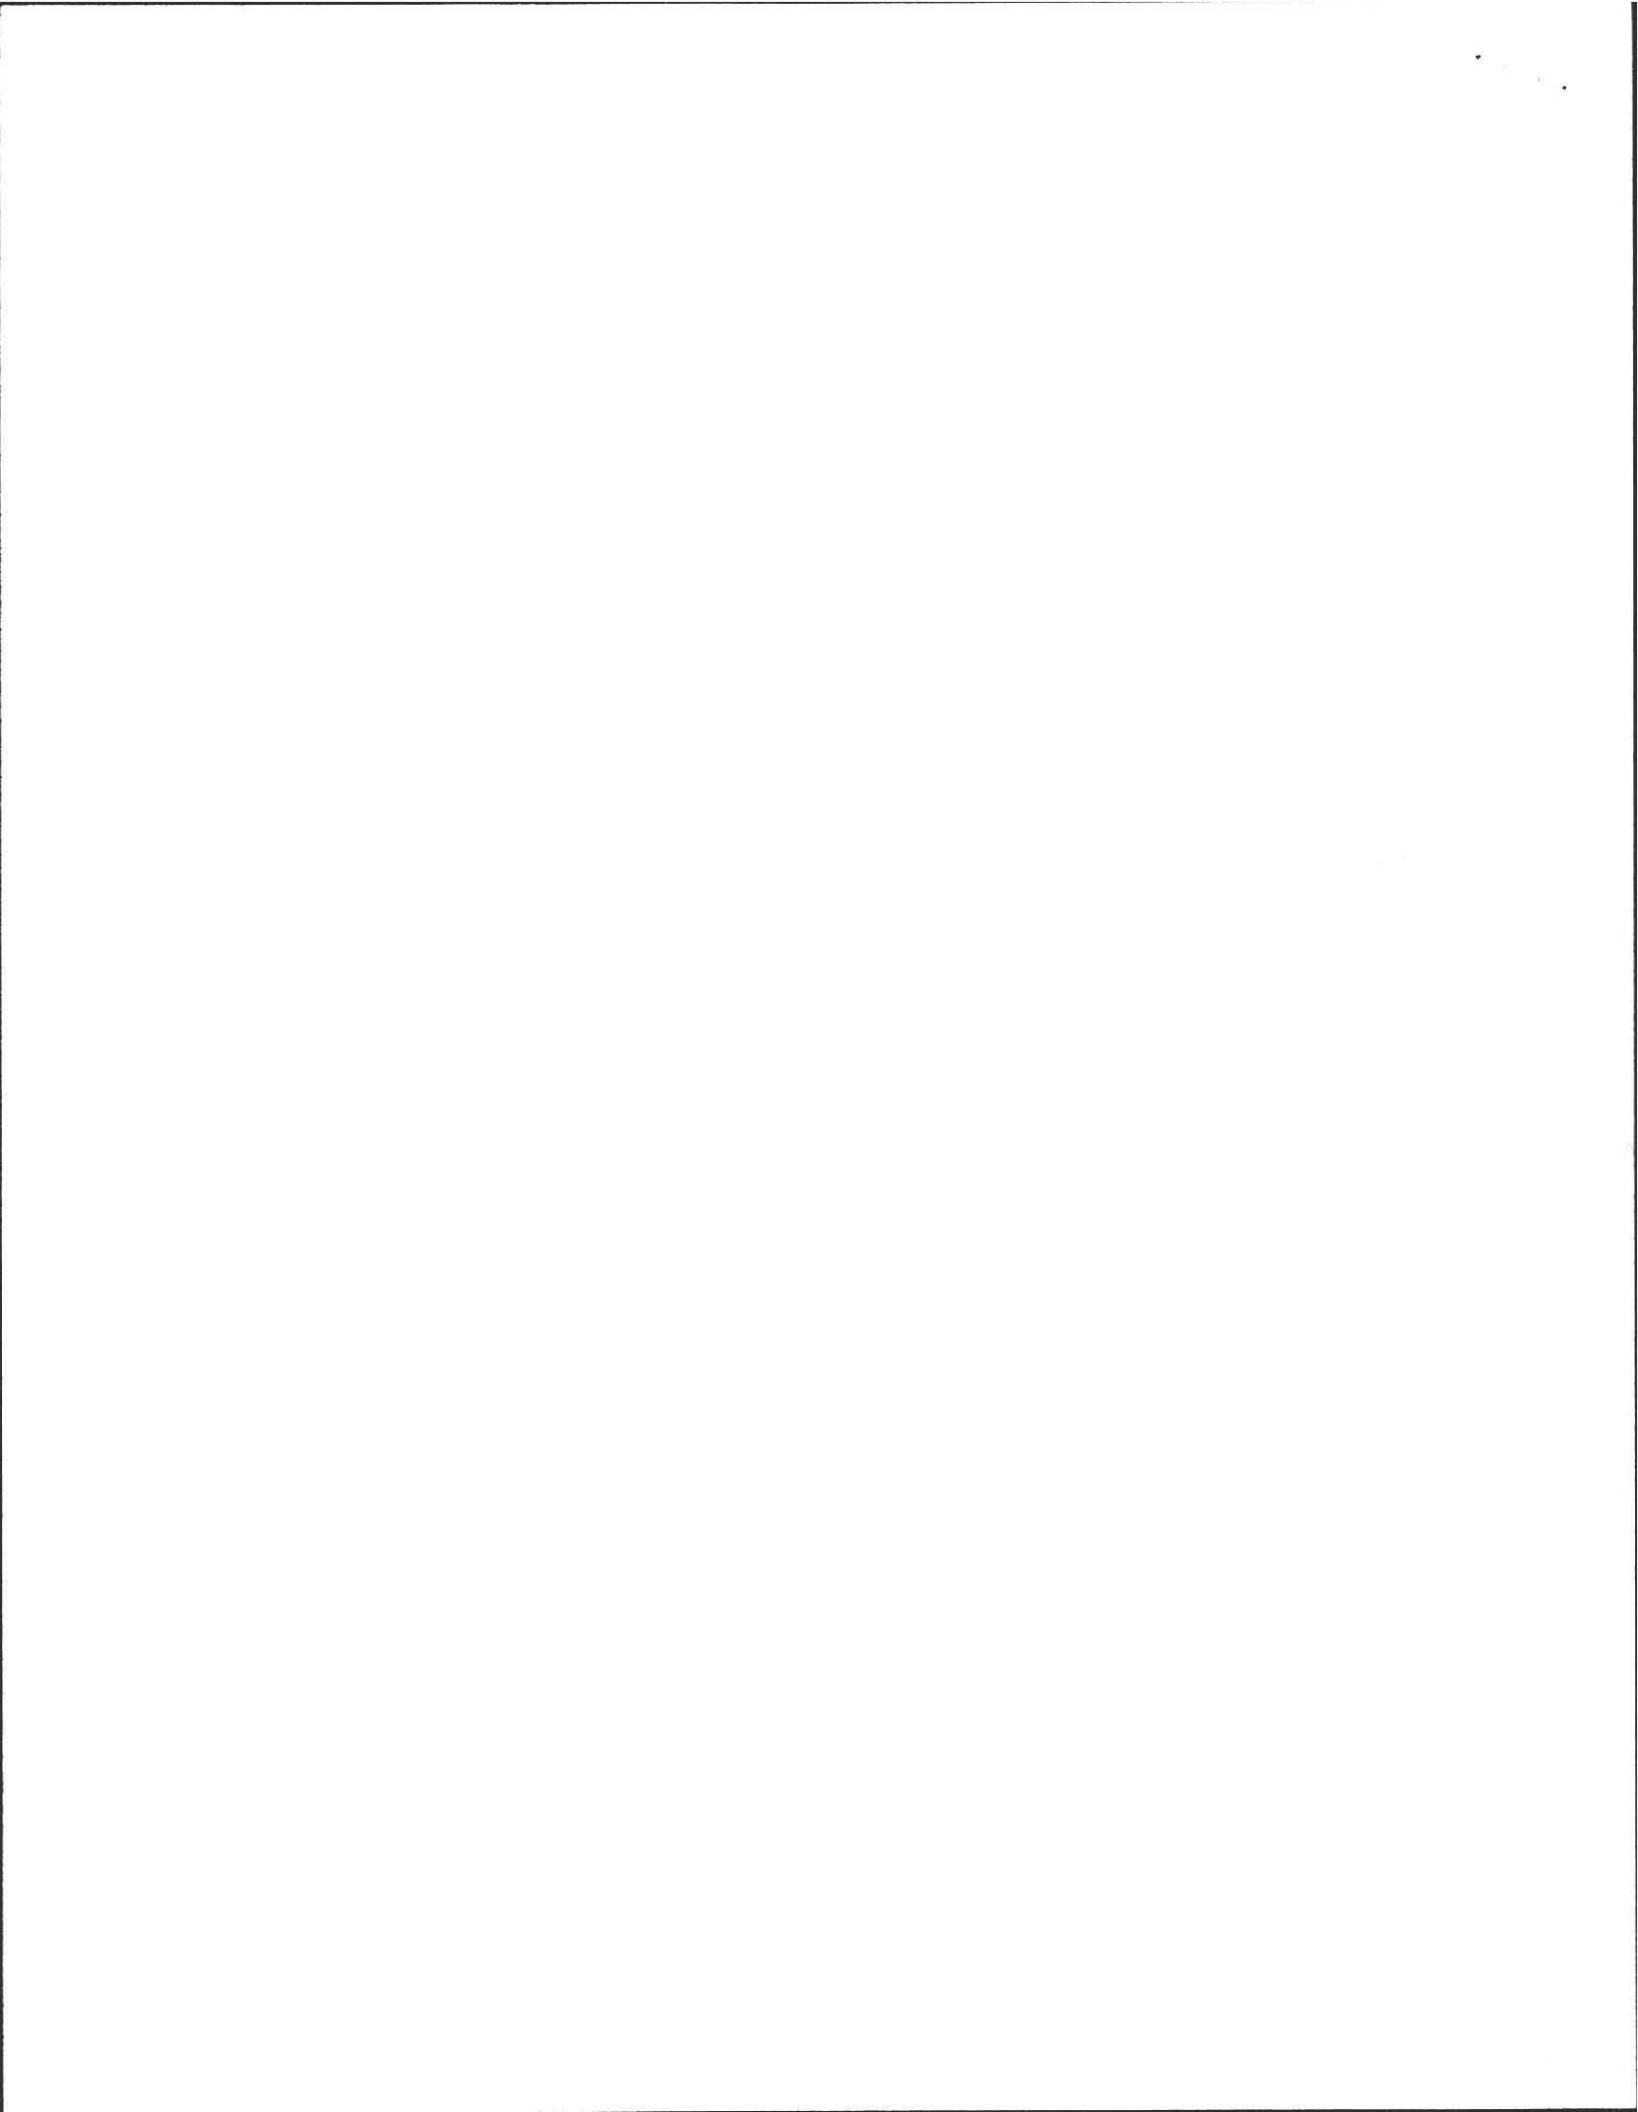

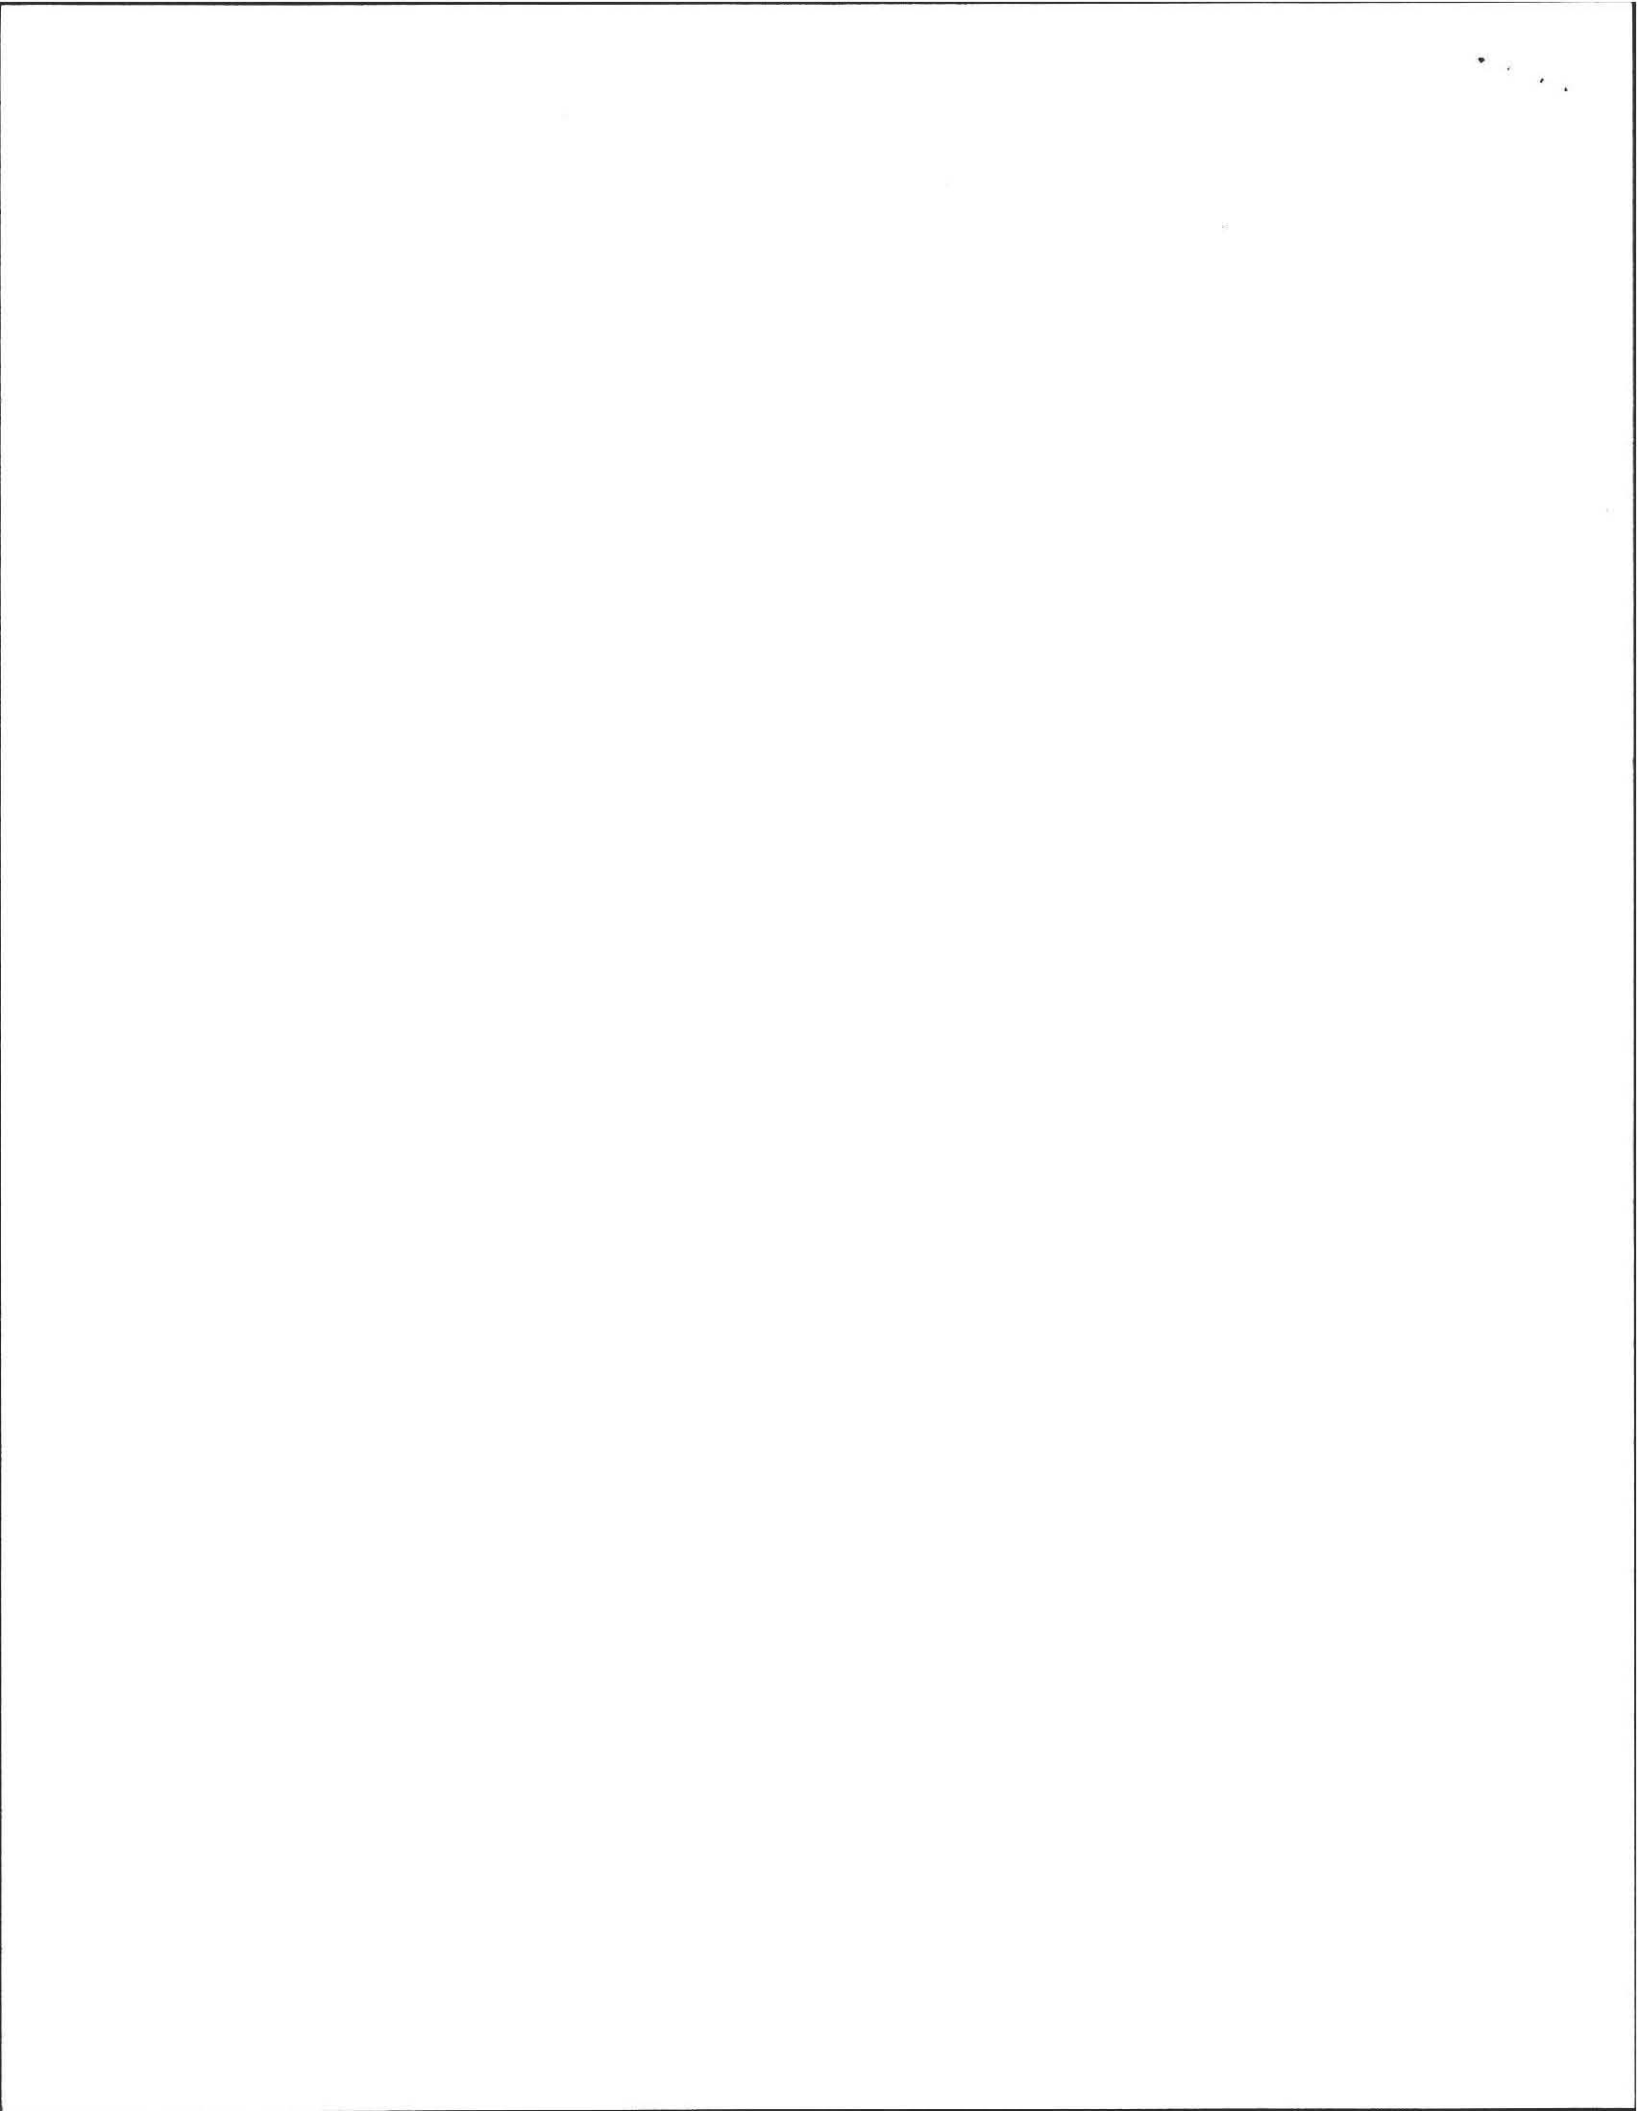


NOTE: There are no surface waters, border of the proposed septic tank or the soil absorber within 400 ft. of the proposed septic tank or to surface water supplies within 200 ft. of the

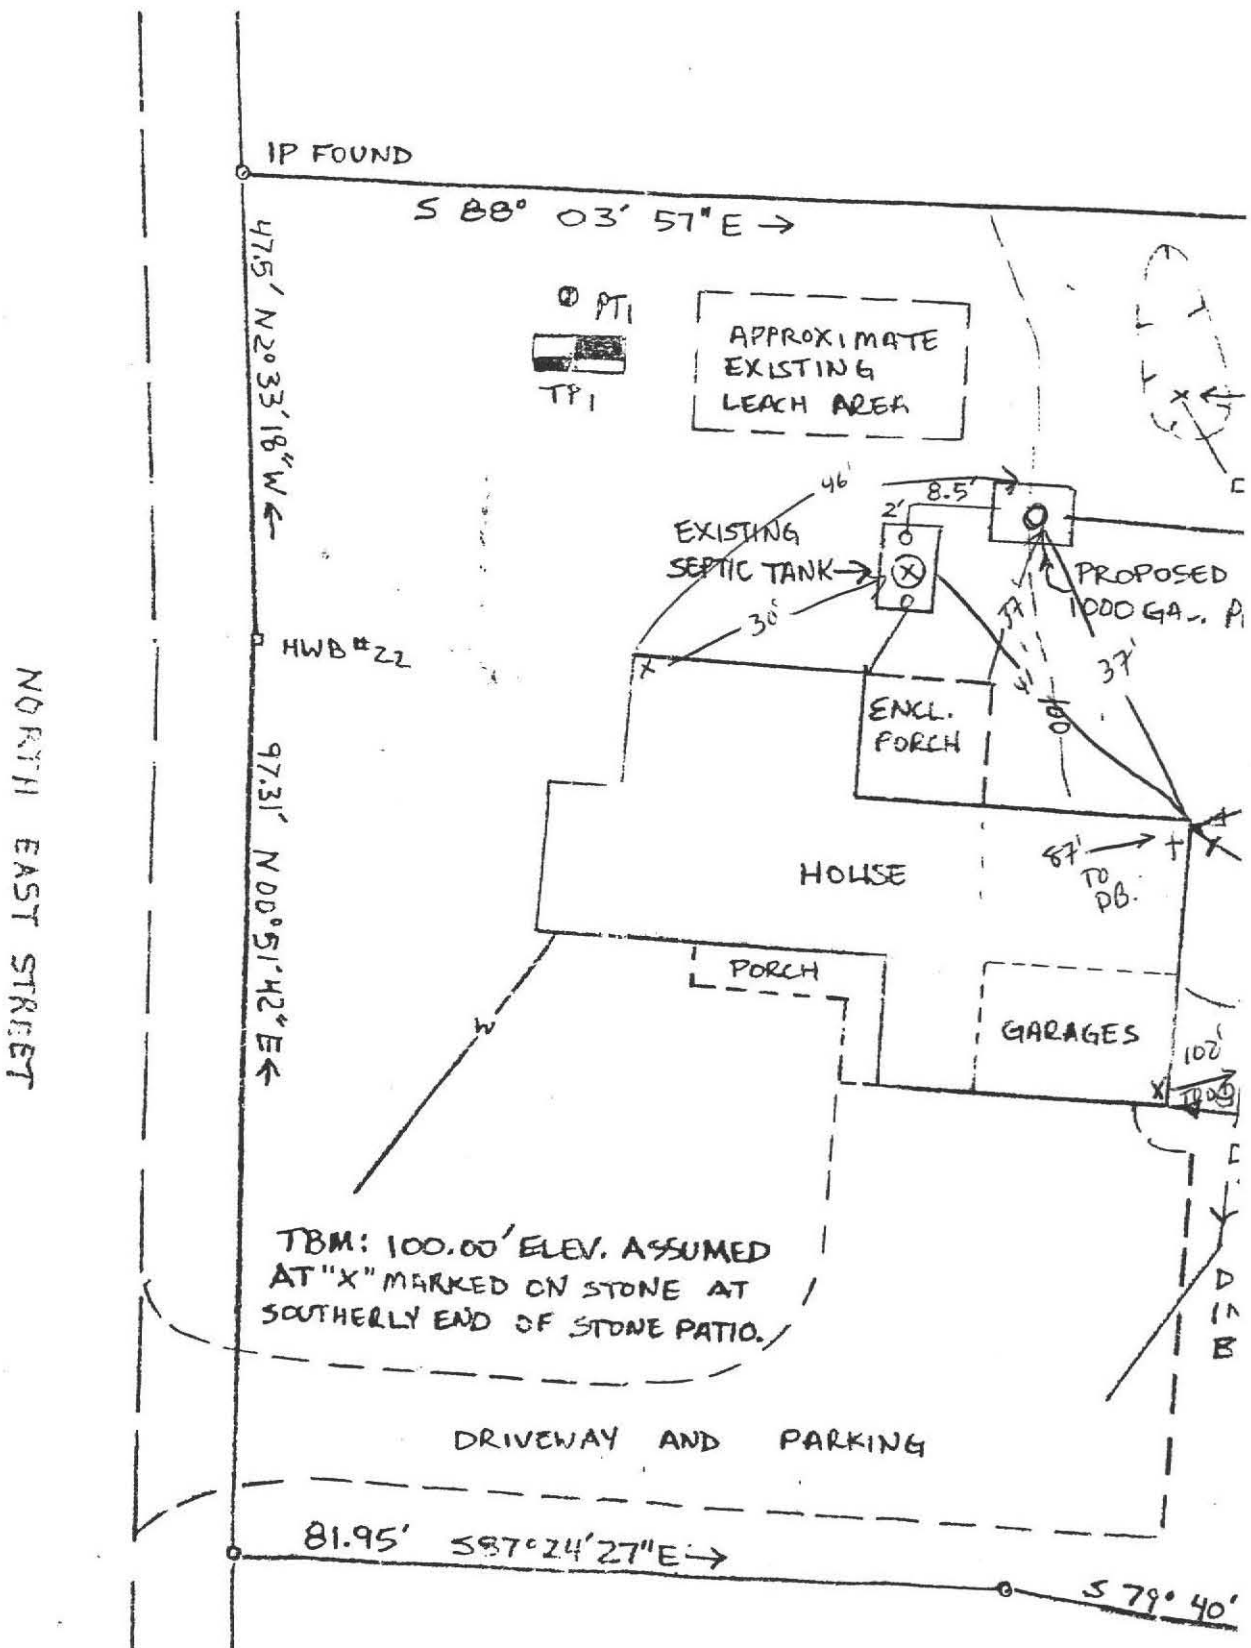

LEGEND

XXX - - - - - CONTOUR LINE (1' INTERVAL)

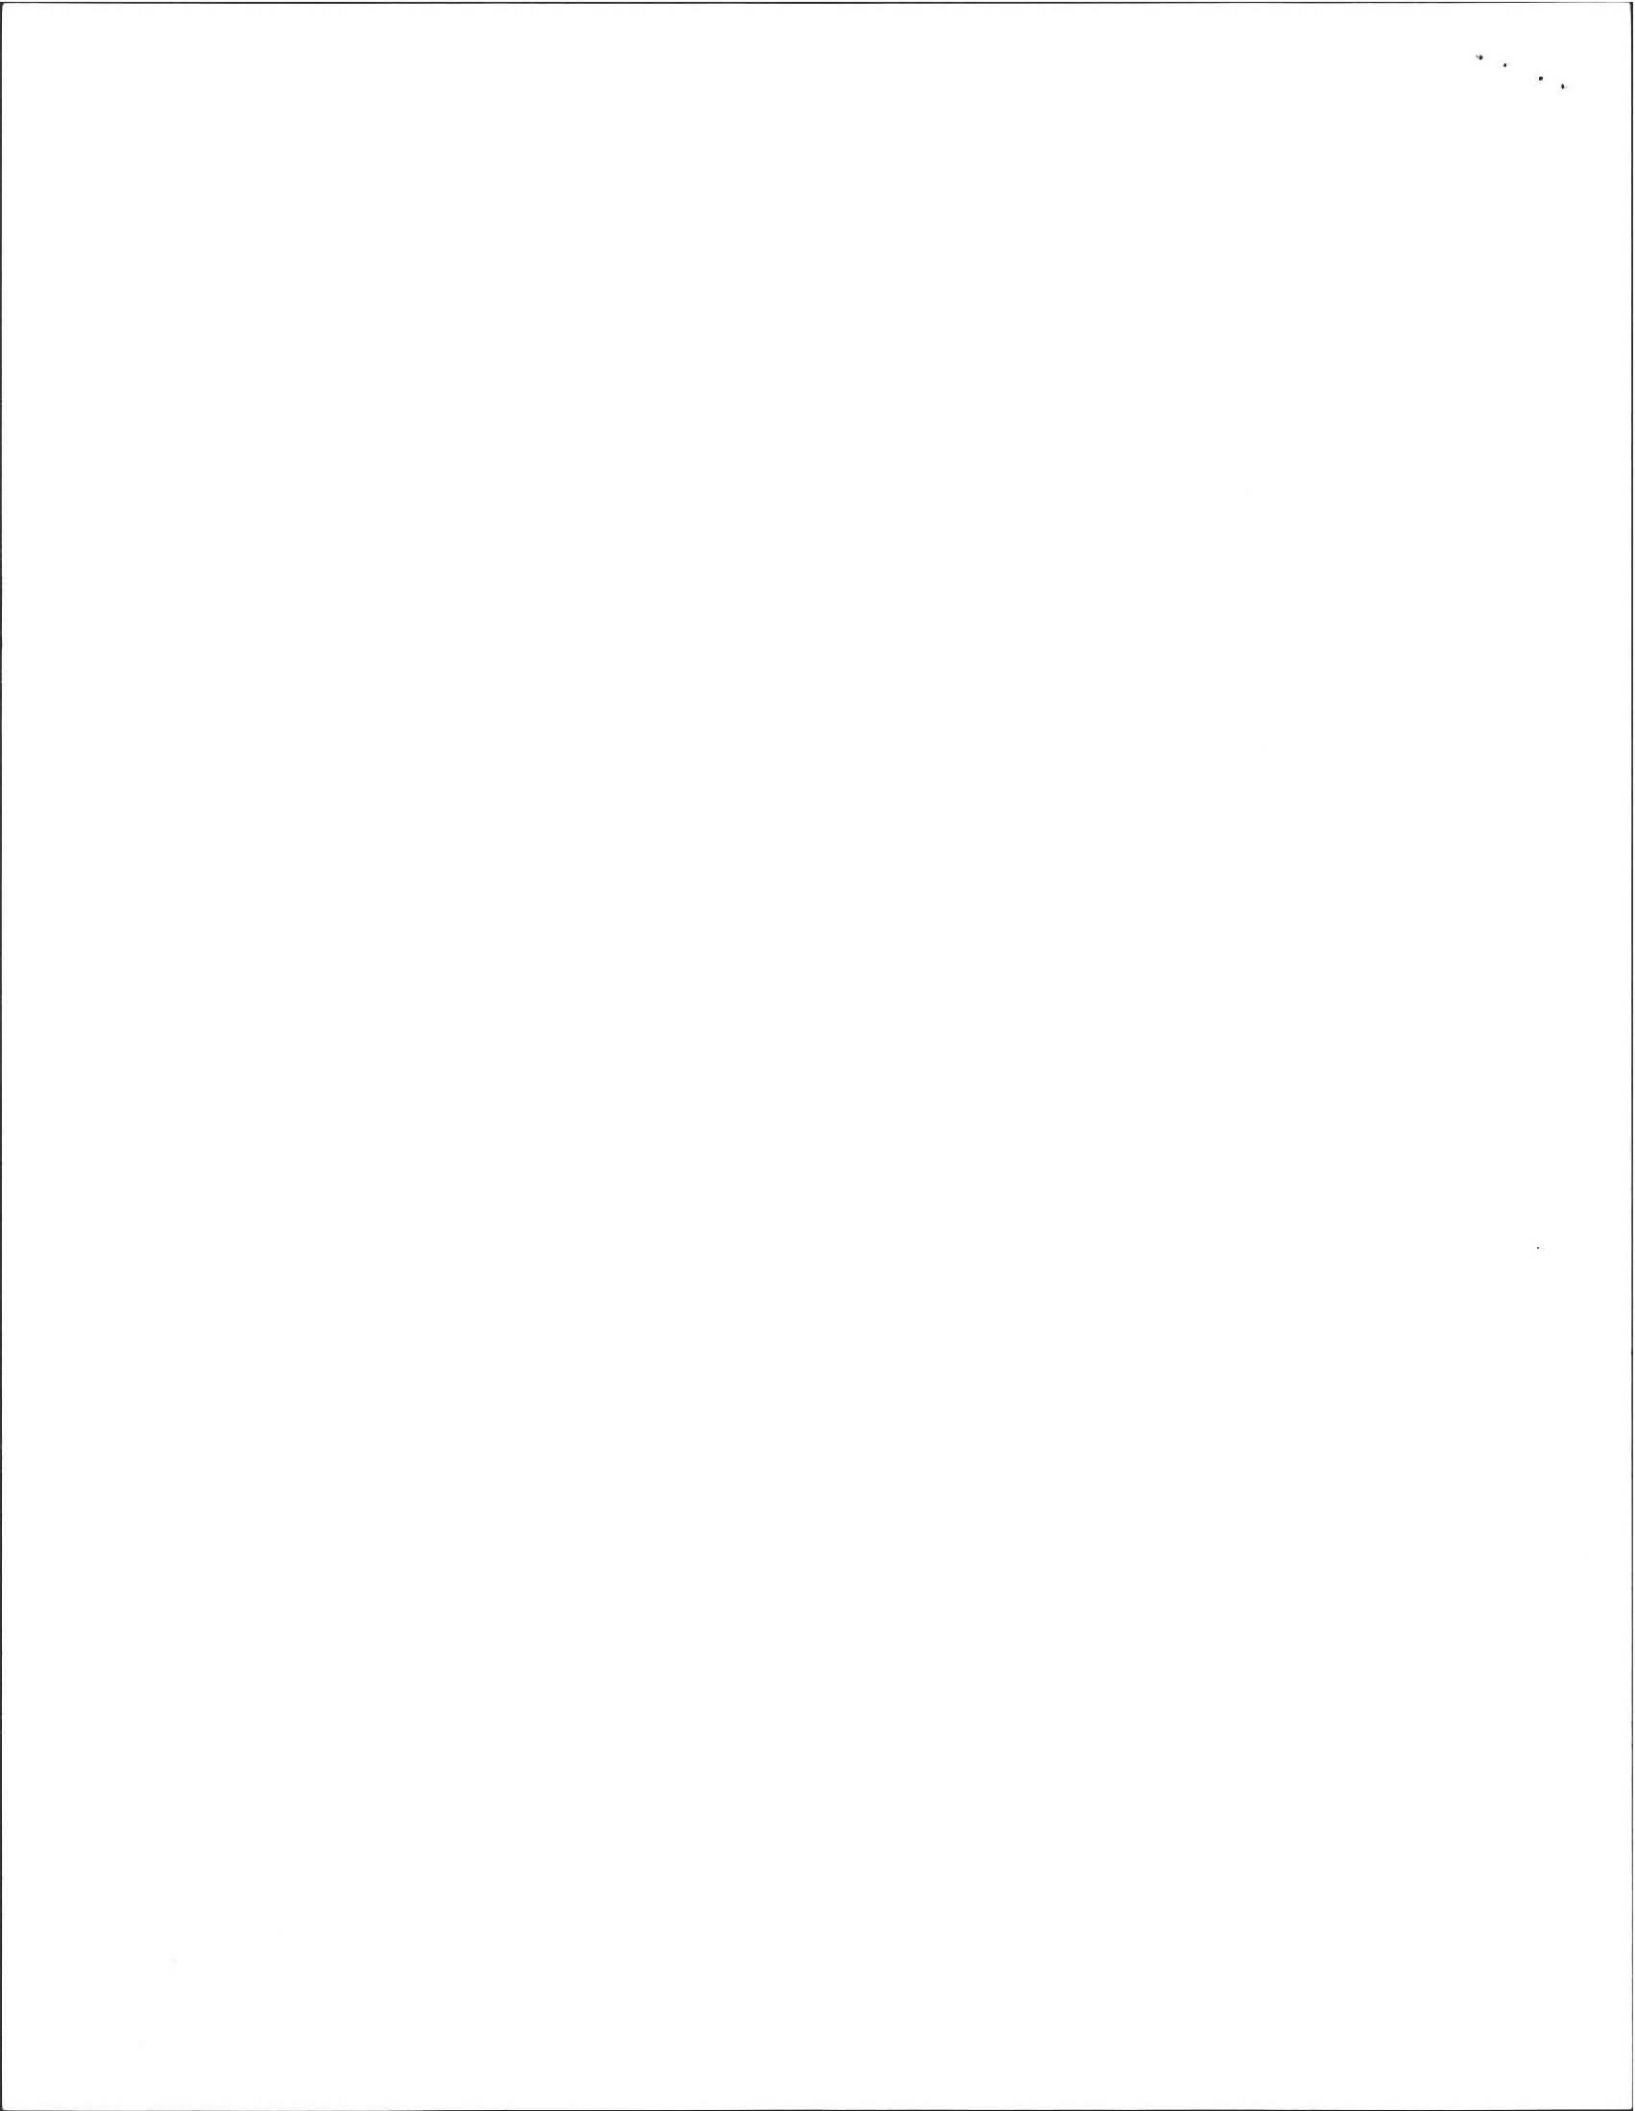



- Property Map**
- Property Lines
 - Hydrographic Property
 - Right of Way Line
 - Town Boundary
 - Lot Lines
 - Former Property Line
 - Subdivision Lot Line
 - Easements
- Driveways**
- Driveway Paved
 - Driveway Unpaved
- Transportation**
- Paved street polygons
 - Unpaved street polyg
- Bridges**
- Bridge decking and str
 - Foot Bridge
 - Rail Bridge
- Basemap 2009**
- Trails
 - Rail Lines
- Structures**
- Building
 - Foundation or in const
 - Outbuilding or Miscel
 - Deck, Porch, Stairs or
 - Mobile home, Trailer
 - Swimming Pool
 - Building Ruins
 - Water storage tank
- Rivers and Streams**
- Streams
 - Major Culverts
 - Hydro Connector
 - Headwalls, Floodwalls
- Landcover**
- Brush and scrub vege
 - Tree and forest vege
 - Cultivated field
 - Gravel pile
 - Quarry
 - Misc Impervious Surfa
- Parking**
- Parking Paved
 - Parking Unpaved

Horizontal Datum: MA Stateplane Coordinate System, Zone 4151, Datum NAD83, Feet
 Vertical Datum: NAVD86, Feet


Planimetric & topographic basemap features compiled at 1"=40' scale from April, 2009 Aerial Photography. Parcels compiled to match the basemap; revisions are ongoing.

The information depicted on this map is for planning purposes only. It may not be adequate for legal boundary definition, regulatory interpretation, or property conveyance purposes. Utility structures and underground utility locations are approximate and require field verification.

THE TOWN OF AMHERST MAKES NO WARRANTIES, EXPRESSED OR IMPLIED, CONCERNING THE ACCURACY, COMPLETENESS, RELIABILITY, OR SUITABILITY OF THESE DATA. THE TOWN OF AMHERST DOES NOT ASSUME ANY LIABILITY ASSOCIATED WITH THE USE OR MISUSE OF THIS INFORMATION.

1" = 51 ft



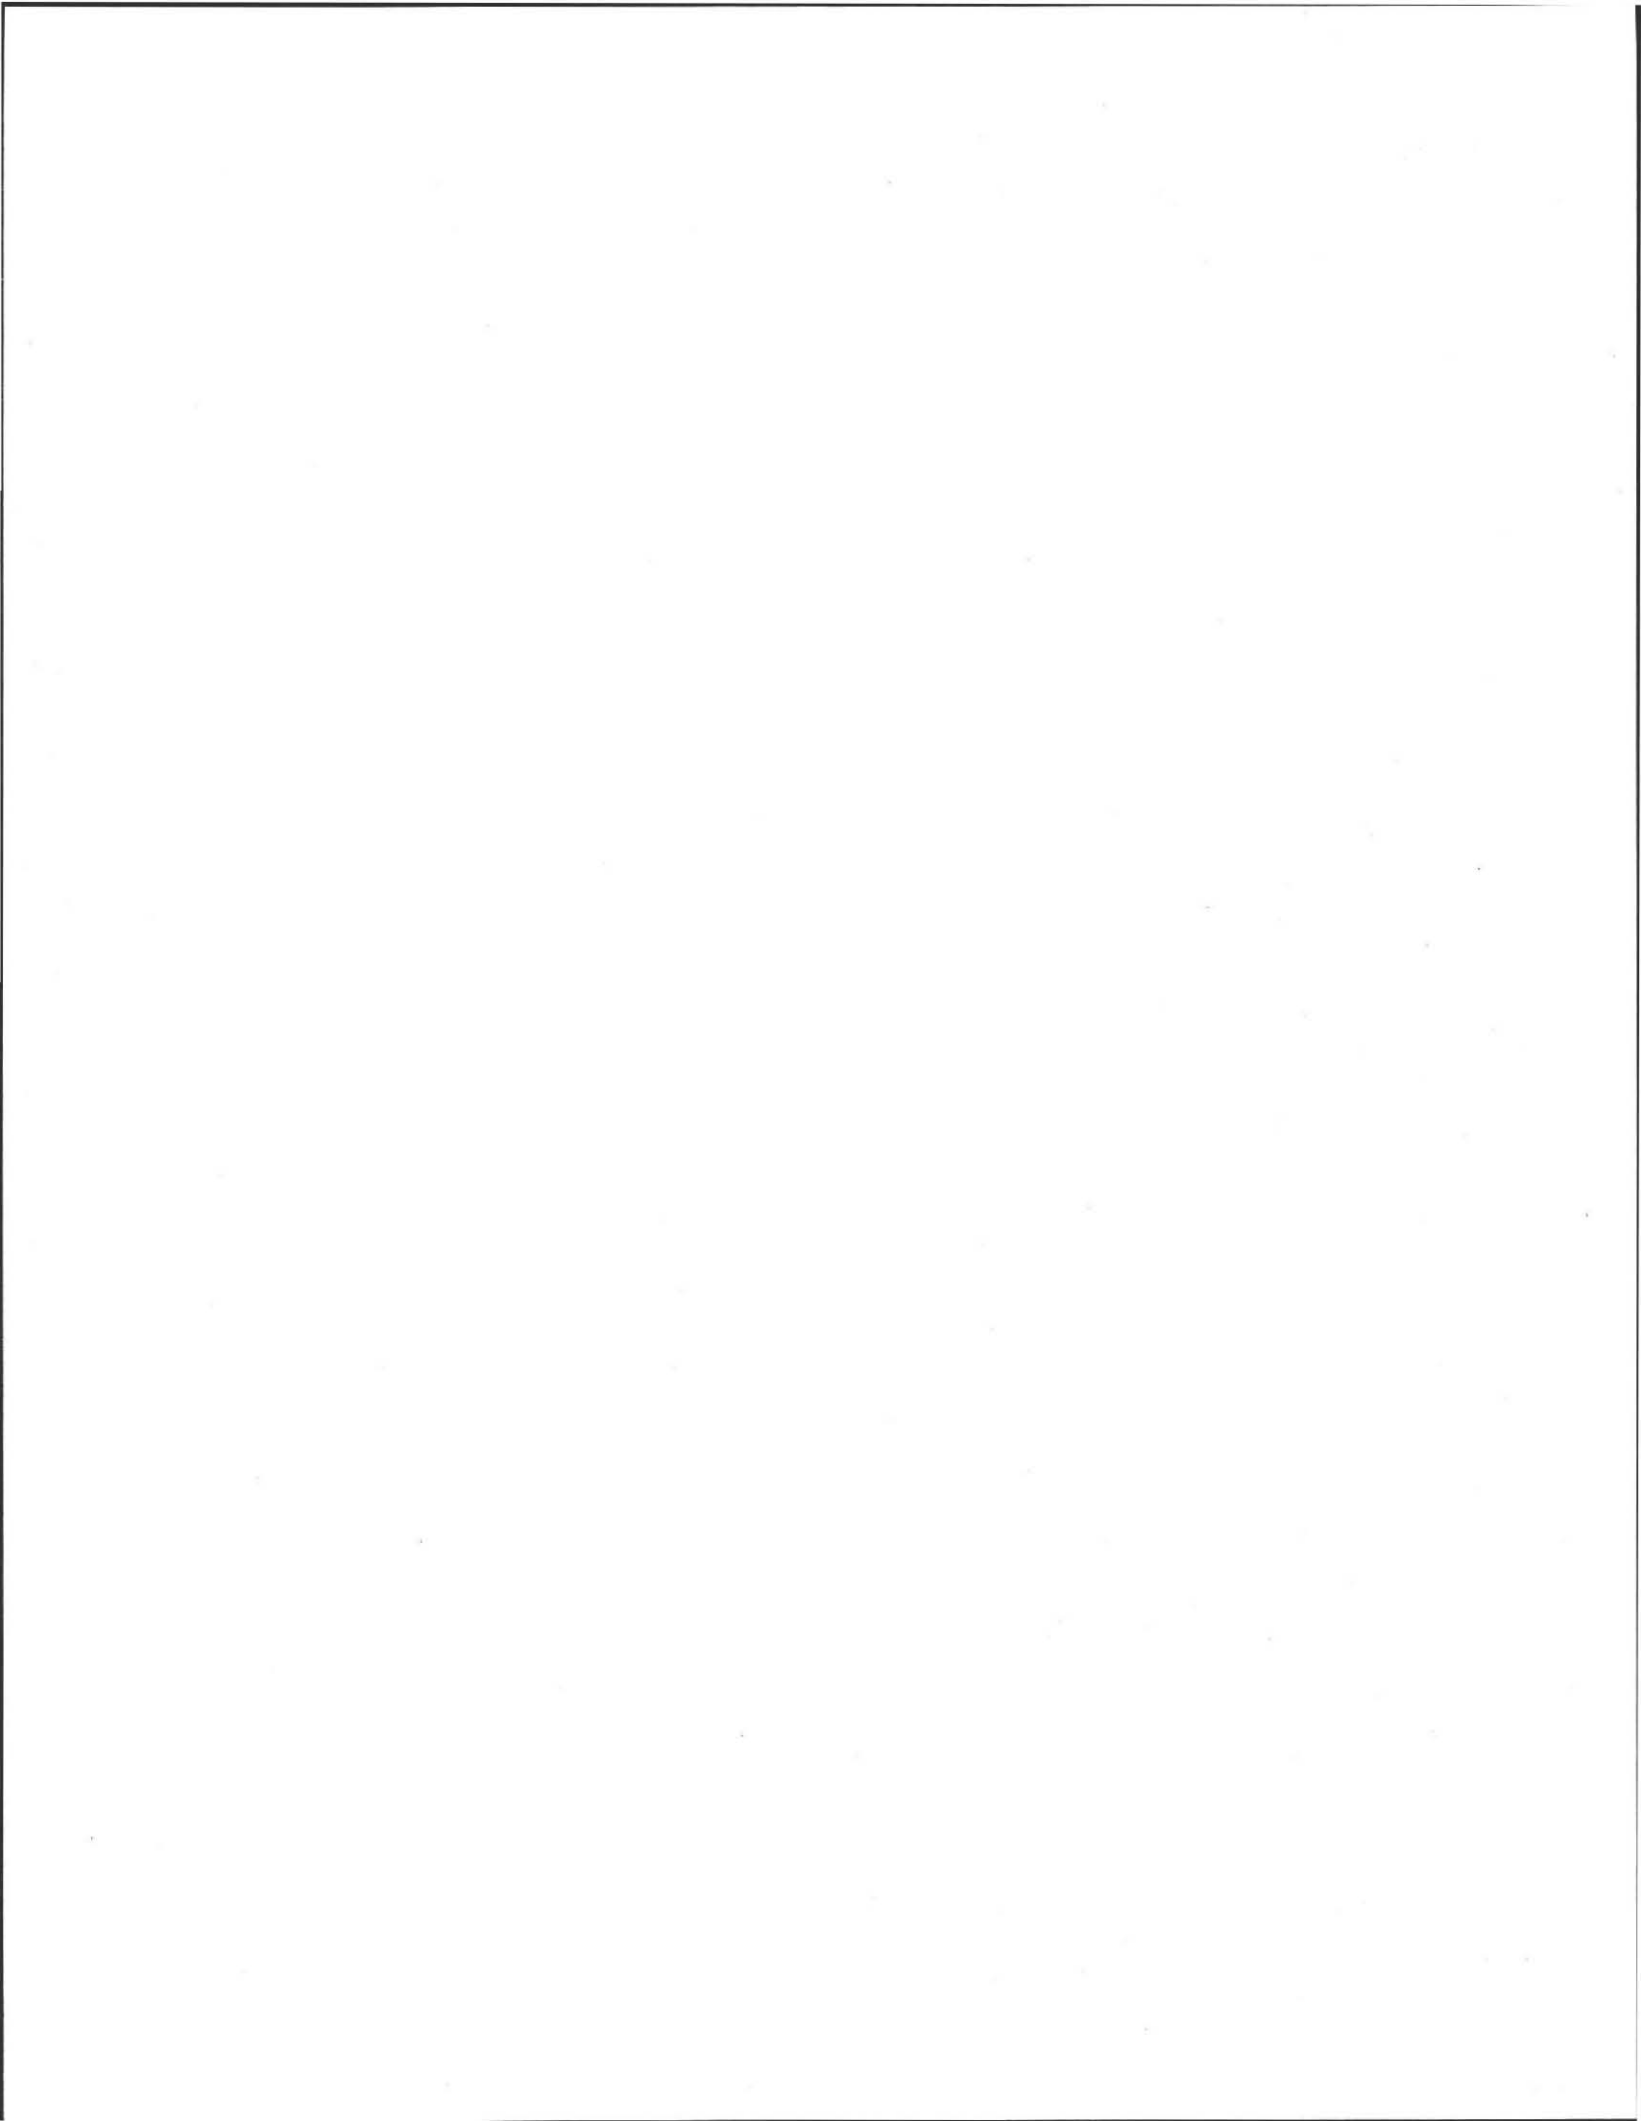

TITLE 5
OFFICIAL INSPECTION FOR - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM FORM
PART A
CERTIFICATION

Property Address: 751 Northeast Street, Amherst, MA
Owner's Name: Steve Founds C/O Jacqui Zuzgo
Owner's Address: 99 Main St Jones Town and Country Real Estate
Shelburne, MA 01370

COPY

Date of Inspection: December 02, 2003

Name of Inspector: Alan E. Weiss, R.S # 933
Company Name: Cold Spring Environmental Inc.
Mailing Address: 350 Old Enfield Road
Belchertown, Massachusetts 01007
Telephone Number: (413) 323-5957 fax: 413-323-4916

CERTIFICATION STATEMENT

I certify that I have personally inspected the sewage disposal system at this address and that the information reported below is true, accurate and complete as of the time of the inspection. The inspection was performed based on my training and experience in the proper function and maintenance of on site sewage disposal systems. I am a DEP approved system inspector pursuant to Section 15.340 of Title 5 (310 CMR 15.000). The system:

Passes
 Conditionally Passes
 Needs Further Evaluation by the Local Approving Authority
 Fails

Inspector's Signature:  Date: **December 02, 2003**


The system inspector shall submit a copy of this inspection report to the Approving Authority (Board of Health or DEP) within 30 days of completing this inspection. If the system is a shared system or has a design flow of 10,000 gpd or greater, the inspector and the system owner shall submit the report to the appropriate regional office of the DEP. The original should be sent to the system owner and copies sent to the buyer, if applicable, and the approving authority.

Notes and Comments:

Septic Tank was in good condition upon inspection. System appears to be functional All Stains, alarms & levels were ok at tank and chamber. SAS is 2+/- years old and had no standing liquid. Outlet & inlet baffles were in place. Tank was pumped. No evidence of failure (Pump tank every other year, or more).

******This report only describes conditions at the time of inspection and under the conditions of use at that time. This inspection does not address how the system will perform in the future under the same different conditions of use.**


10
FIC

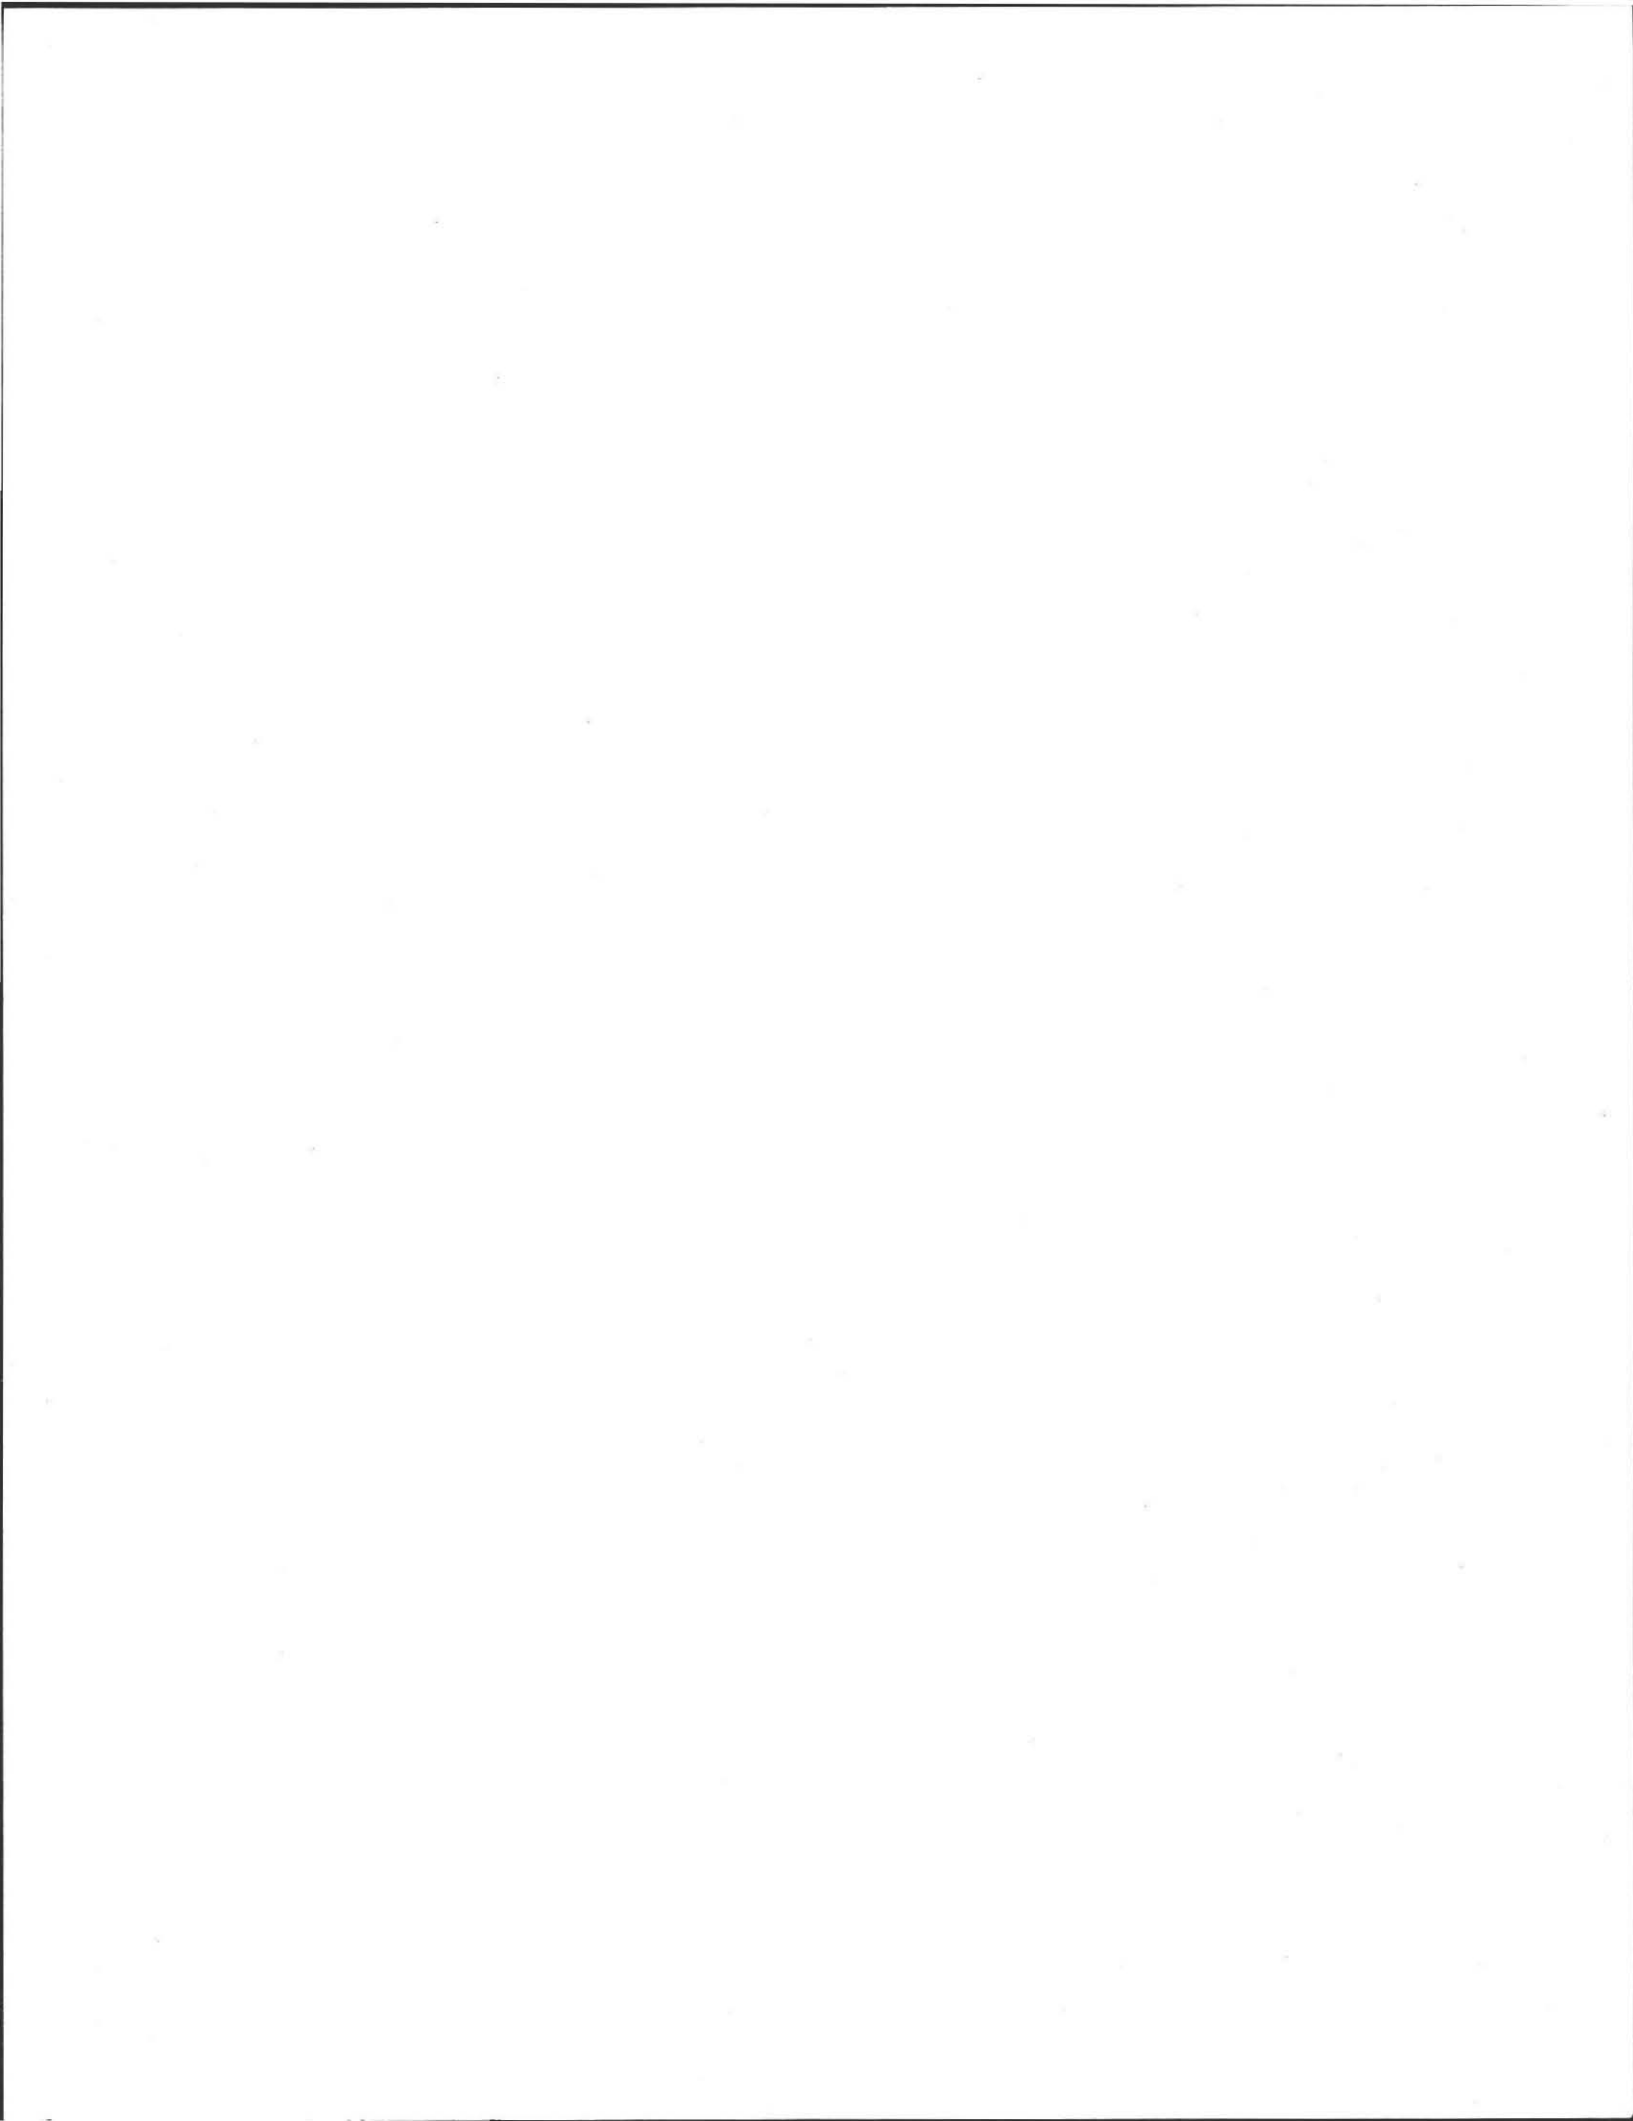

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART A
CERTIFICATION (continued)

Property Address: 751 NE ST

Owner: Found S

Date of Inspection: 12/2/03

Inspection Summary: Check A,B,C,D or E / ALWAYS complete all of Section D

A. System Passes:

yes I have not found any information which indicates that any of the failure criteria described in 310 CMR 15.303 or in 310 CMR 15.304 exist. Any failure criteria not evaluated are indicated below.

Comments:

B. System Conditionally Passes:

No One or more system components as described in the "Conditional Pass" section need to be replaced or repaired. The system, upon completion of the replacement or repair, as approved by the Board of Health, will pass.

Answer yes, no or not determined (Y,N,ND) in the ____ for the following statements. If "not determined" please explain.

____ The septic tank is metal and over 20 years old* or the septic tank (whether metal or not) is structurally unsound, exhibits substantial infiltration or exfiltration or tank failure is imminent. System will pass inspection if the existing tank is replaced with a complying septic tank as approved by the Board of Health.

*A metal septic tank will pass inspection if it is structurally sound, not leaking and if a Certificate of Compliance indicating that the tank is less than 20 years old is available.

ND explain:

____ Observation of sewage backup or break out or high static water level in the distribution box due to broken or obstructed pipe(s) or due to a broken, settled or uneven distribution box. System will pass inspection if (with approval of Board of Health):


- ____ broken pipe(s) are replaced
- ____ obstruction is removed
- ____ distribution box is leveled or replaced

ND explain:

____ The system required pumping more than 4 times a year due to broken or obstructed pipe(s). The system will pass inspection if (with approval of the Board of Health):

- ____ broken pipe(s) are replaced
- ____ obstruction is removed

ND explain:

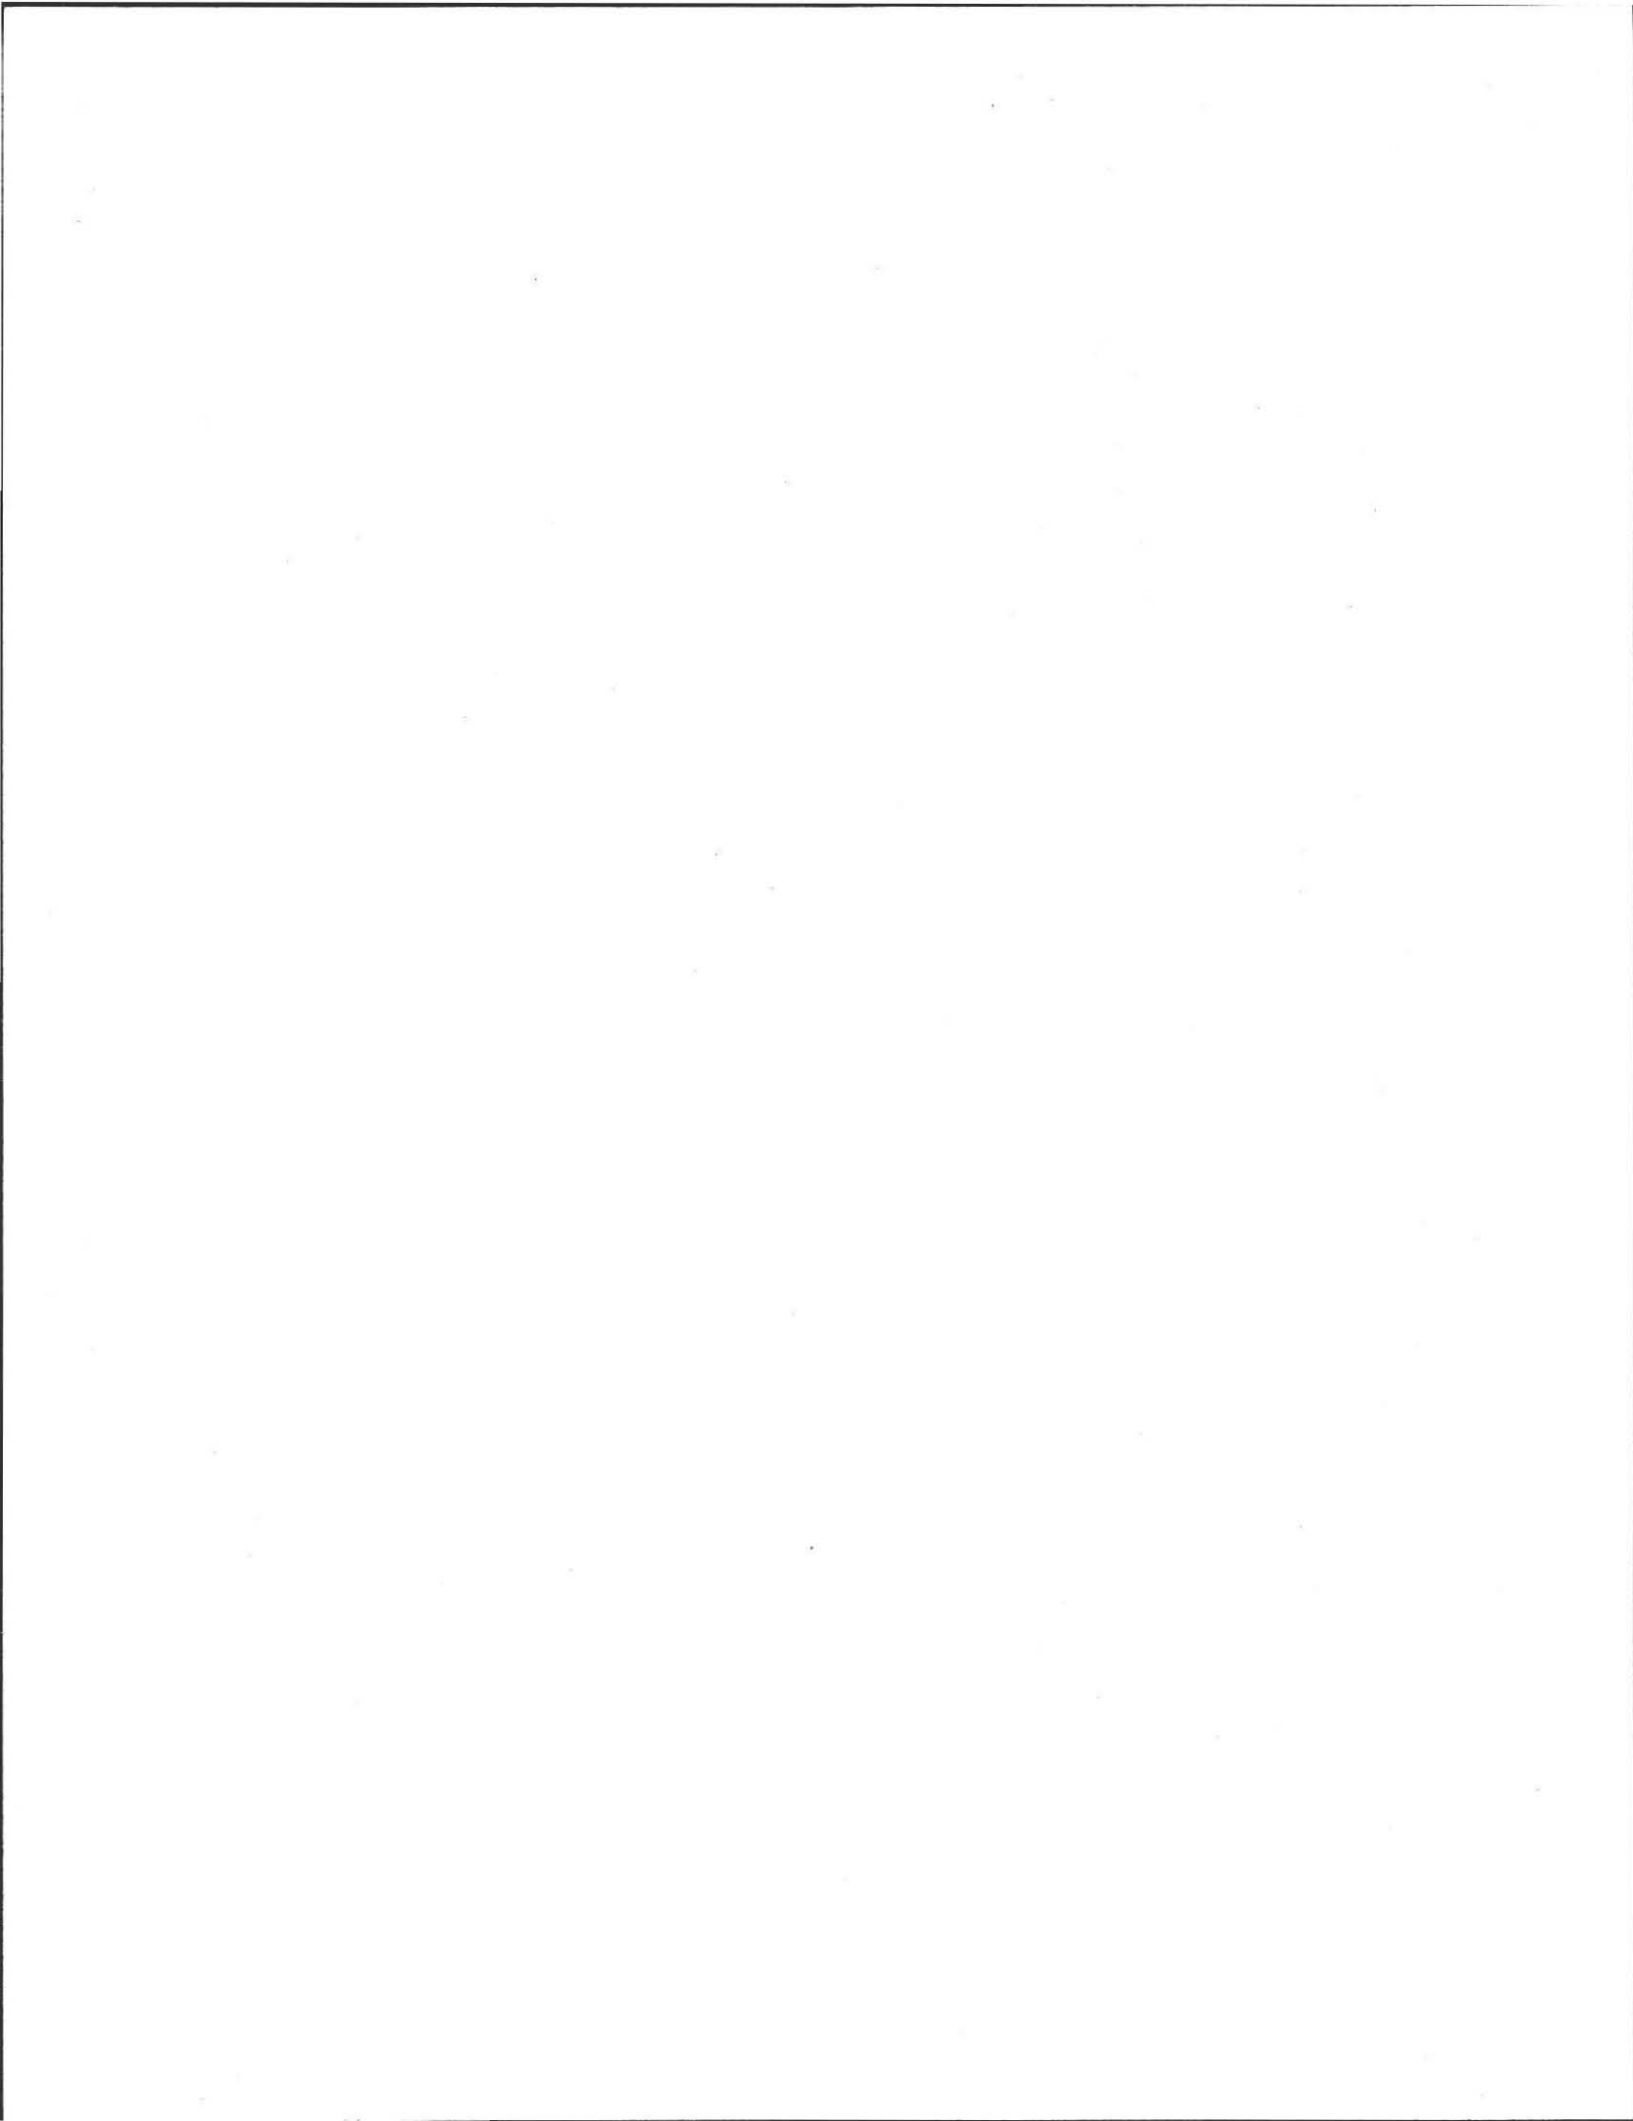

**OFFICIAL INSPECTION FORM - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART A
CERTIFICATION (continued)**

Property Address: 751 NE 51

Owner: FRANDS

Date of Inspection: 12/7/03

C. Further Evaluation is Required by the Board of Health:

No Conditions exist which require further evaluation by the Board of Health in order to determine if the system is failing to protect public health, safety or the environment.

1. System will pass unless Board of Health determines in accordance with 310 CMR 15.303(1)(b) that the system is not functioning in a manner which will protect public health, safety and the environment:


- Cesspool or privy is within 50 feet of a surface water
- Cesspool or privy is within 50 feet of a bordering vegetated wetland or a salt marsh

2. System will fail unless the Board of Health (and Public Water Supplier, if any) determines that the system is functioning in a manner that protects the public health, safety and environment:

- The system has a septic tank and soil absorption system (SAS) and the SAS is within 100 feet of a surface water supply or tributary to a surface water supply.
- The system has a septic tank and SAS and the SAS is within a Zone 1 of a public water supply.
- The system has a septic tank and SAS and the SAS is within 50 feet of a private water supply well.
- The system has a septic tank and SAS and the SAS is less than 100 feet but 50 feet or more from a private water supply well**. Method used to determine distance _____

**This system passes if the well water analysis, performed at a DEP certified laboratory, for coliform bacteria and volatile organic compounds indicates that the well is free from pollution from that facility and the presence of ammonia nitrogen and nitrate nitrogen is equal to or less than 5 ppm, provided that no other failure criteria are triggered. A copy of the analysis must be attached to this form.

3. Other:

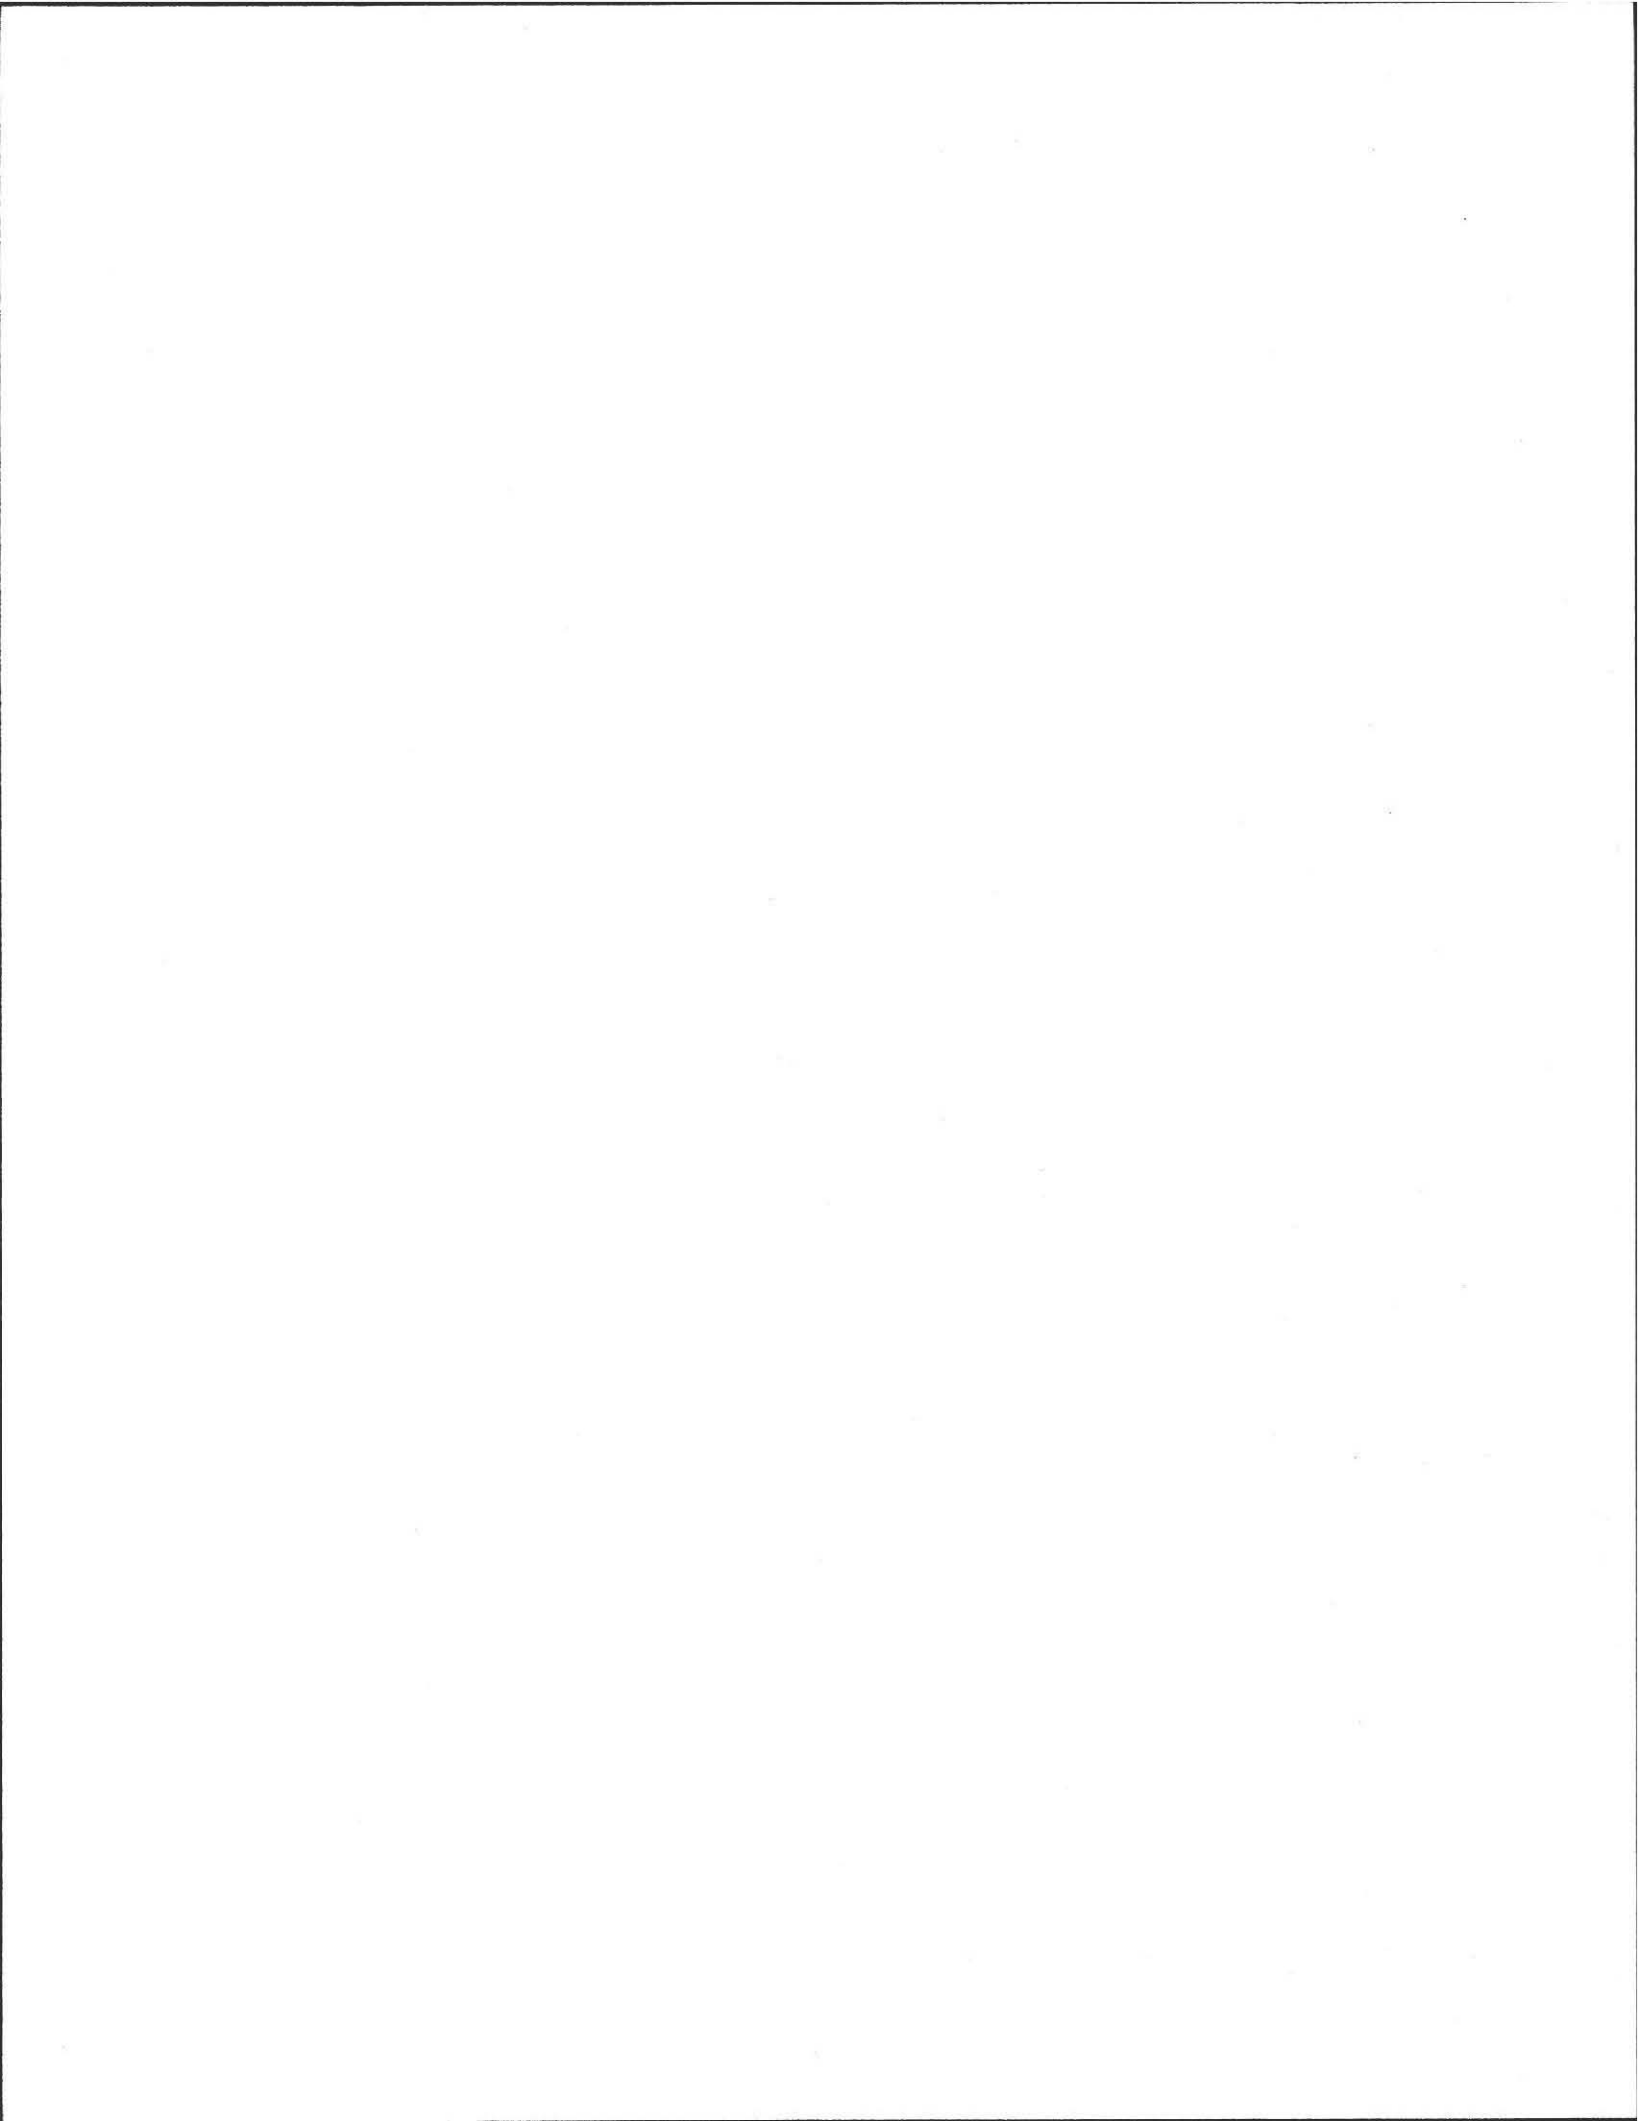

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART A
CERTIFICATION (continued)

Property Address: 751 NE ST.

Owner: Fonds

Date of Inspection: 12/26/03

D. System Failure Criteria applicable to all systems:

You **must** indicate "yes" or "no" to each of the following for **all** inspections:

- | | | |
|--------------------------|-------------------------------------|---|
| Yes | No | |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Backup of sewage into facility or system component due to overloaded or clogged SAS or cesspool |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Discharge or ponding of effluent to the surface of the ground or surface waters due to an overloaded or clogged SAS or cesspool |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Static liquid level in the distribution box above outlet invert due to an overloaded or clogged SAS or cesspool |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Liquid depth in cesspool is less than 6" below invert or available volume is less than 1/2 day flow |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Required pumping more than 4 times in the last year NOT due to clogged or obstructed pipe(s). Number of times pumped <u> </u> |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Any portion of the SAS, cesspool or privy is below high ground water elevation. |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Any portion of cesspool or privy is within 100 feet of a surface water supply or tributary to a surface water supply. |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Any portion of a cesspool or privy is within a Zone 1 of a public well. |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Any portion of a cesspool or privy is within 50 feet of a private water supply well. |
| <input type="checkbox"/> | <input checked="" type="checkbox"/> | Any portion of a cesspool or privy is less than 100 feet but greater than 50 feet from a private water supply well with no acceptable water quality analysis. [This system passes if the well water analysis, performed at a DEP certified laboratory, for coliform bacteria and volatile organic compounds indicates that the well is free from pollution from that facility and the presence of ammonia nitrogen and nitrate nitrogen is equal to or less than 5 ppm, provided that no other failure criteria are triggered. A copy of the analysis must be attached to this form.] |

No (Yes/No) The system **fails**. I have determined that one or more of the above failure criteria exist as described in 310 CMR 15.303, therefore the system fails. The system owner should contact the Board of Health to determine what will be necessary to correct the failure.

E. Large Systems:


To be considered a large system the system must serve a facility with a design flow of 10,000 gpd to 15,000 gpd.

You must indicate either "yes" or "no" to each of the following:

(The following criteria apply to large systems in addition to the criteria above)

- | | | |
|--------------------------|--------------------------|--|
| yes | no | |
| <input type="checkbox"/> | <input type="checkbox"/> | the system is within 400 feet of a surface drinking water supply |
| <input type="checkbox"/> | <input type="checkbox"/> | the system is within 200 feet of a tributary to a surface drinking water supply |
| <input type="checkbox"/> | <input type="checkbox"/> | the system is located in a nitrogen sensitive area (Interim Wellhead Protection Area – IWPA) or a mapped Zone II of a public water supply well |

If you have answered "yes" to any question in Section E the system is considered a significant threat, or answered "yes" in Section D above the large system has failed. The owner or operator of any large system considered a significant threat under Section E or failed under Section D shall upgrade the system in accordance with 310 CMR 15.304. The system owner should contact the appropriate regional office of the Department.

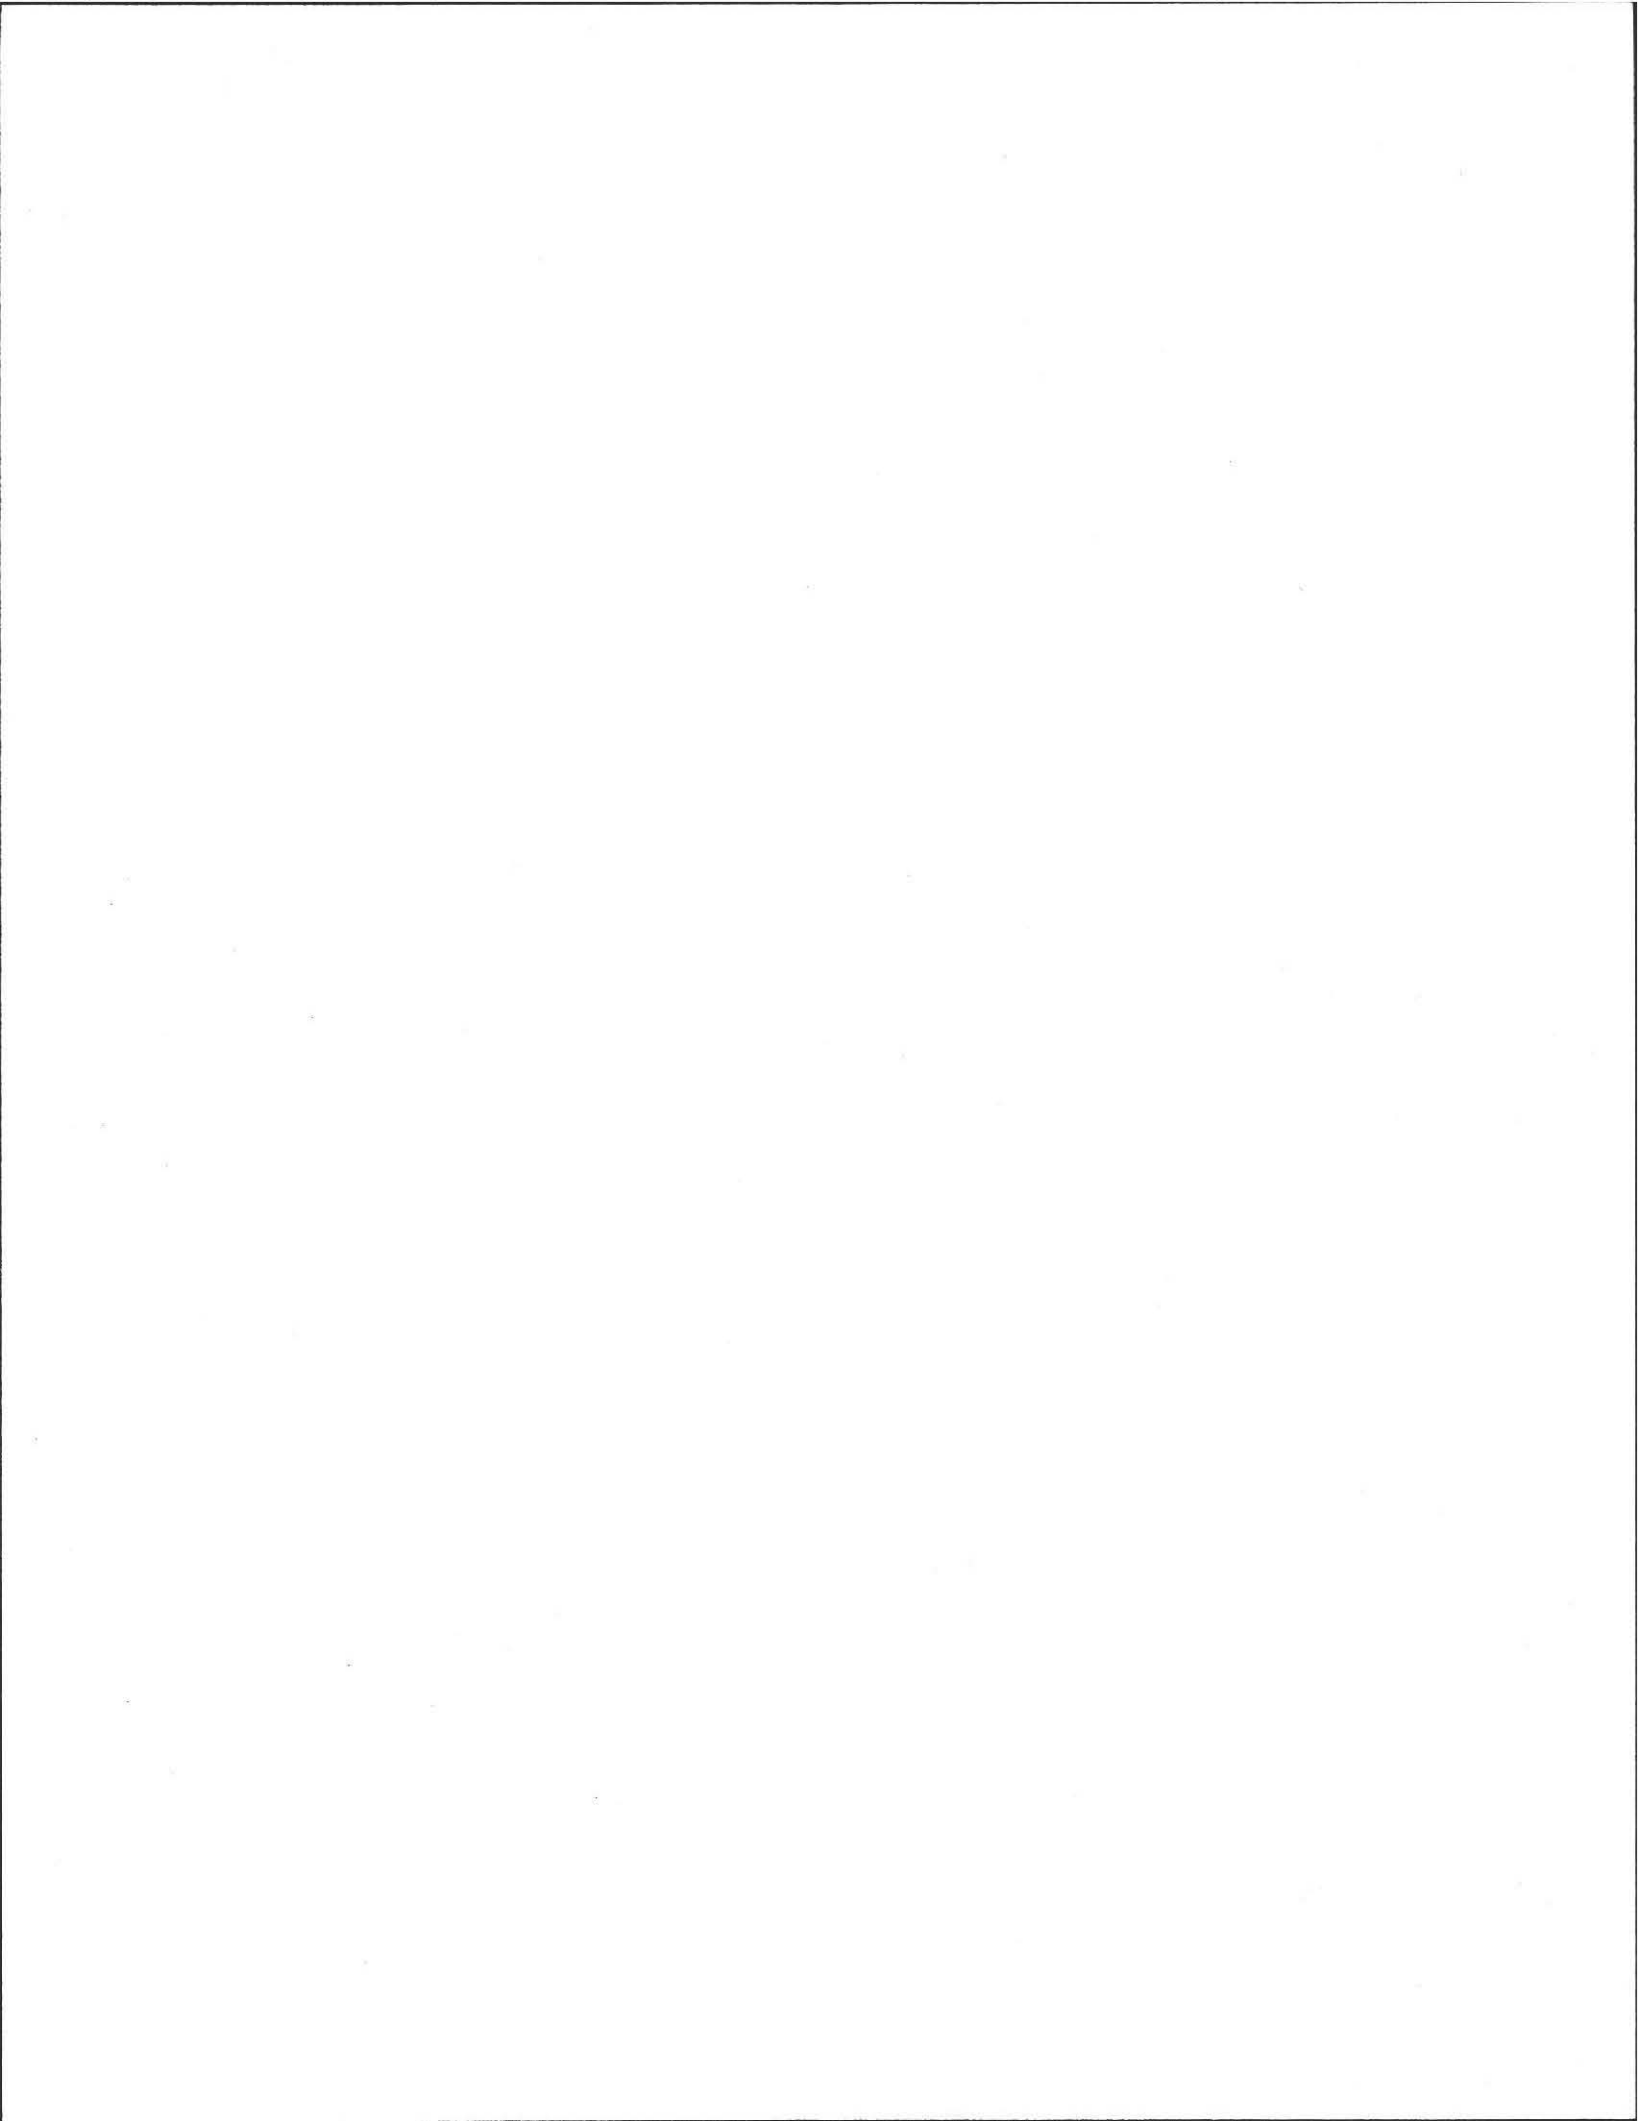

**OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART B
CHECKLIST**

Property Address: 751 NE ST.

Owner: FARDS


Date of Inspection: 12/2/03

Check if the following have been done. You must indicate "yes" or "no" as to each of the following:

- Yes No
- yes Pumping information was provided by the owner, occupant, or Board of Health
- No Were any of the system components pumped out in the previous two weeks ?
- No Has the system received normal flows in the previous two week period ? (OCTOBER)
- No Have large volumes of water been introduced to the system recently or as part of this inspection ?
- yes Were as built plans of the system obtained and examined? (If they were not available note as N/A)
- yes Was the facility or dwelling inspected for signs of sewage back up ?
- yes Was the site inspected for signs of break out ?
- yes Were all system components, excluding the SAS, located on site ?
- yes Were the septic tank manholes uncovered, opened, and the interior of the tank inspected for the condition of the baffles or tees, material of construction, dimensions, depth of liquid, depth of sludge and depth of scum ?
- yes Was the facility owner (and occupants if different from owner) provided with information on the proper maintenance of subsurface sewage disposal systems ?

The size and location of the Soil Absorption System (SAS) on the site has been determined based on:

- Yes no
- yes Existing information. For example, a plan at the Board of Health.
- yes Determined in the field (if any of the failure criteria related to Part C is at issue approximation of distance is unacceptable) [310 CMR 15.302(3)(b)]

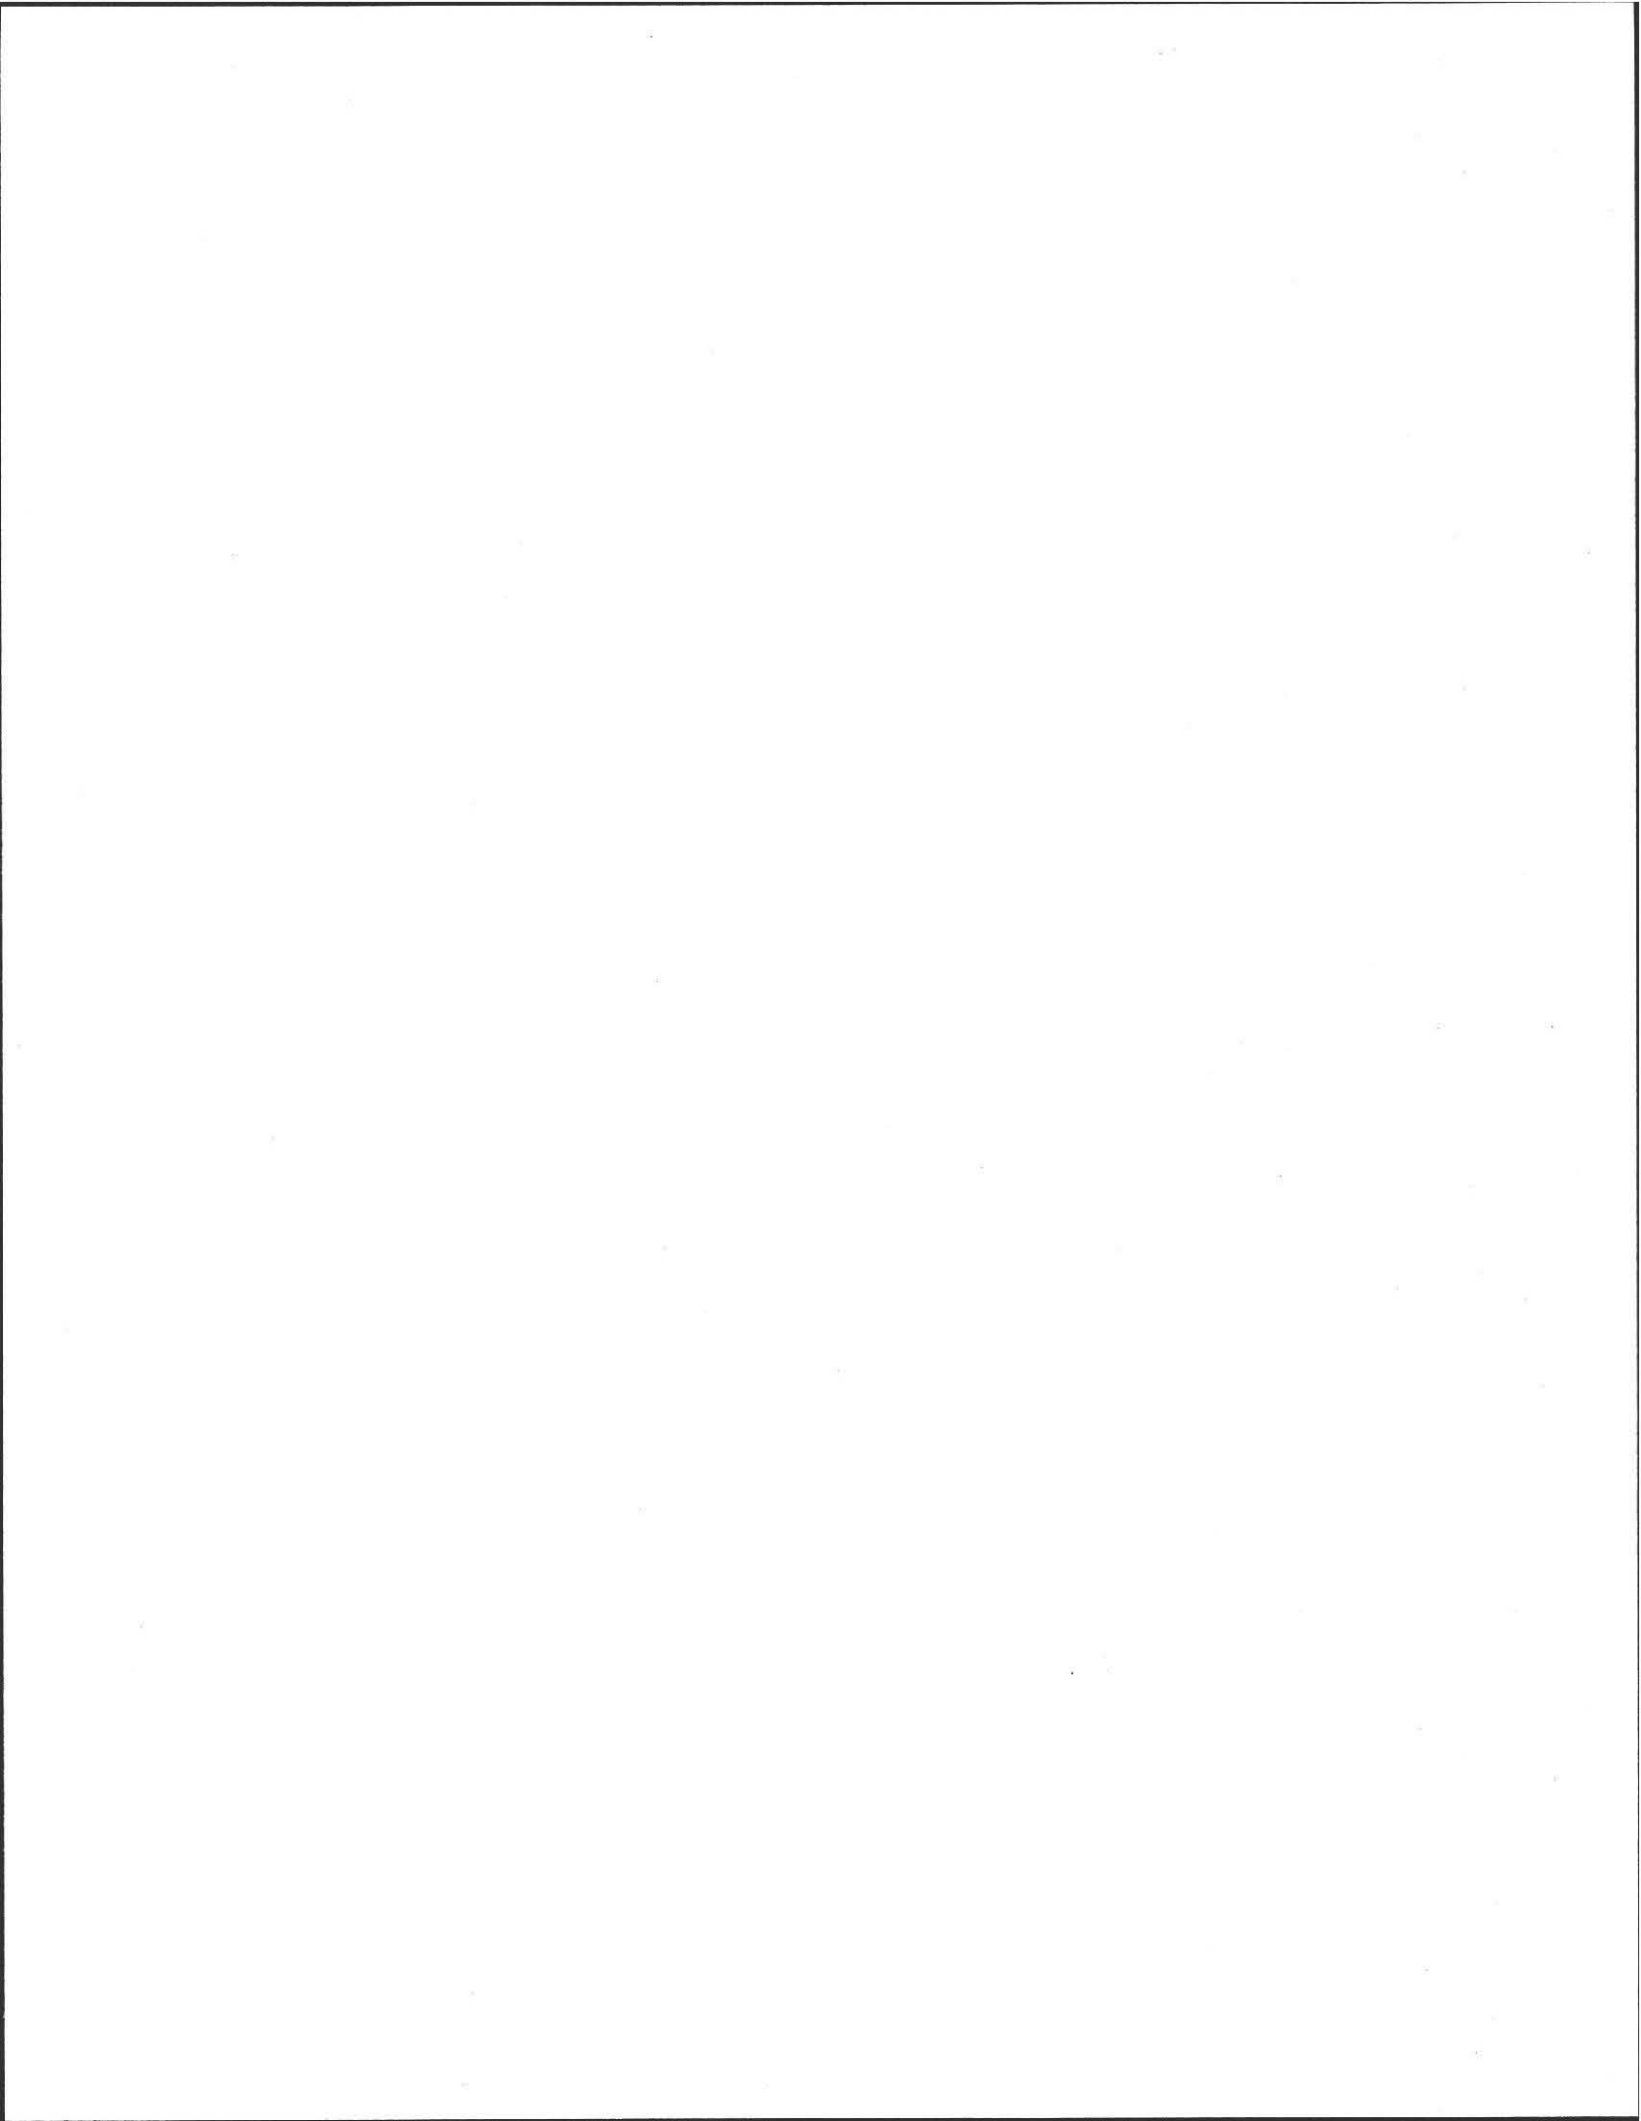

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION

Property Address: 751 NE ST.

Owner: Foungis

Date of Inspection: 12/2/03

FLOW CONDITIONS

RESIDENTIAL

Number of bedrooms (design): 7 Number of bedrooms (actual): 7

DESIGN flow based on 310 CMR 15.203 (for example: 110 gpd x # of bedrooms): 770

Number of current residents: 0 (4 in October)

Does residence have a garbage grinder (yes or no): no

Is laundry on a separate sewage system (yes or no) no [if yes separate inspection required]

Laundry system inspected (yes or no): no

Seasonal use: (yes or no): No

Water meter readings, if available (last 2 years usage (gpd)): N/A.

Sump pump (yes or no): No

Last date of occupancy: Oct. 03

COMMERCIAL/INDUSTRIAL

Type of establishment: N/A

Design flow (based on 310 CMR 15.203): _____ gpd

Basis of design flow (seats/persons/sqft, etc.): _____

Grease trap present (yes or no): _____

Industrial waste holding tank present (yes or no): _____

Non-sanitary waste discharged to the Title 5 system (yes or no): _____

Water meter readings, if available: _____

Last date of occupancy/use: _____

OTHER (describe): _____

GENERAL INFORMATION

Pumping Records

Source of information: _____

Was system pumped as part of the inspection (yes or no): _____

If yes, volume pumped: 1000 gallons -- How was quantity pumped determined? _____

Reason for pumping: _____

TYPE OF SYSTEM

Septic tank, distribution box, soil absorption system

Single cesspool

Overflow cesspool

Privy

Shared system (yes or no) (if yes, attach previous inspection records, if any)

Innovative/Alternative technology. Attach a copy of the current operation and maintenance contract (to be obtained from system owner)


Tight tank Attach a copy of the DEP approval

Other (describe): _____

Approximate age of all components, date installed (if known) and source of information:

2001.

Were sewage odors detected when arriving at the site (yes or no): No

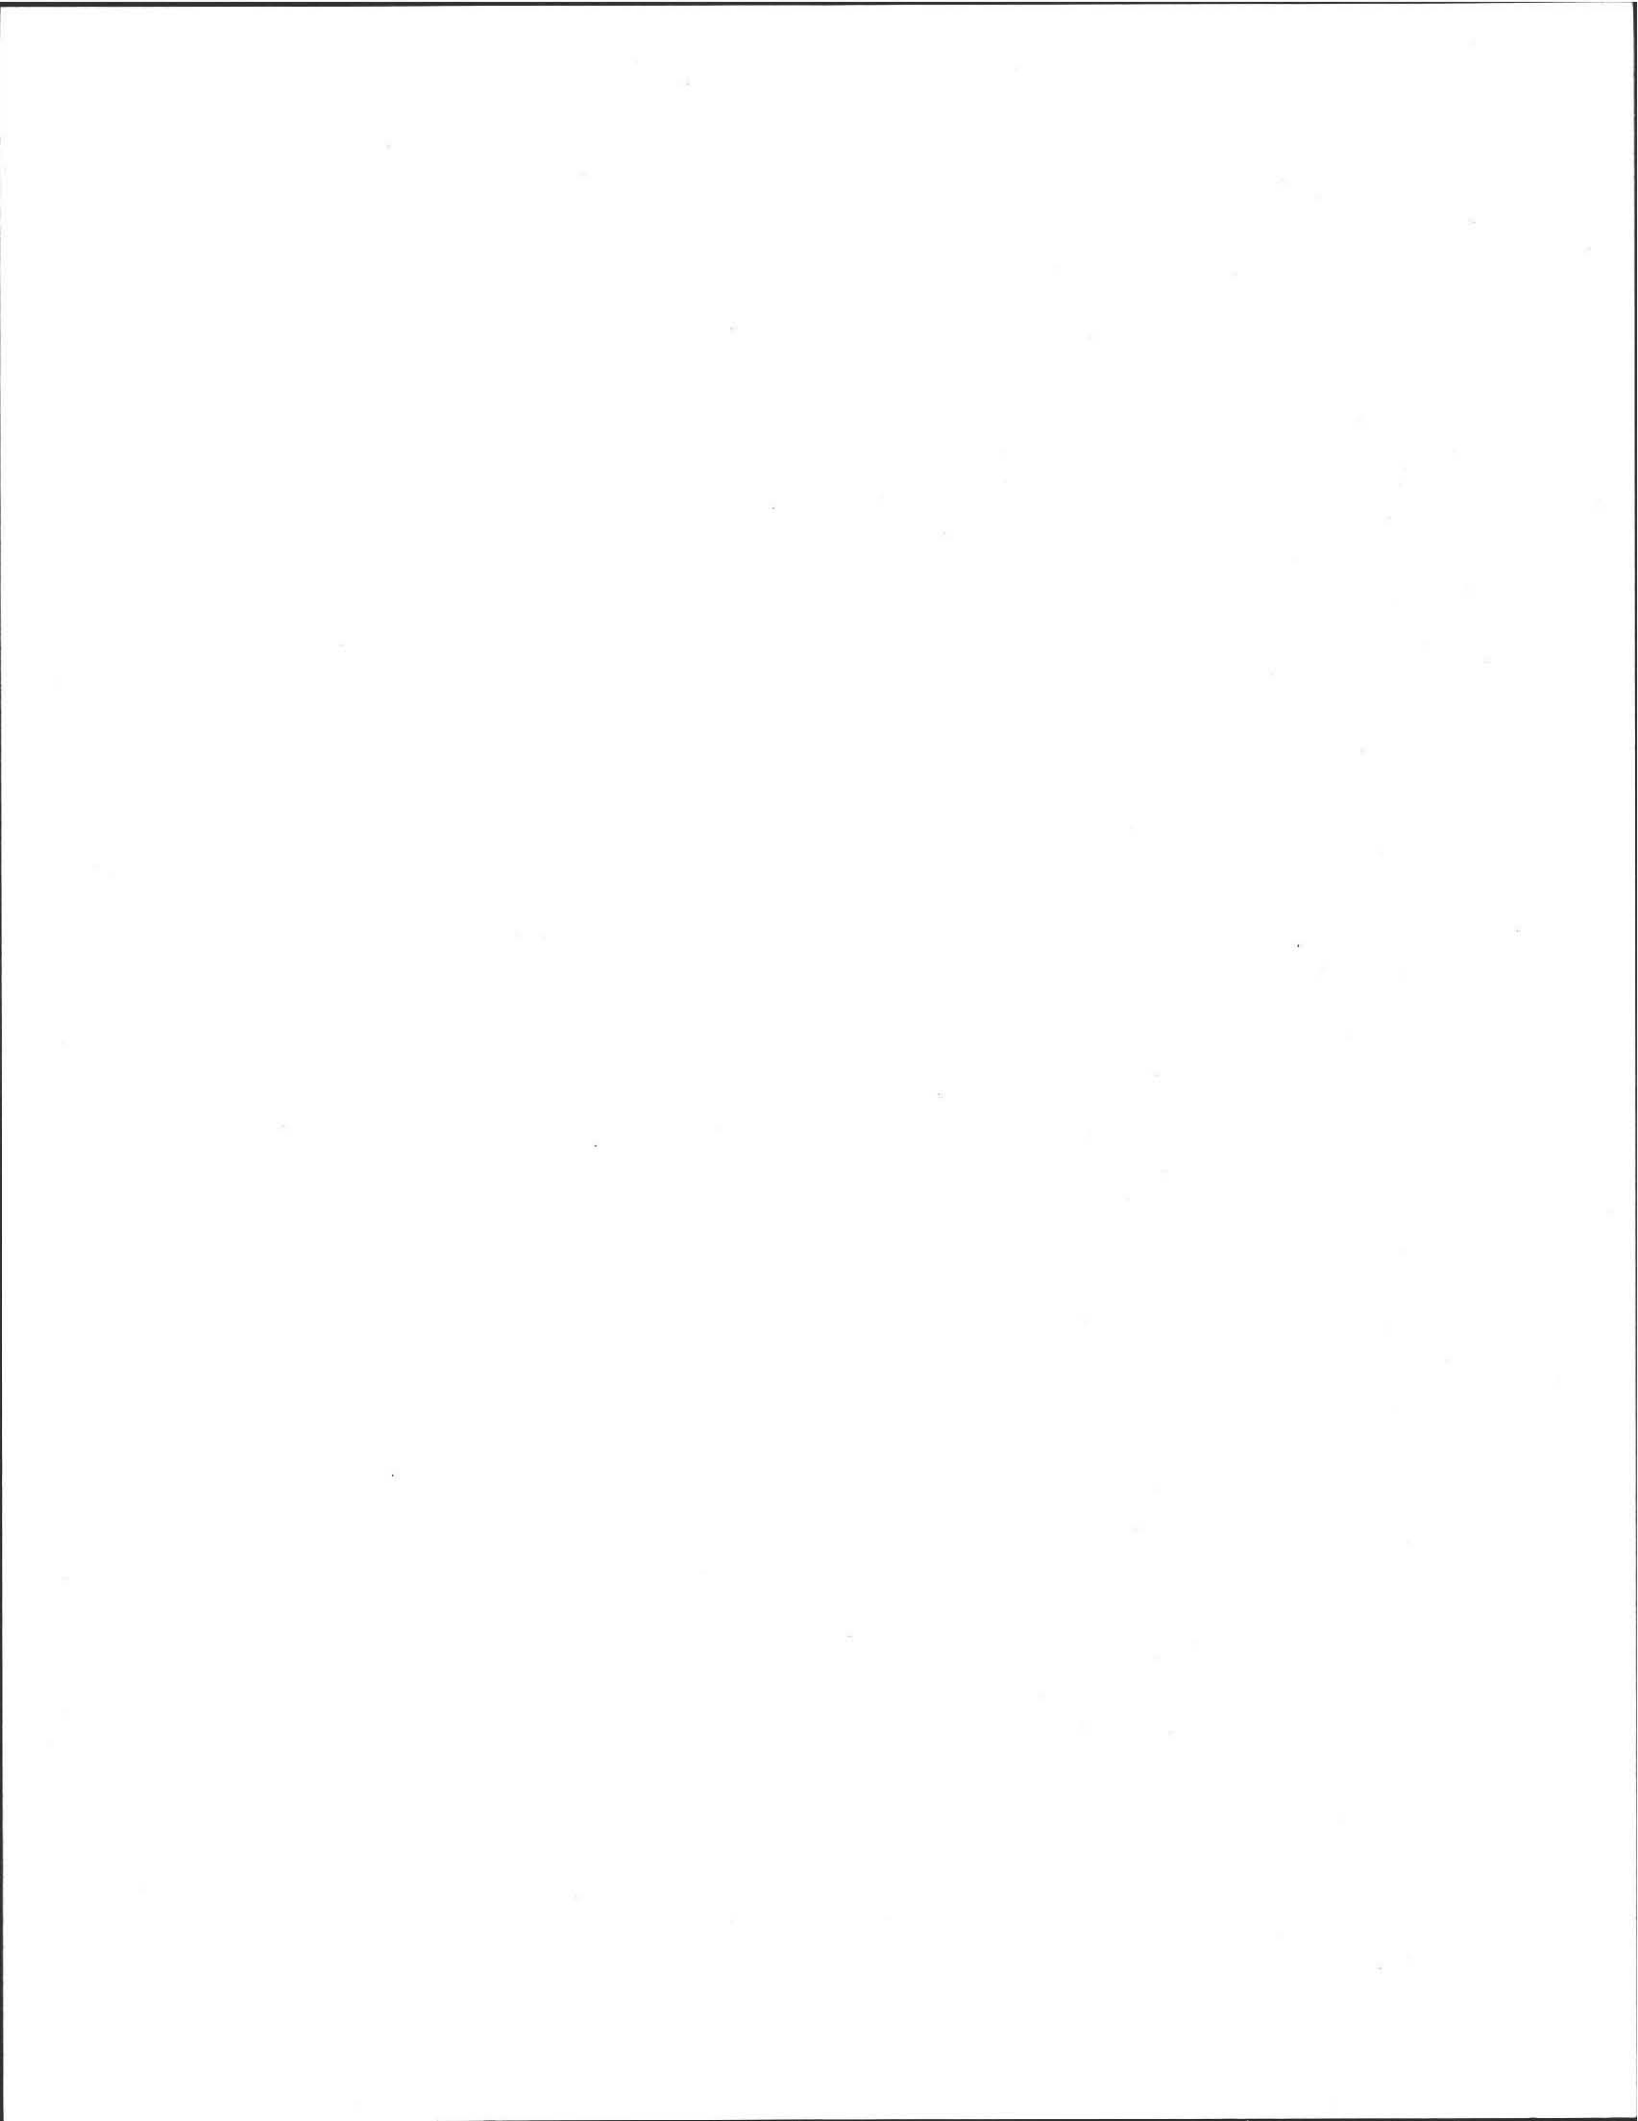

OFFICIAL INSPECTION FORM - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION (continued)

Property Address: 751 NE ST
Owner: FOUNDS
Date of Inspection: 12/2/03

BUILDING SEWER (locate on site plan)


Depth below grade: 14"
Materials of construction: cast iron 40 PVC other (explain): _____
Distance from private water supply well or suction line: 10' +
Comments (on condition of joints, venting, evidence of leakage, etc.):
OK

SEPTIC TANK: 45' (locate on site plan)

Depth below grade: 20'
Material of construction: concrete metal fiberglass polyethylene
 other (explain) _____
If tank is metal list age: ___ Is age confirmed by a Certificate of Compliance (yes or no): ___ (attach a copy of certificate)
Dimensions: 8.5' x 4.5' x 4.5'
Sludge depth: 3"
Distance from top of sludge to bottom of outlet tee or baffle: 40"
Scum thickness: 1"
Distance from top of scum to top of outlet tee or baffle: 6"
Distance from bottom of scum to bottom of outlet tee or baffle: 10"
How were dimensions determined: MEAS.
Comments (on pumping recommendations, inlet and outlet tee or baffle condition, structural integrity, liquid levels as related to outlet invert, evidence of leakage, etc.):
BUILT-IN - BAFFLES. OK.

GREASE TRAP: N/A (locate on site plan)

Depth below grade: _____
Material of construction: concrete metal fiberglass polyethylene other (explain): _____
Dimensions: _____
Scum thickness: _____
Distance from top of scum to top of outlet tee or baffle: _____
Distance from bottom of scum to bottom of outlet tee or baffle: _____
Date of last pumping: _____
Comments (on pumping recommendations, inlet and outlet tee or baffle condition, structural integrity, liquid levels as related to outlet invert, evidence of leakage, etc.):

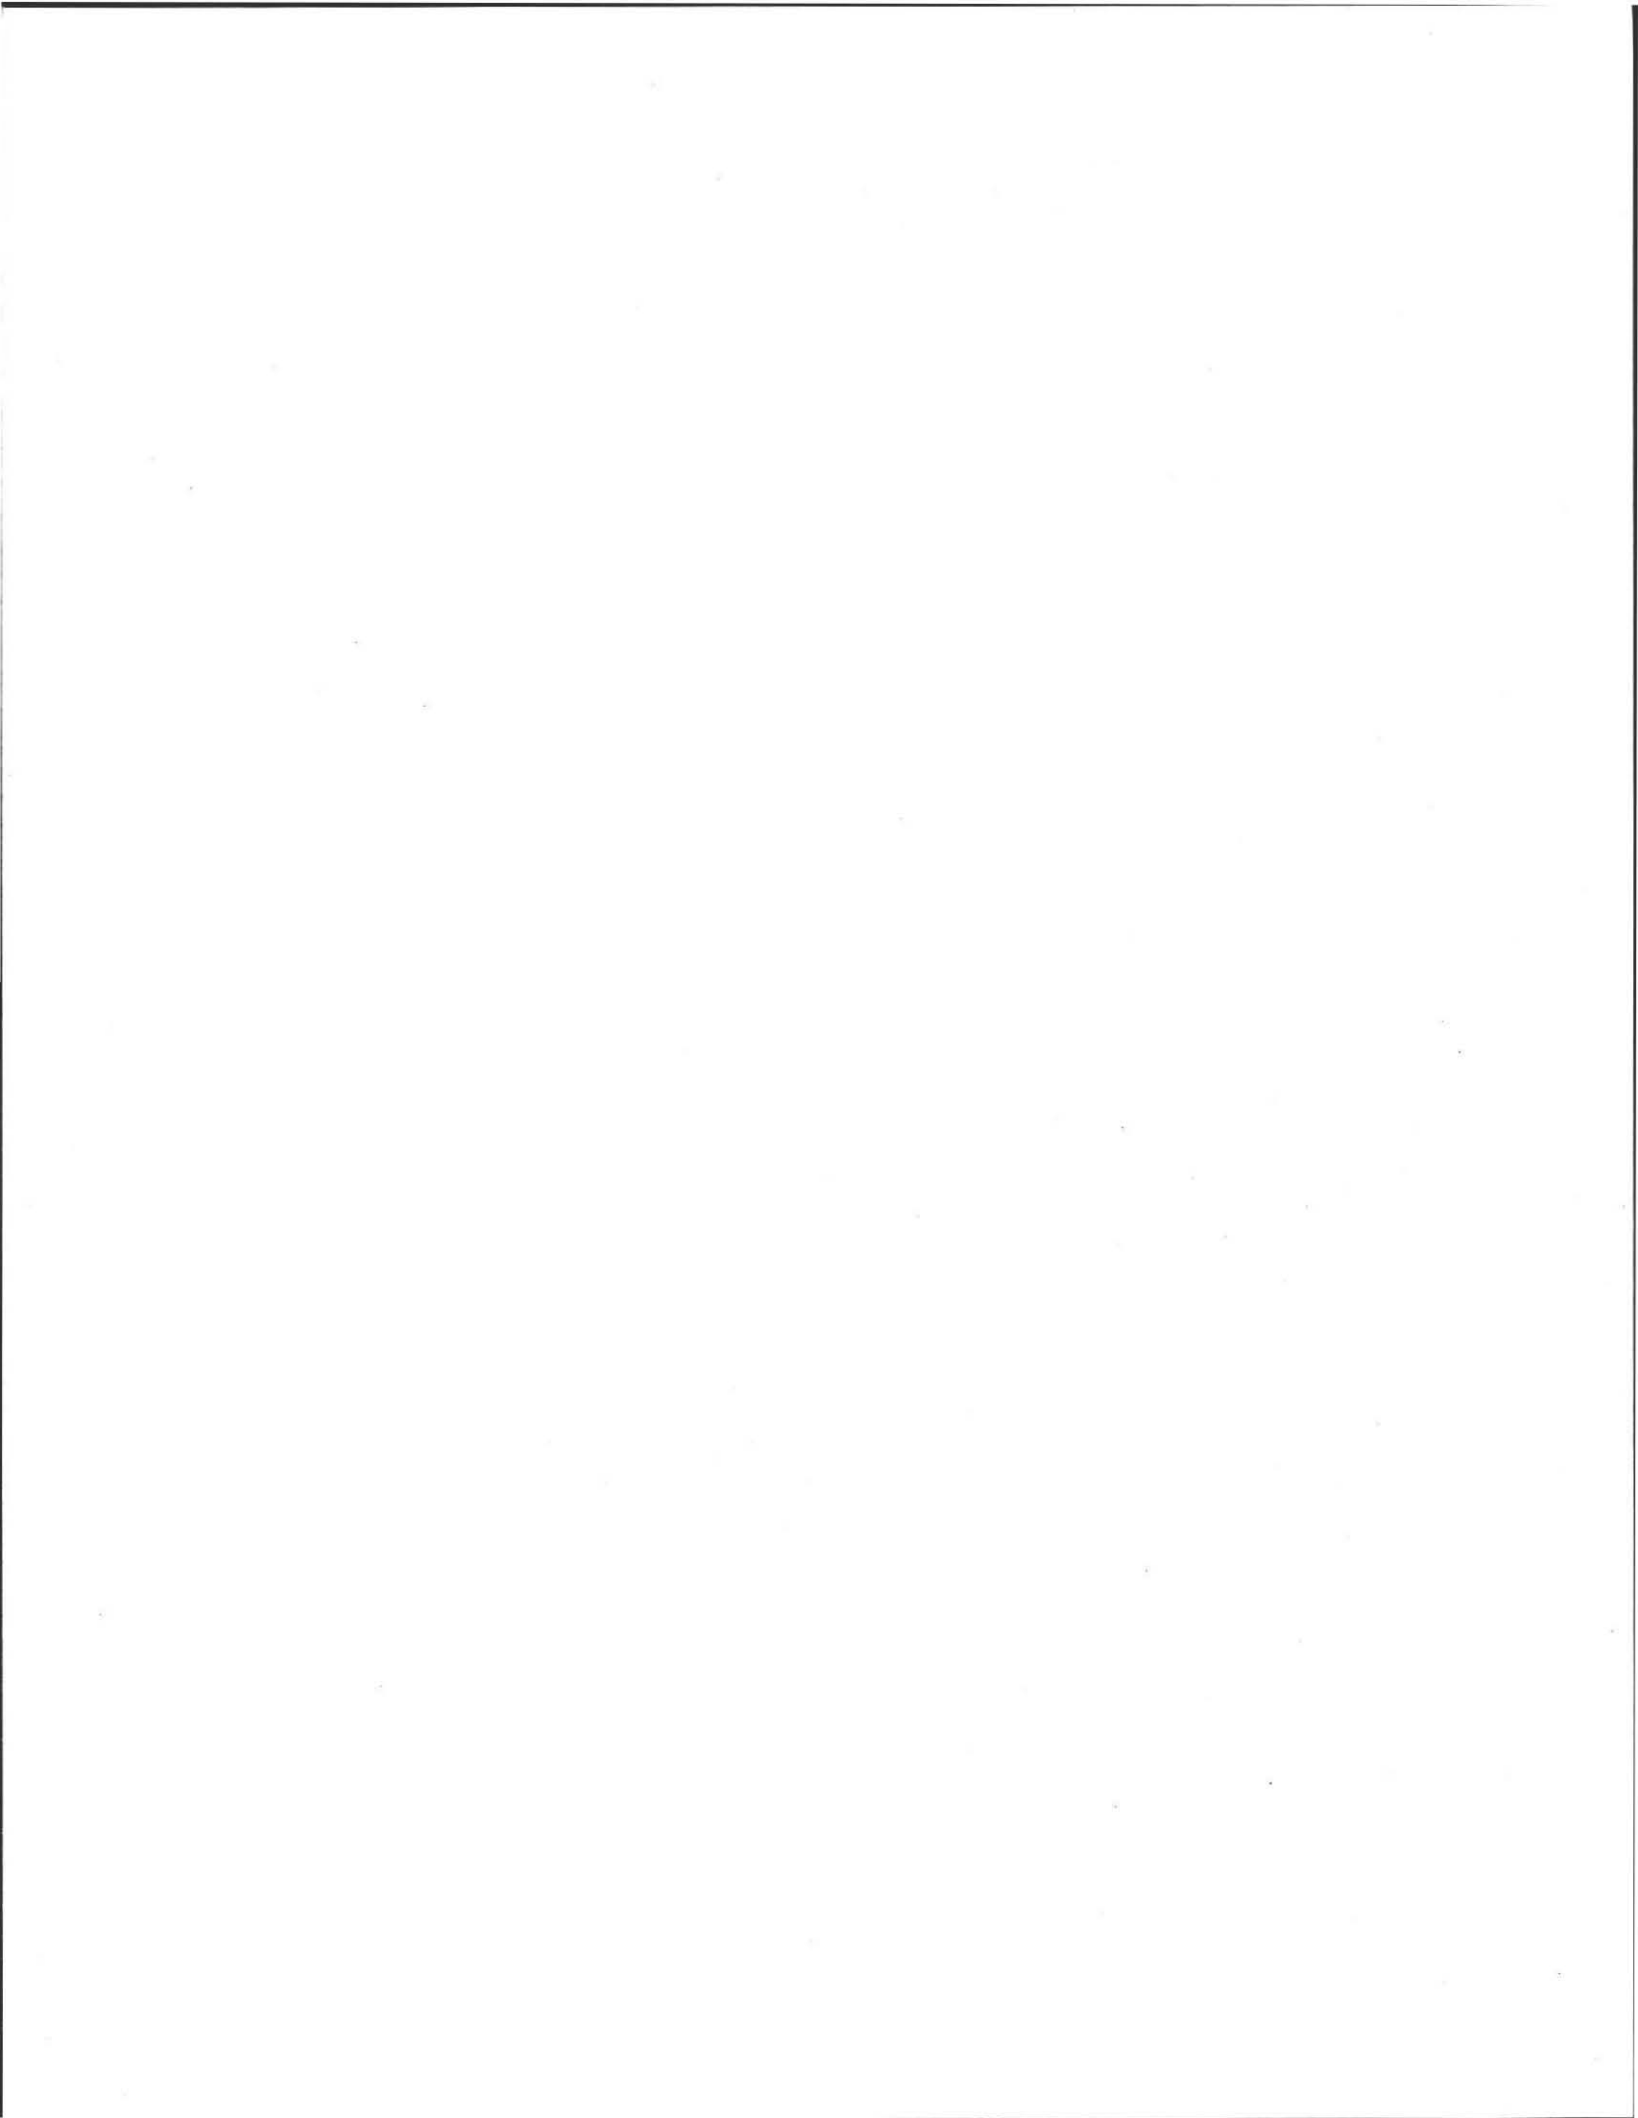

OFFICIAL INSPECTION FORM - NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION (continued)

Property Address: 751 NE ST.

Owner: Fonds.

Date of Inspection: 12/2/03

TIGHT or HOLDING TANK: No (tank must be pumped at time of inspection)(locate on site plan)

Depth below grade: _____

Material of construction: _____ concrete _____ metal _____ fiberglass _____ polyethylene _____ other(explain): _____

Dimensions: _____

Capacity: _____ gallons

Design Flow: _____ gallons/day

Alarm present (yes or no): _____

Alarm level: _____ Alarm in working order (yes or no): _____

Date of last pumping: _____

Comments (condition of alarm and float switches, etc.): _____

DISTRIBUTION BOX: yes (if present must be opened)(locate on site plan)

Depth of liquid level above outlet invert: 0.100


Comments (note if box is level and distribution to outlets equal, any evidence of solids carryover, any evidence of leakage into or out of box, etc.):
Good condition

PUMP CHAMBER: yes (locate on site plan)

Pumps in working order (yes or no): yes

Alarms in working order (yes or no): yes

Comments (note condition of pump chamber, condition of pumps and appurtenances, etc.): _____

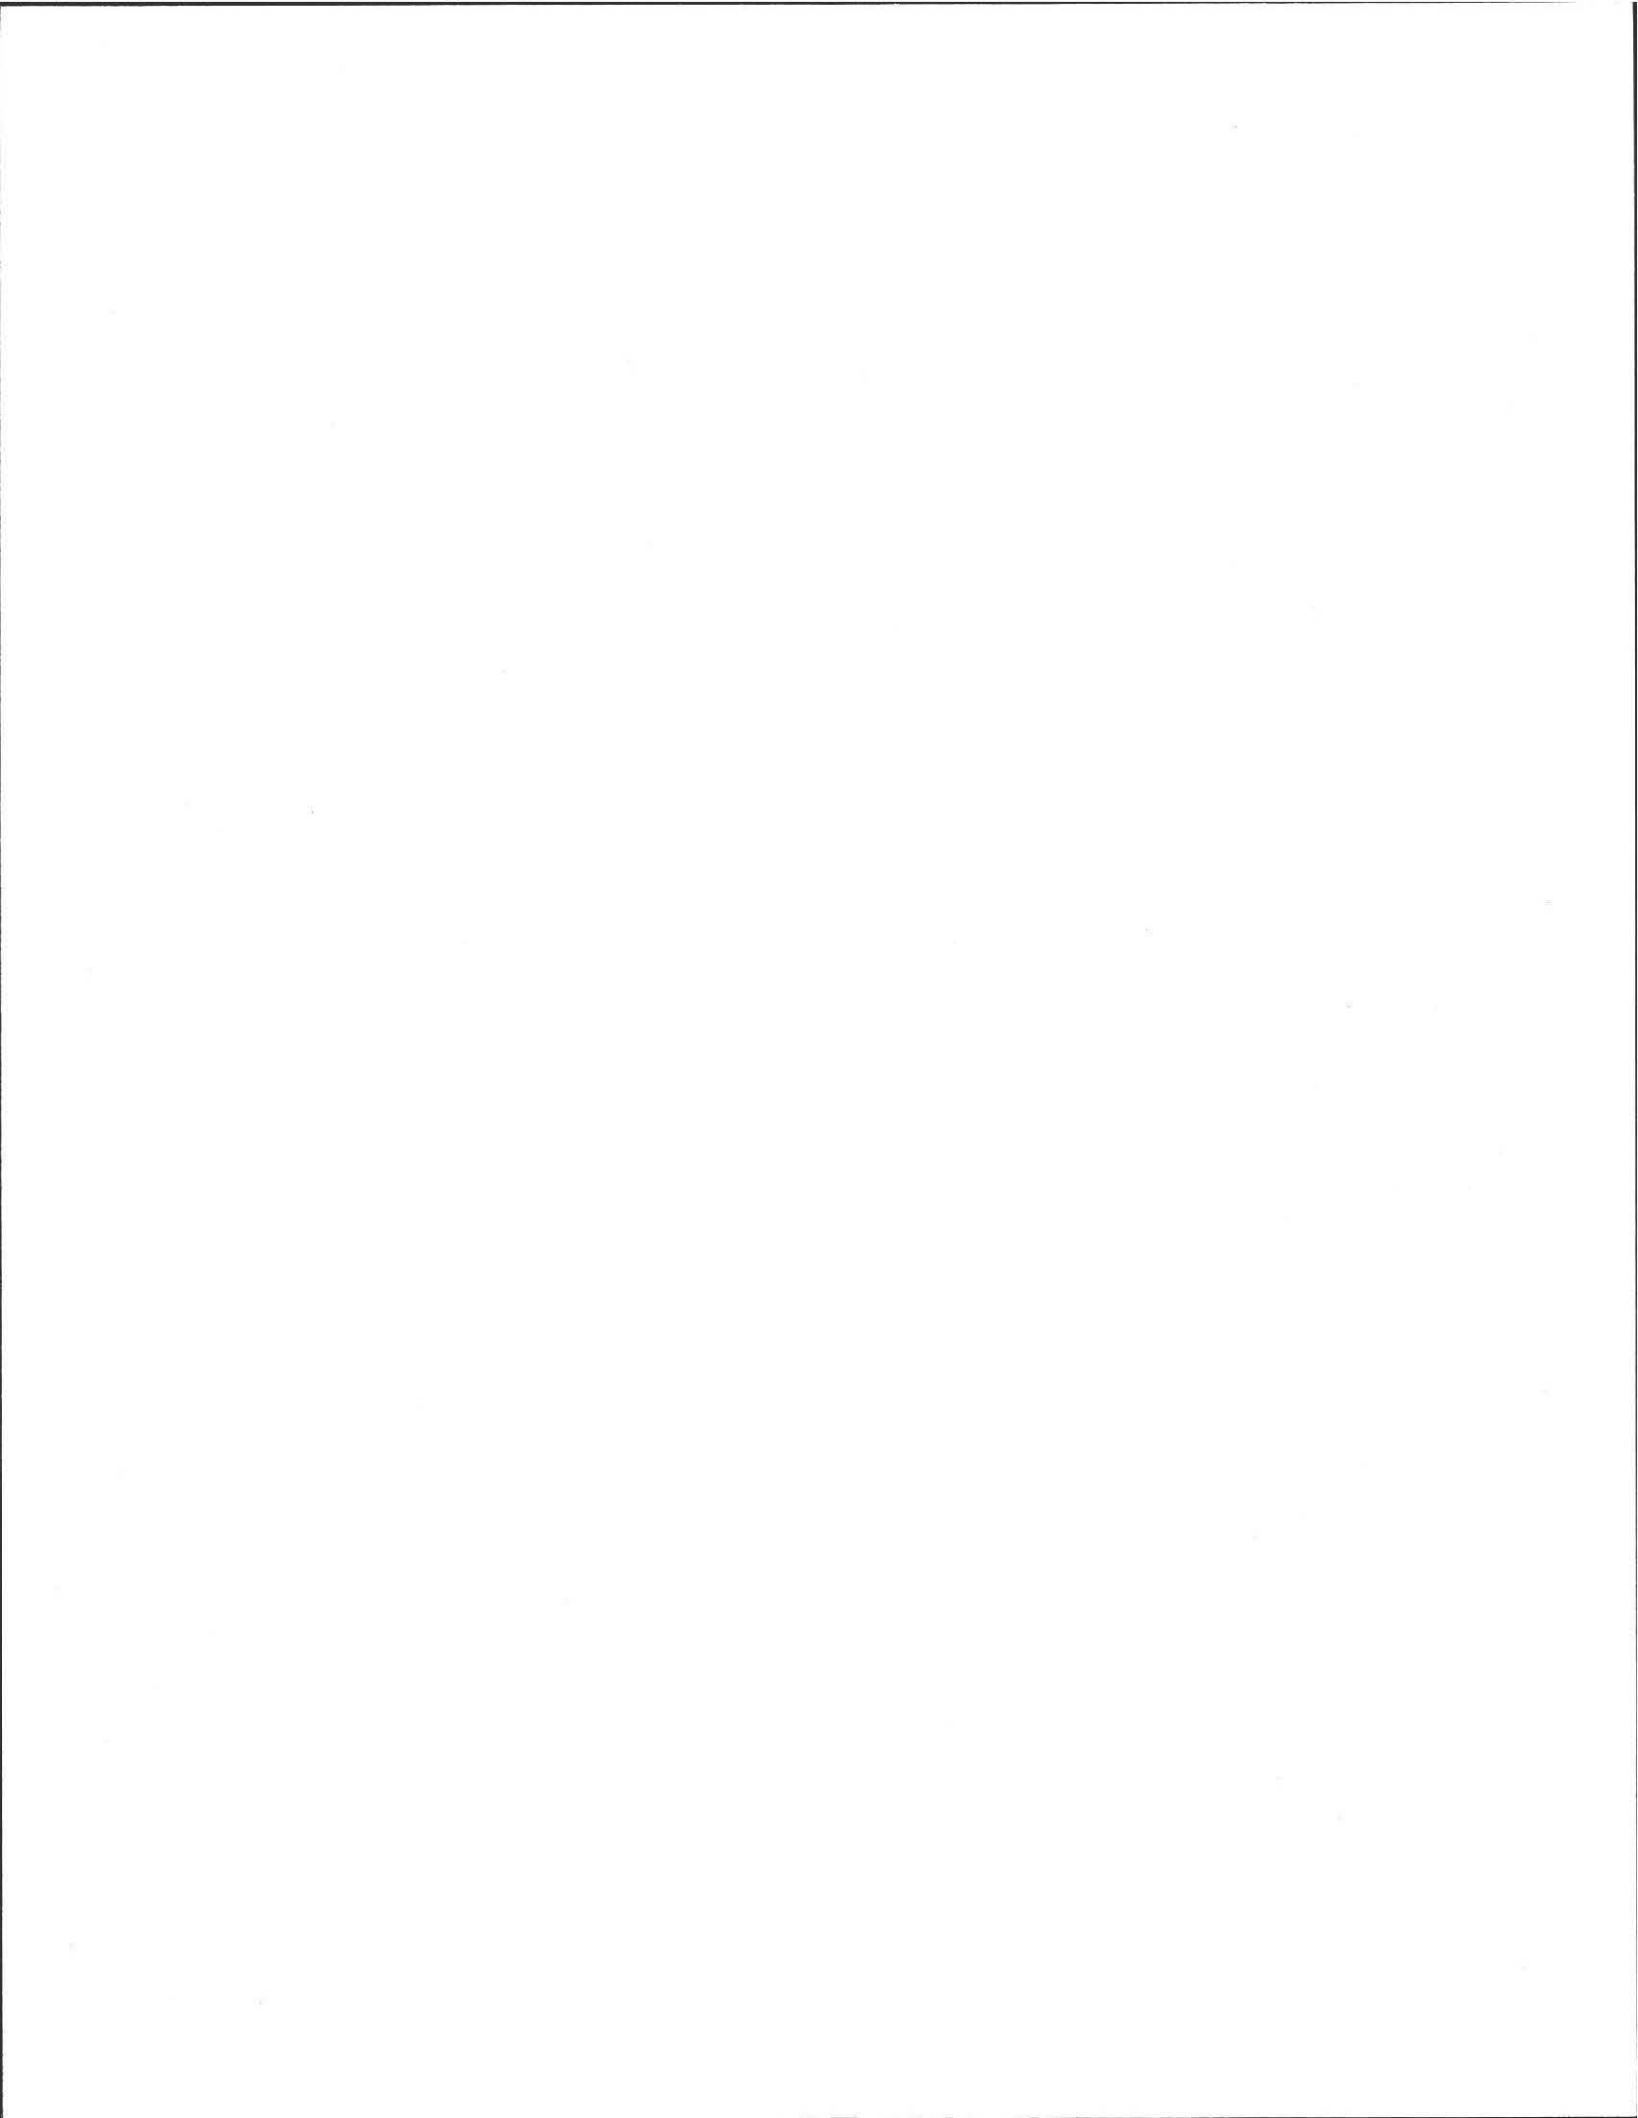

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION (continued)

Property Address: 751 NE ST.

Owner: Founds

Date of Inspection: 12/2/03

SOIL ABSORPTION SYSTEM (SAS): Y (locate on site plan, excavation not required)

If SAS not located explain why:

Type

- leaching pits, number: _____
- leaching chambers, number: _____
- leaching galleries, number: _____
- leaching trenches, number, length: _____
- leaching fields, number, dimensions: 60' L x 18' W
- overflow cesspool, number: _____
- innovative/alternative system Type/name of technology: _____

Comments (note condition of soil, signs of hydraulic failure, level of ponding, damp soil, condition of vegetation, etc.):

No signs of Failure

CESSPOOLS: No (cesspool must be pumped as part of inspection)(locate on site plan)


- Number and configuration: _____
- Depth – top of liquid to inlet invert: _____
- Depth of solids layer: _____
- Depth of scum layer: _____
- Dimensions of cesspool: _____
- Materials of construction: _____
- Indication of groundwater inflow (yes or no): _____

Comments (note condition of soil, signs of hydraulic failure, level of ponding, condition of vegetation, etc.):

PRIVY: No (locate on site plan)

- Materials of construction: _____
- Dimensions: _____
- Depth of solids: _____

Comments (note condition of soil, signs of hydraulic failure, level of ponding, condition of vegetation, etc.):

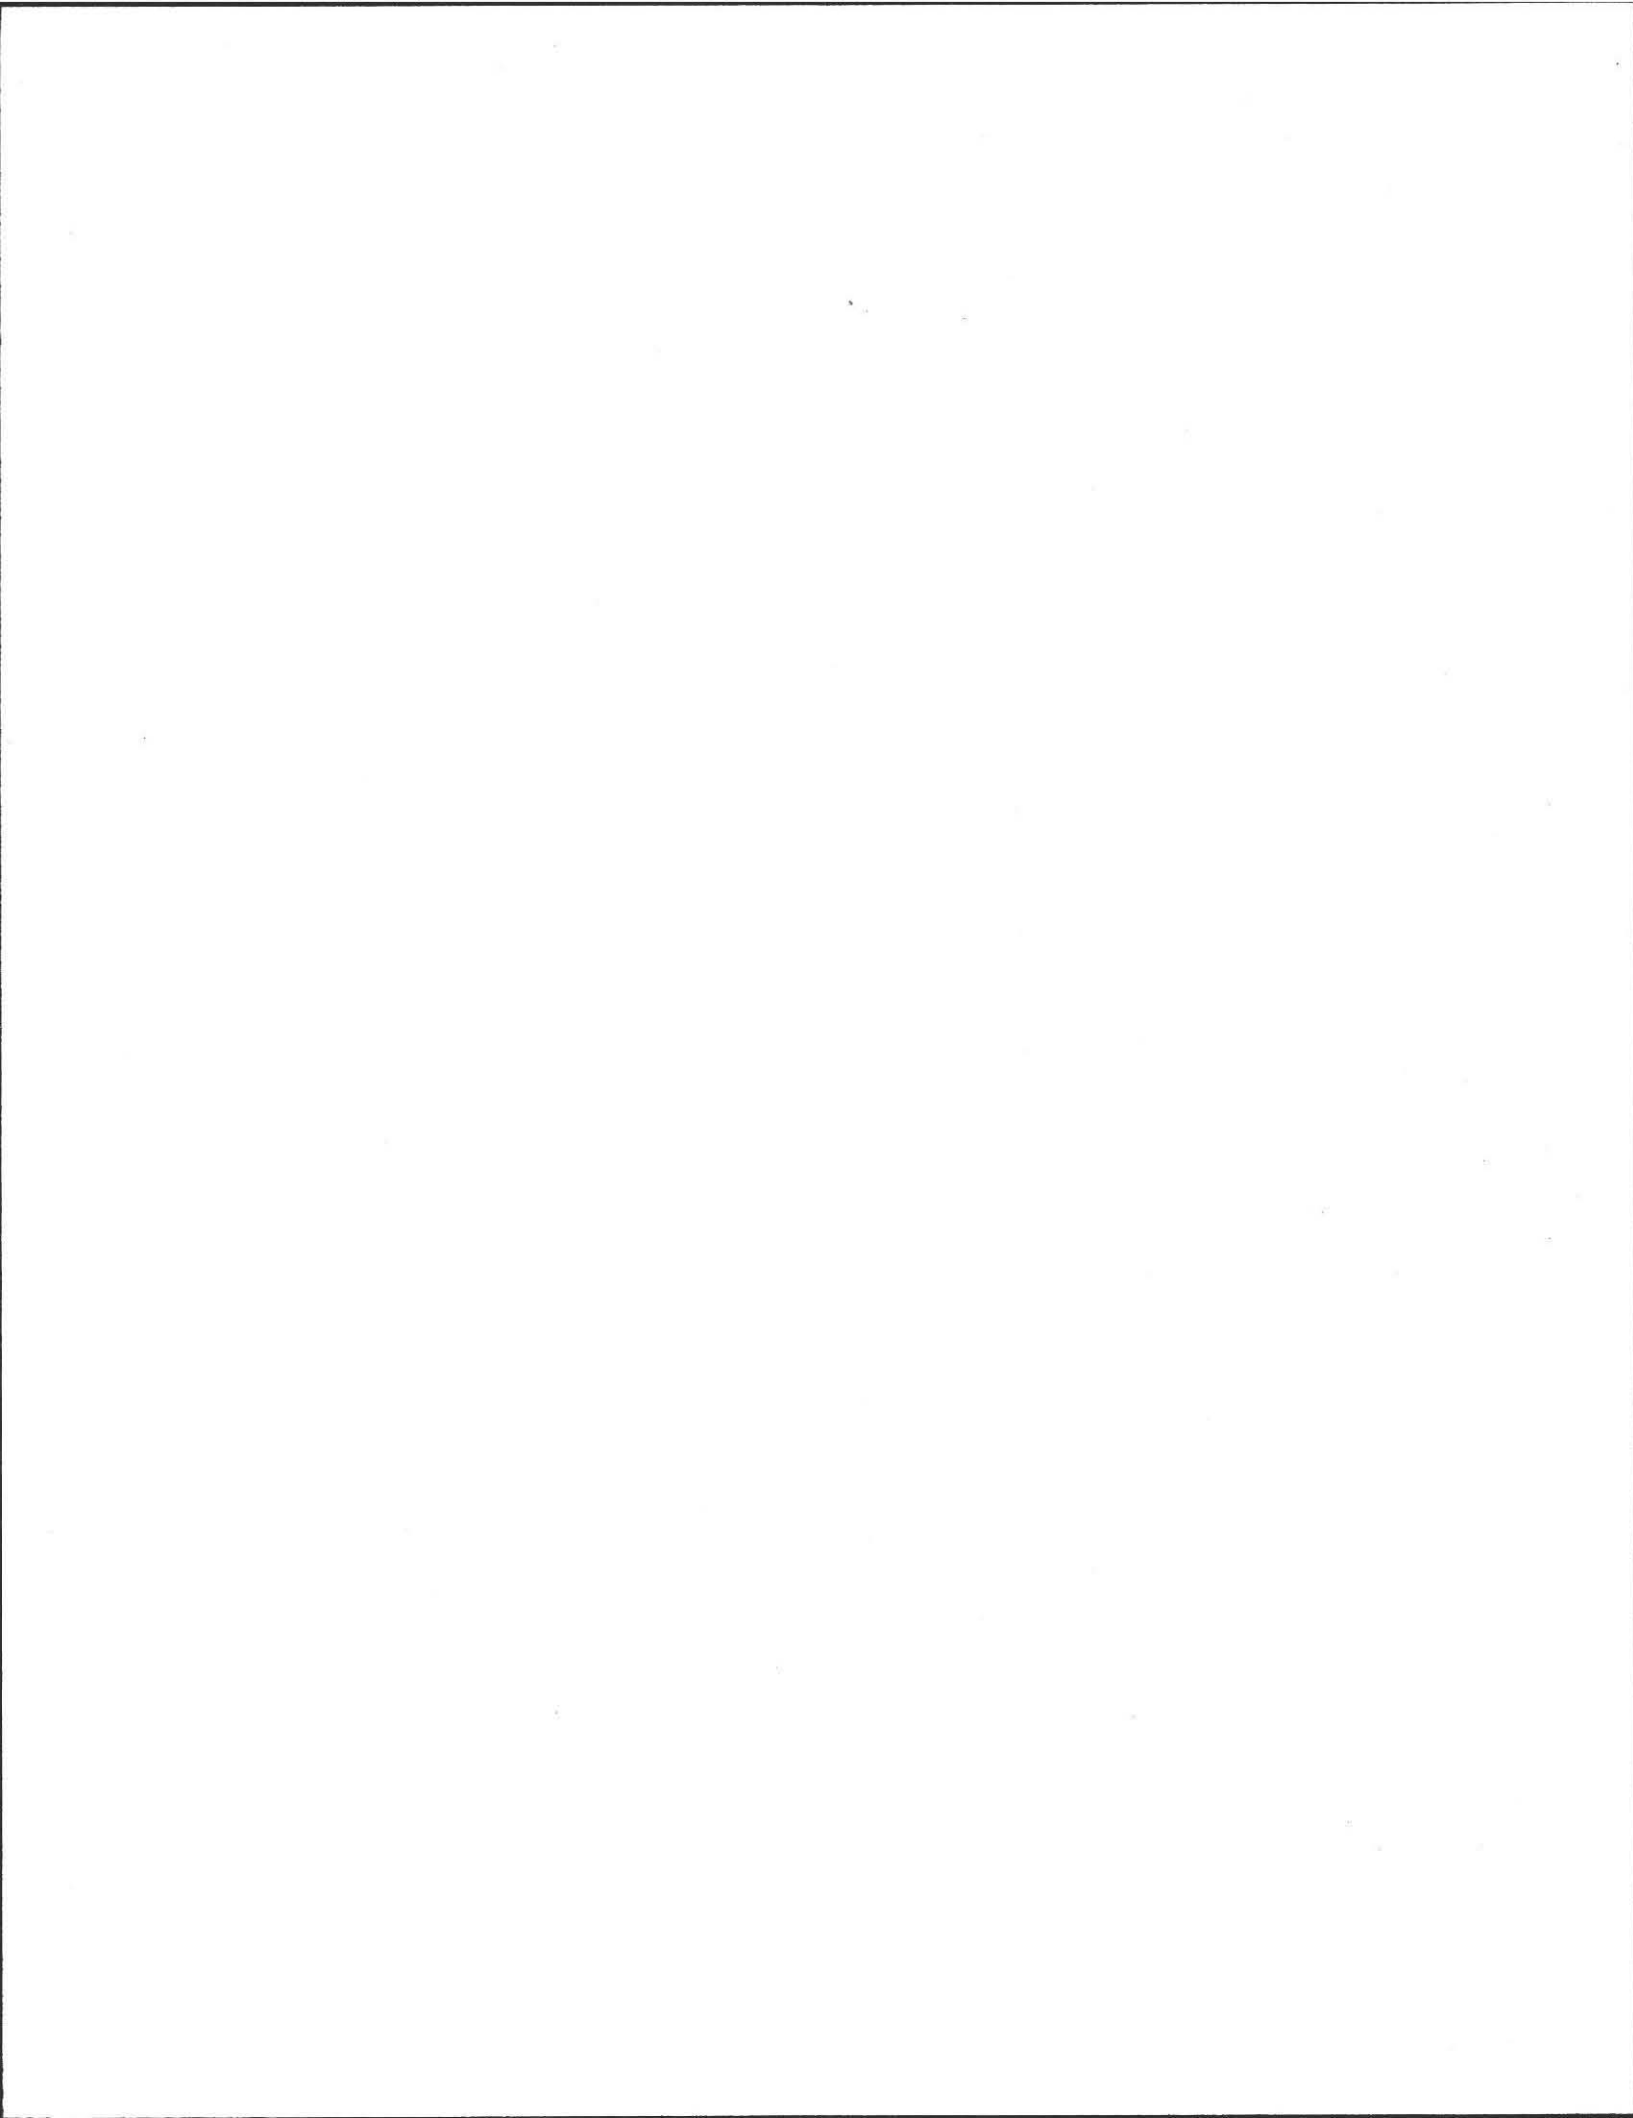

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION (continued)

Property Address: 751 NE ST


Owner: Founds

Date of Inspection: 12/2/03

SKETCH OF SEWAGE DISPOSAL SYSTEM

Provide a sketch of the sewage disposal system including ties to at least two permanent reference landmarks or benchmarks. Locate all wells within 100 feet. Locate where public water supply enters the building.

SEE PLAN ATTACHED

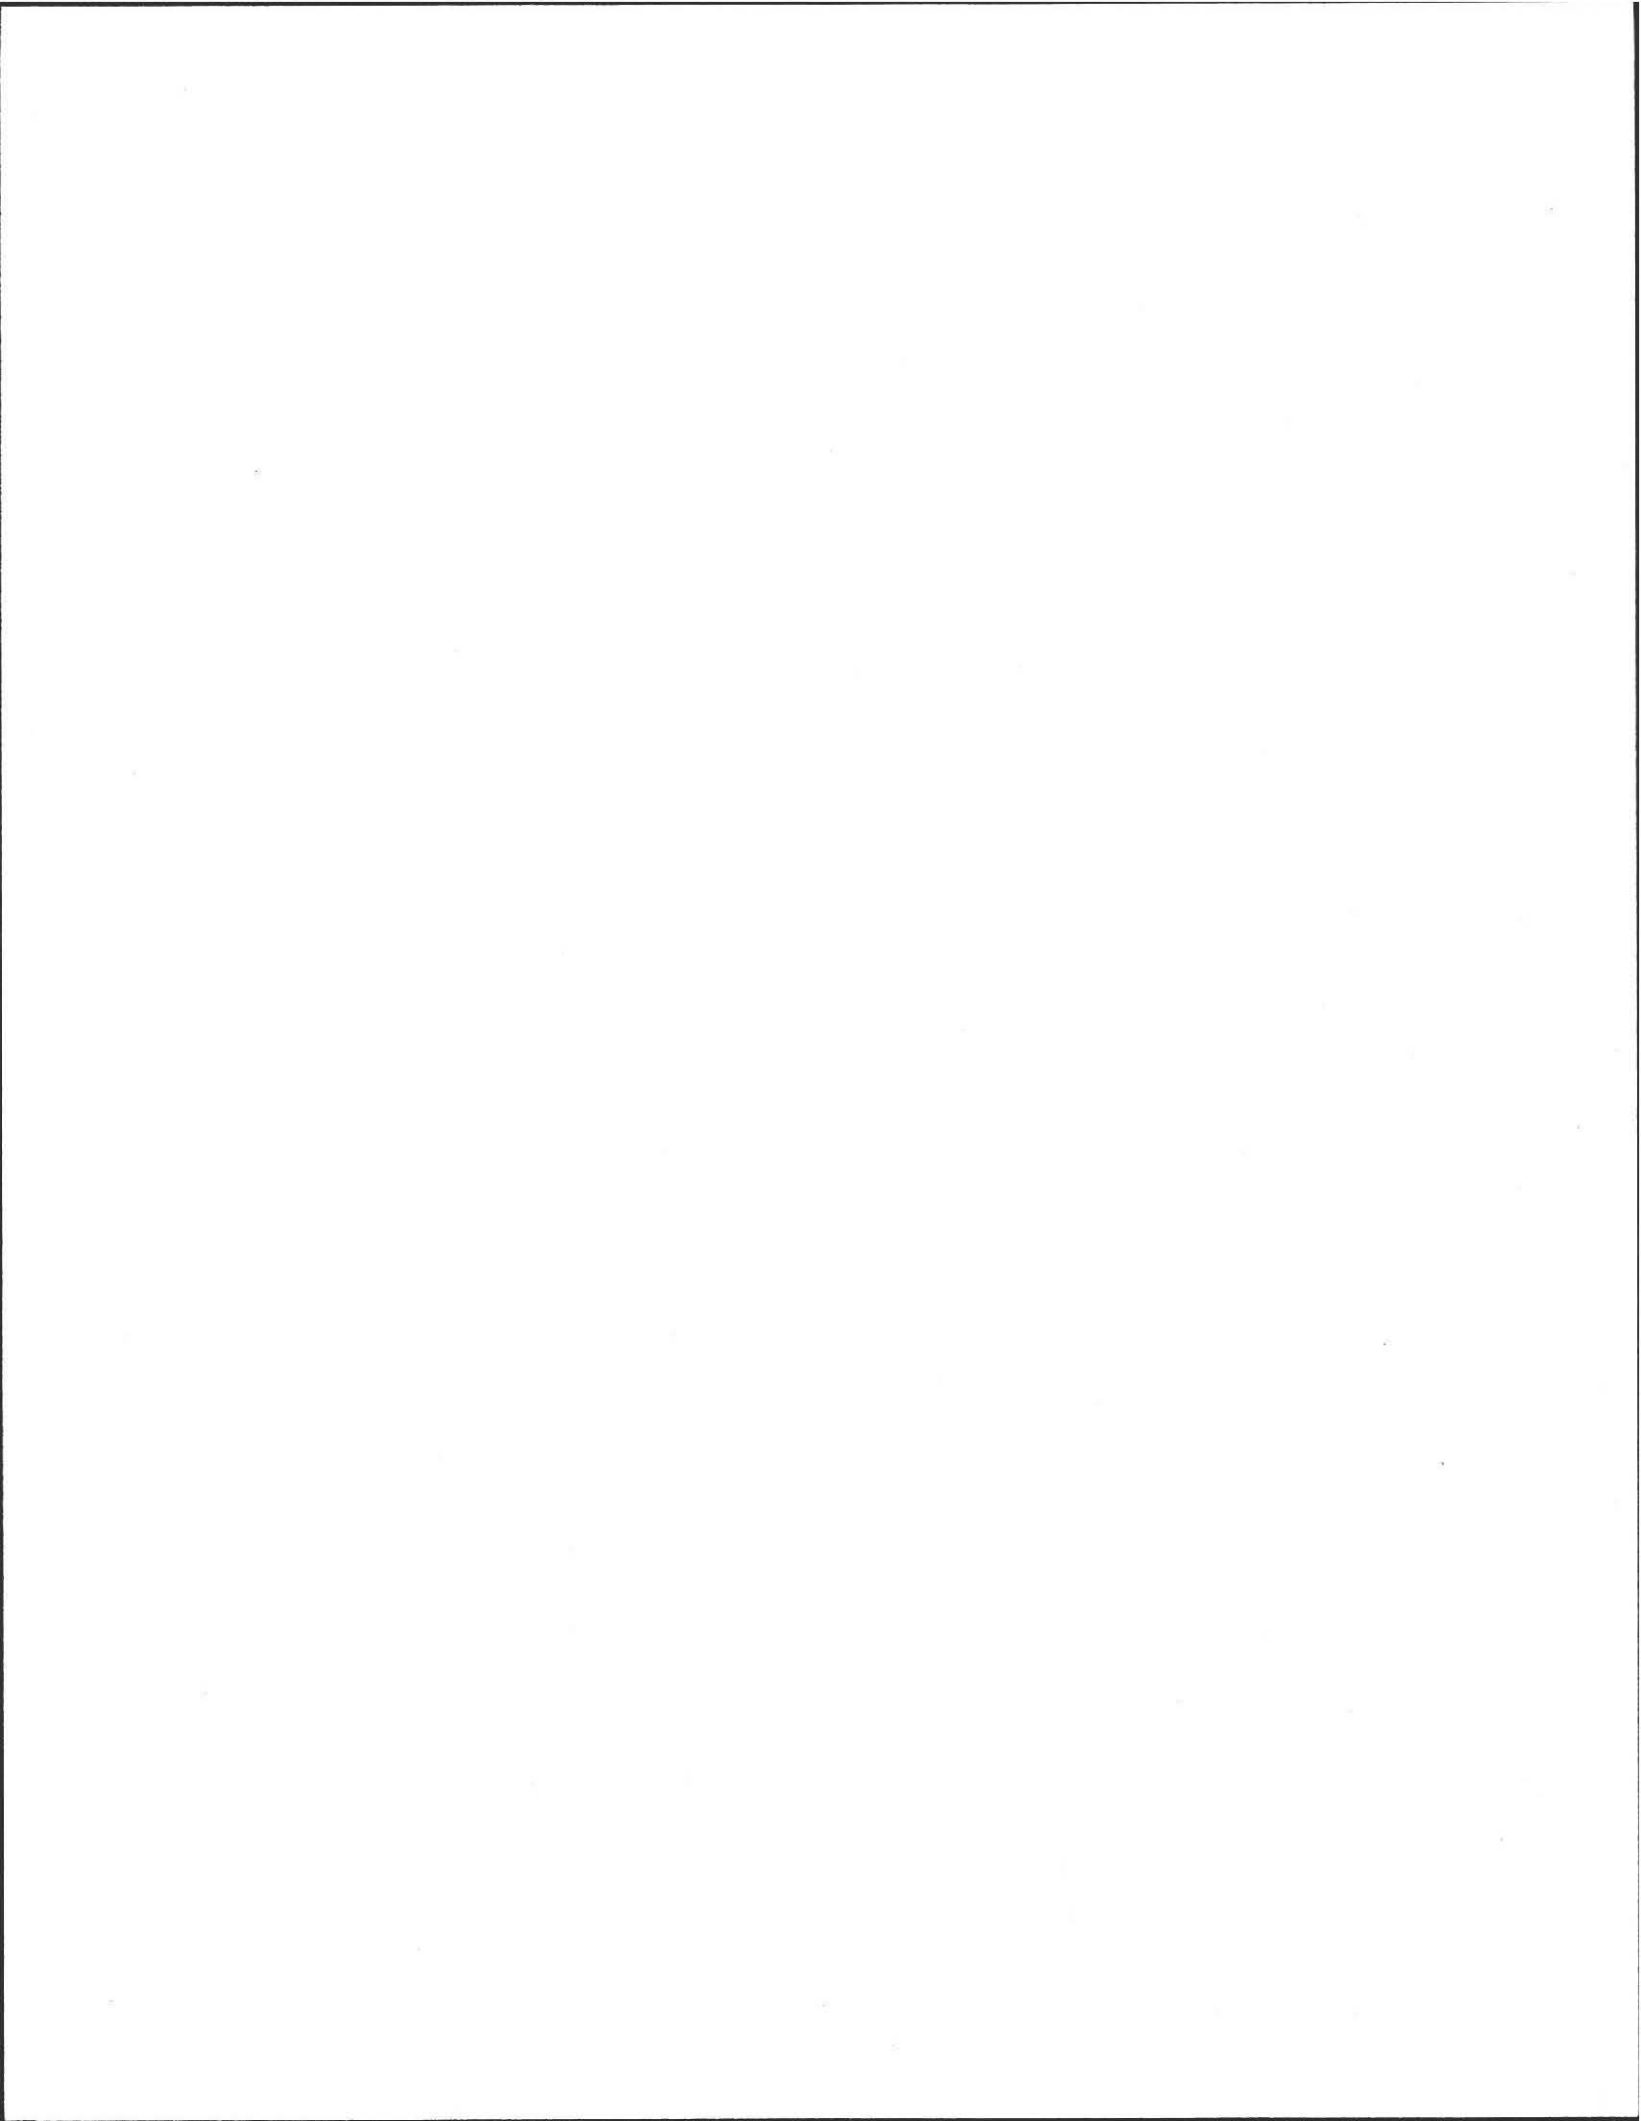

OFFICIAL INSPECTION FORM – NOT FOR VOLUNTARY ASSESSMENTS
SUBSURFACE SEWAGE DISPOSAL SYSTEM INSPECTION FORM
PART C
SYSTEM INFORMATION (continued)

Property Address: 751 NE ST.

Owner: Founds

Date of Inspection: 12/2/03

SITE EXAM

- Slope
- Surface water
- Check cellar
- Shallow wells


Estimated depth to ground water 4' feet AT SAS. (Elevated)

Please indicate (check) all methods used to determine the high ground water elevation:


- Obtained from system design plans on record - If checked, date of design plan reviewed: 7/13/01
- Observed site (abutting property/observation hole within 150 feet of SAS)
- Checked with local Board of Health-explain: _____
- Checked with local excavators, installers- (attach documentation)
- Accessed USGS database-explain: _____


You must describe how you established the high ground water elevation:

SEE RECORDS.

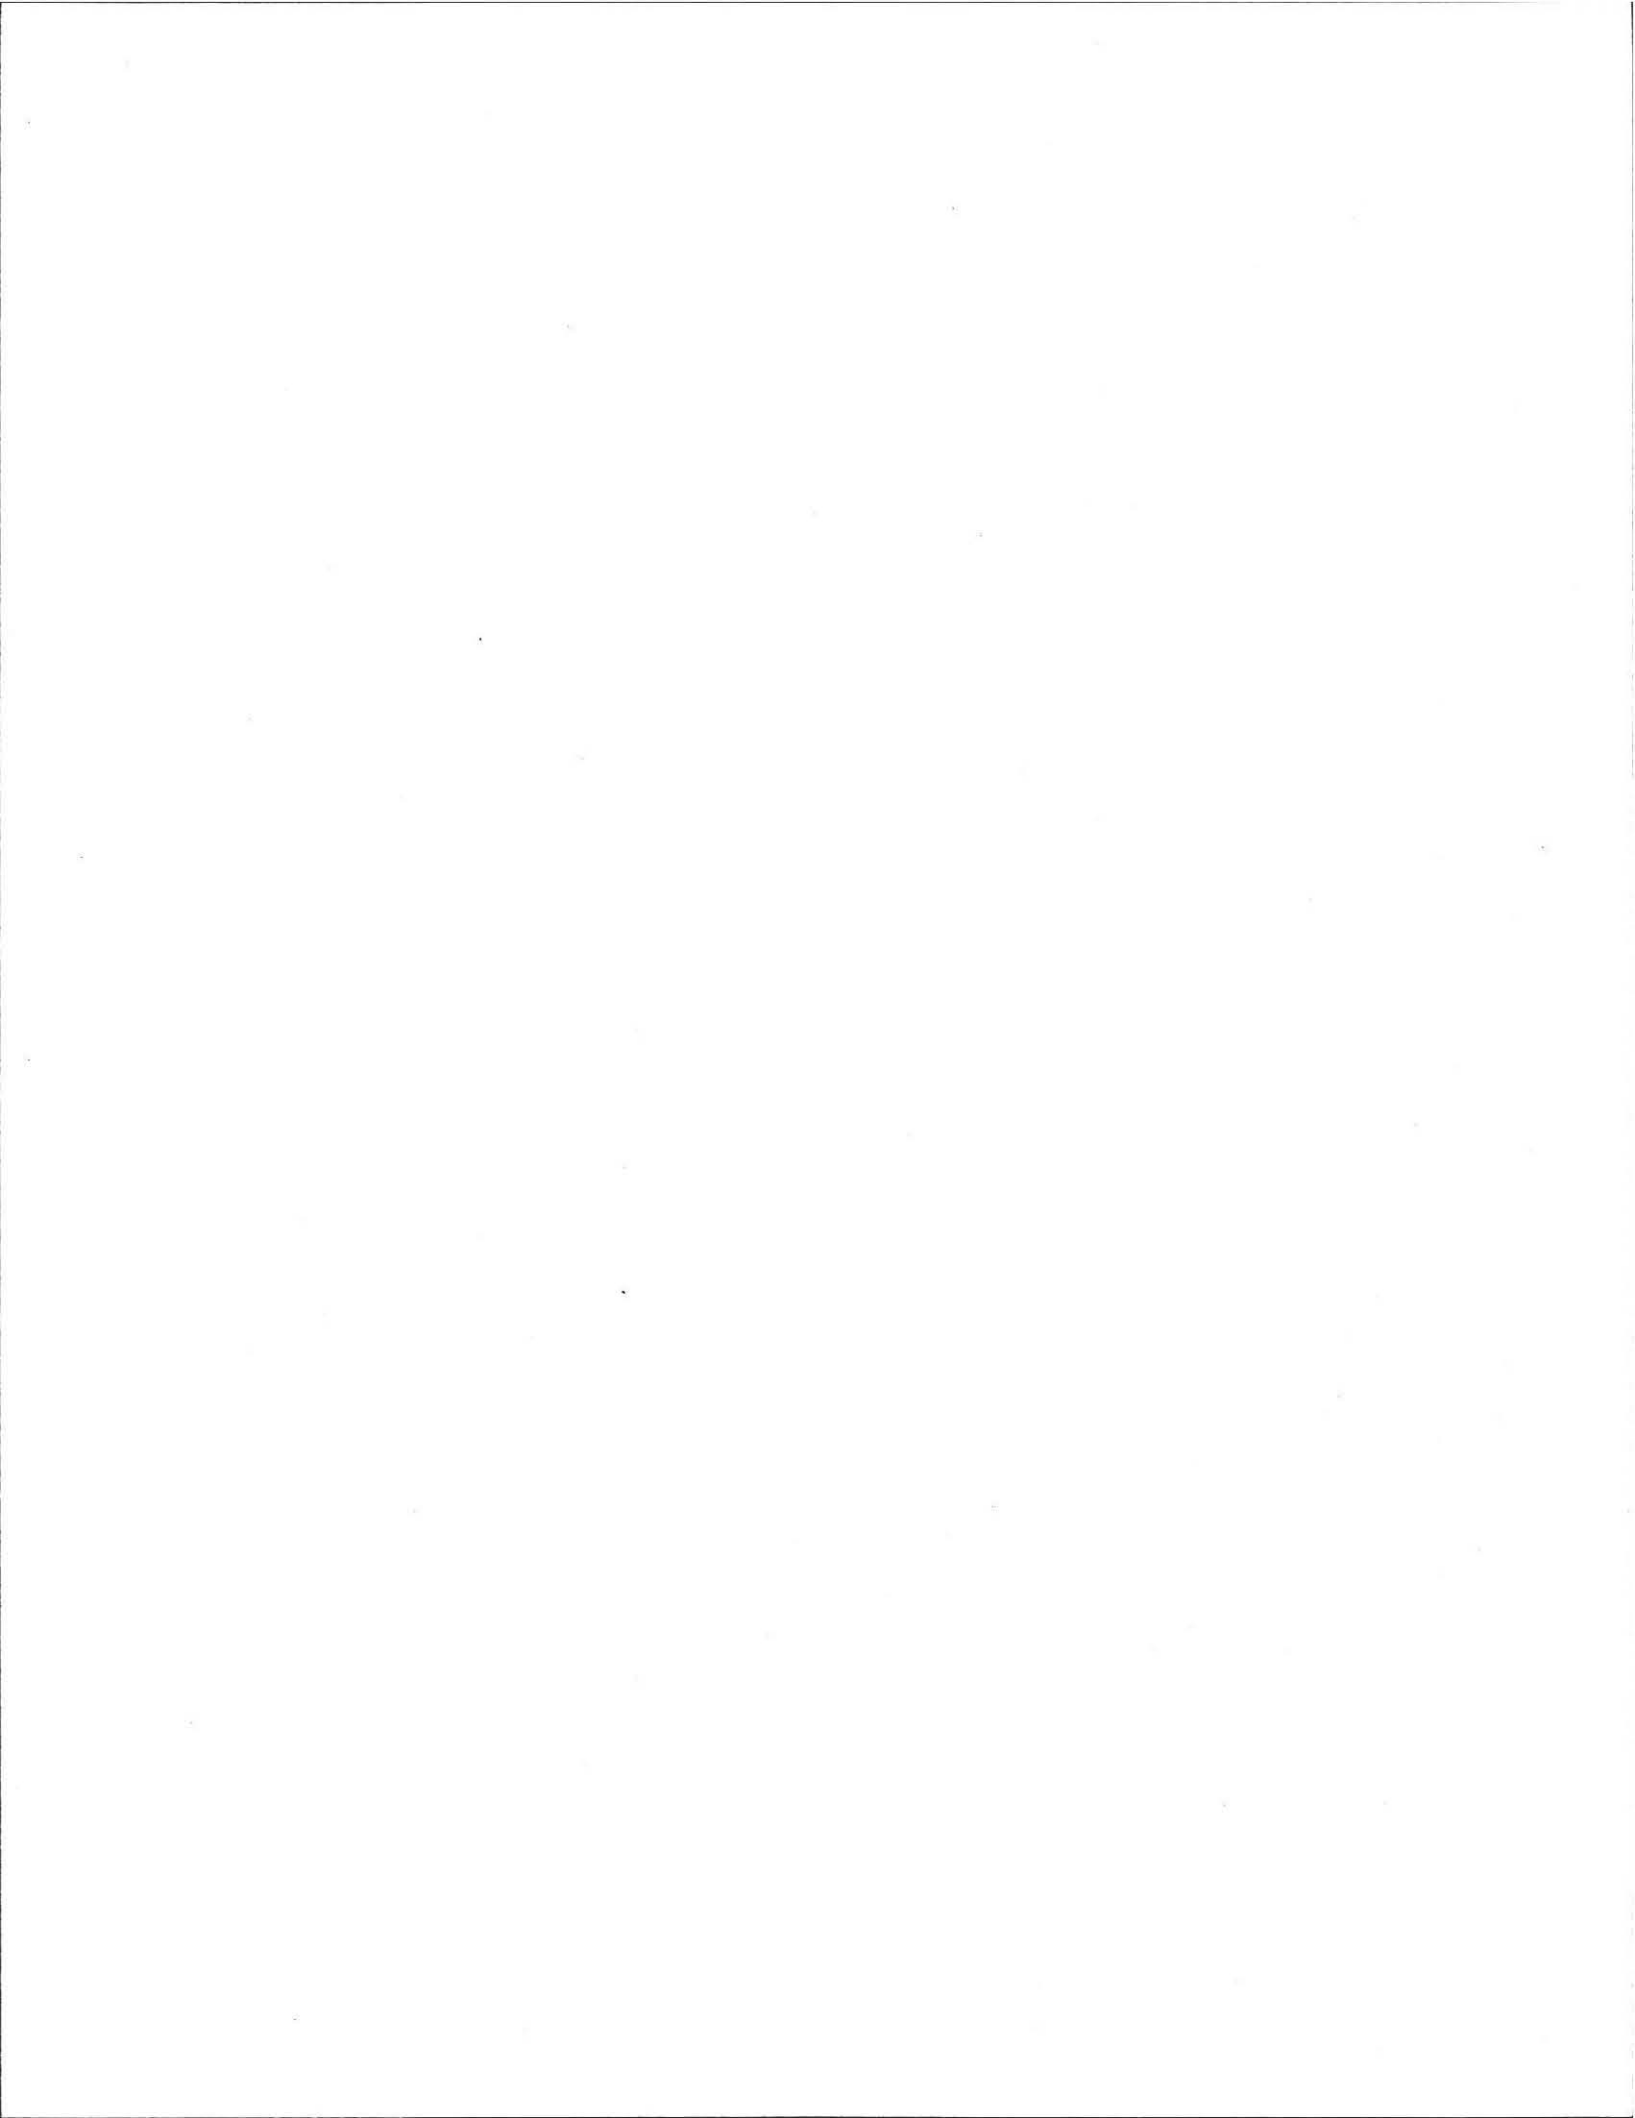


being vegetated wetland is or certified vernal pools within 100 ft.
 tion system (S.A.S.). There are no surface water supplies
 he S.A.S. There are no other water supply wells or tributaries
 proposed septic tank or the S.A.S.

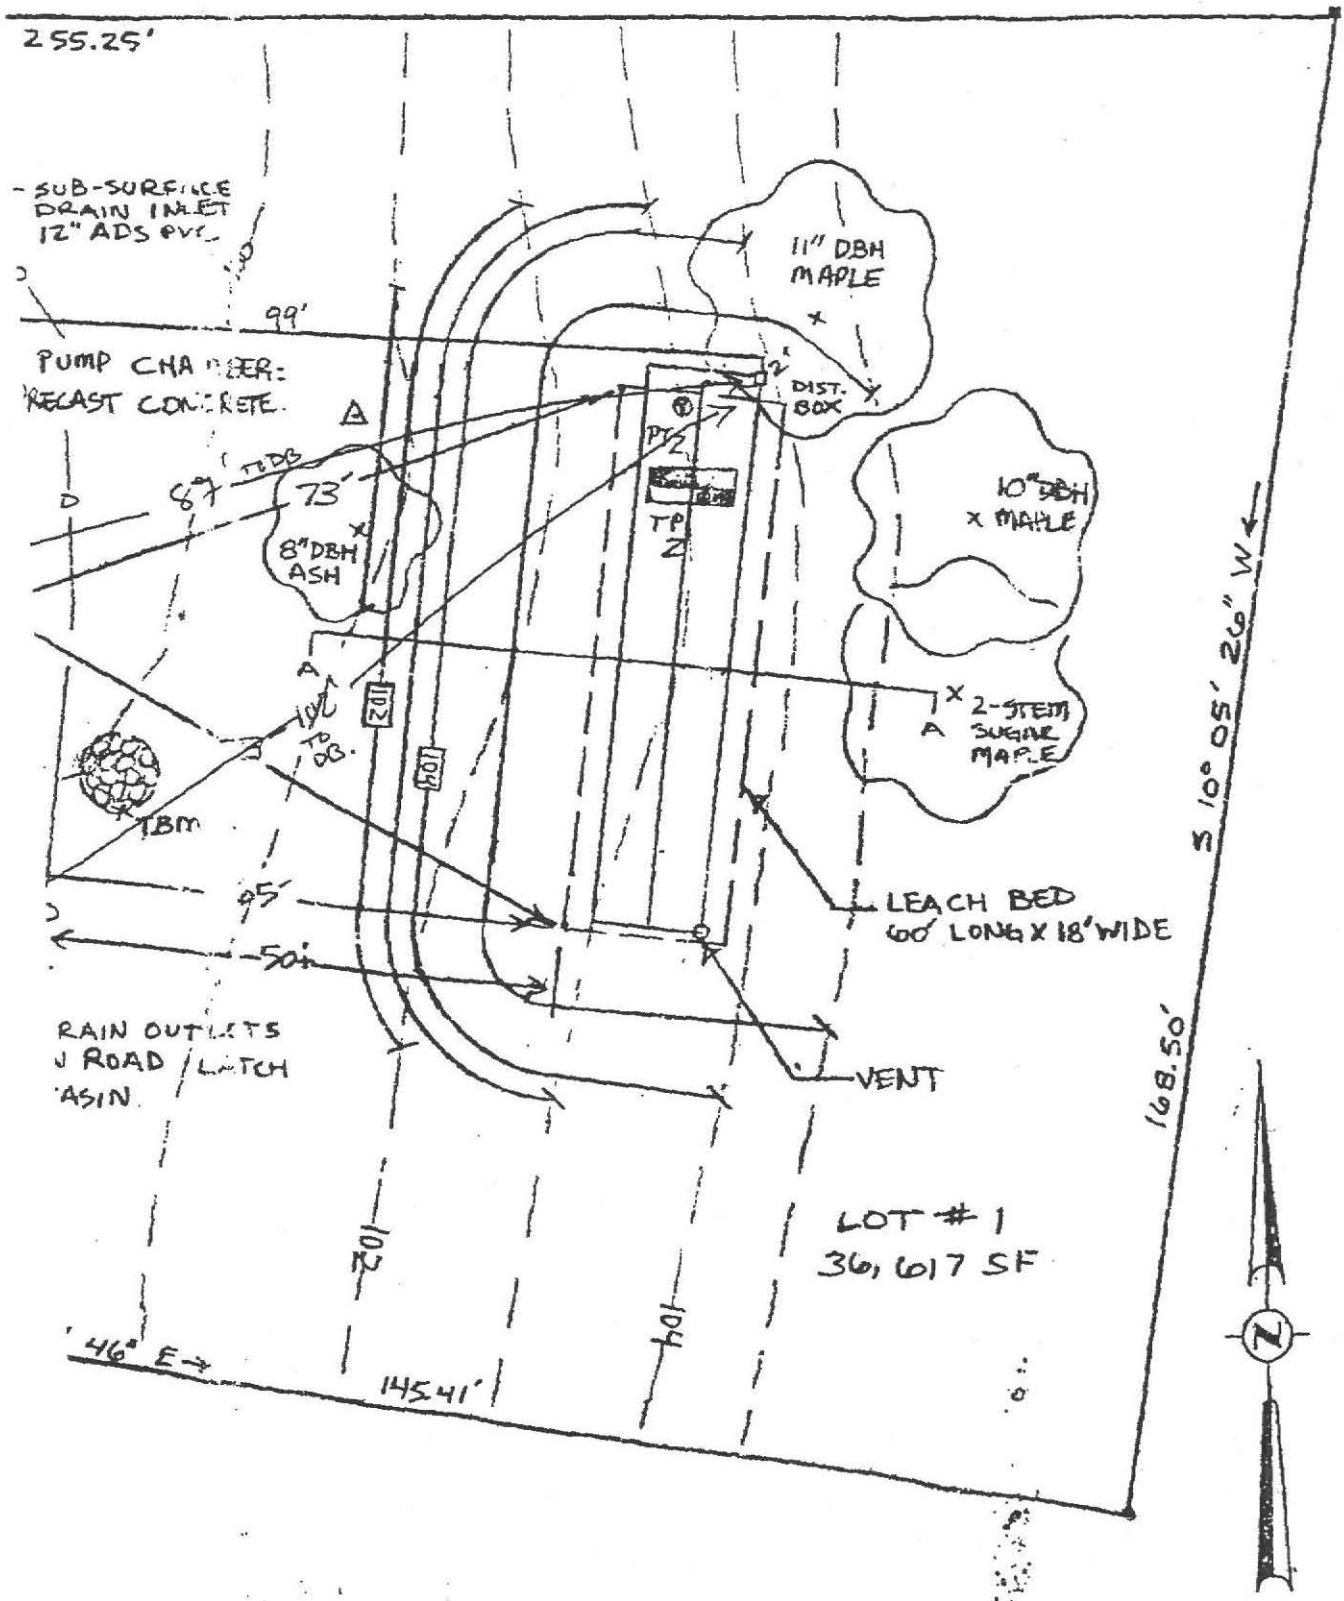

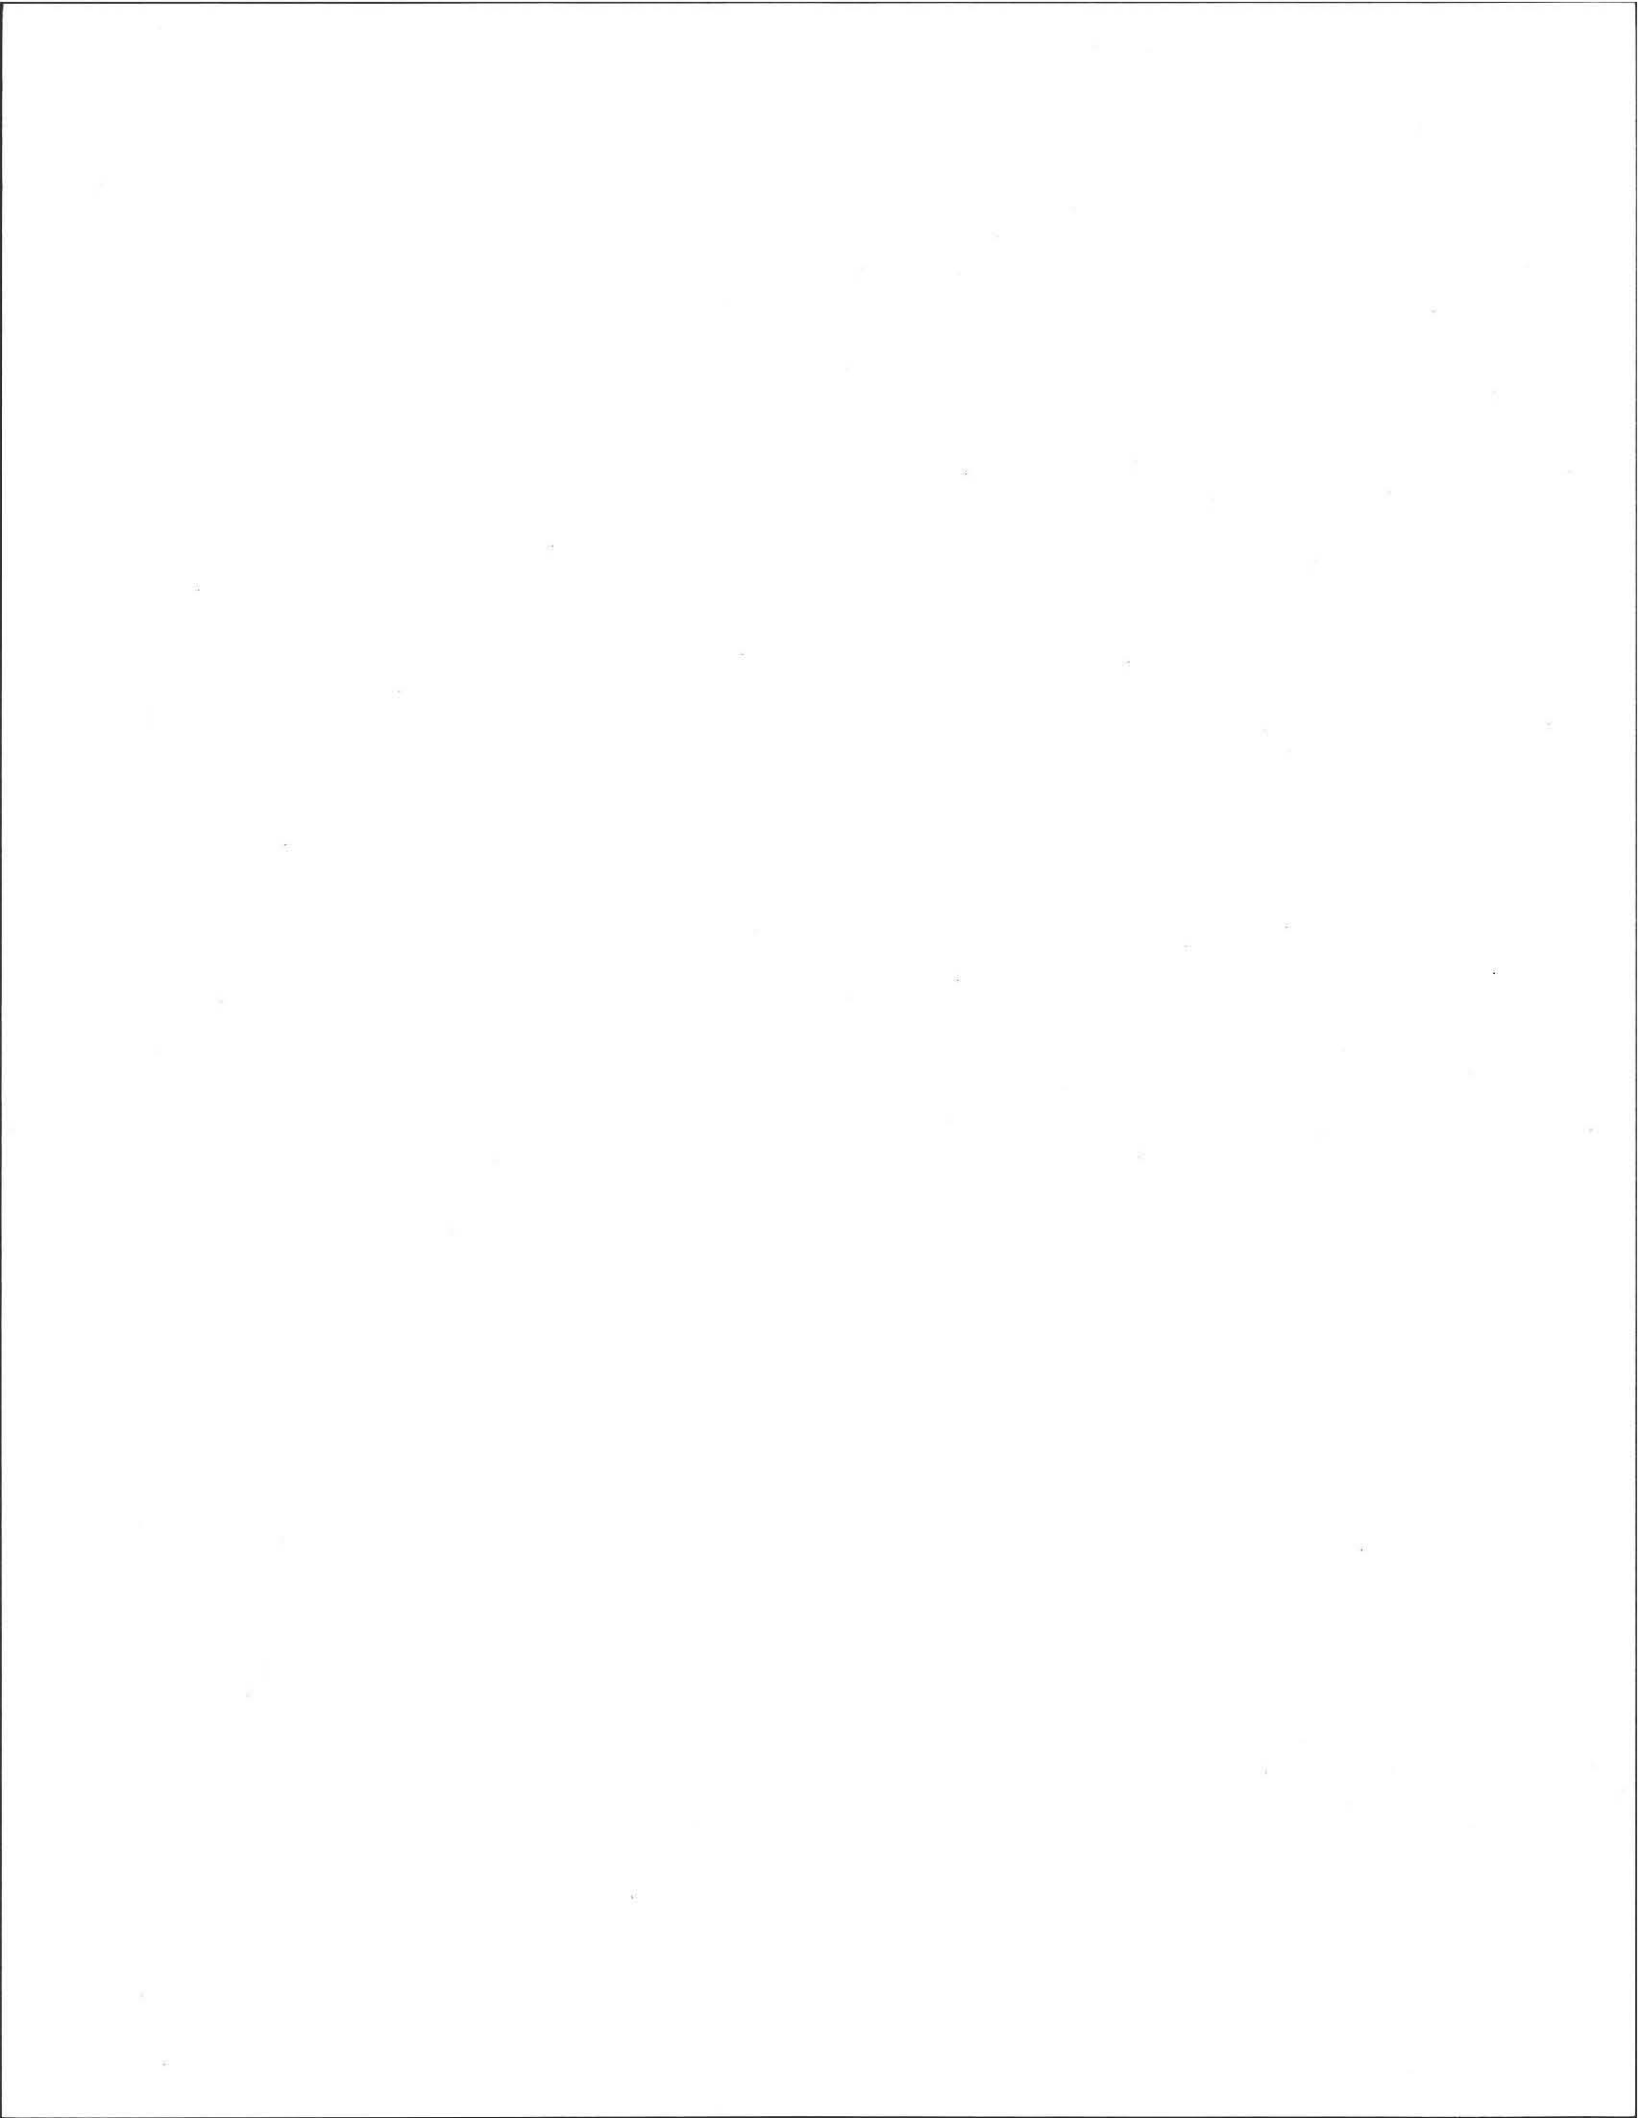

NOTE: There are no surface waters, border of the proposed septic tank or the soil absorber within 400 ft. of the proposed septic tank or to surface water supplies within 200 ft. of the

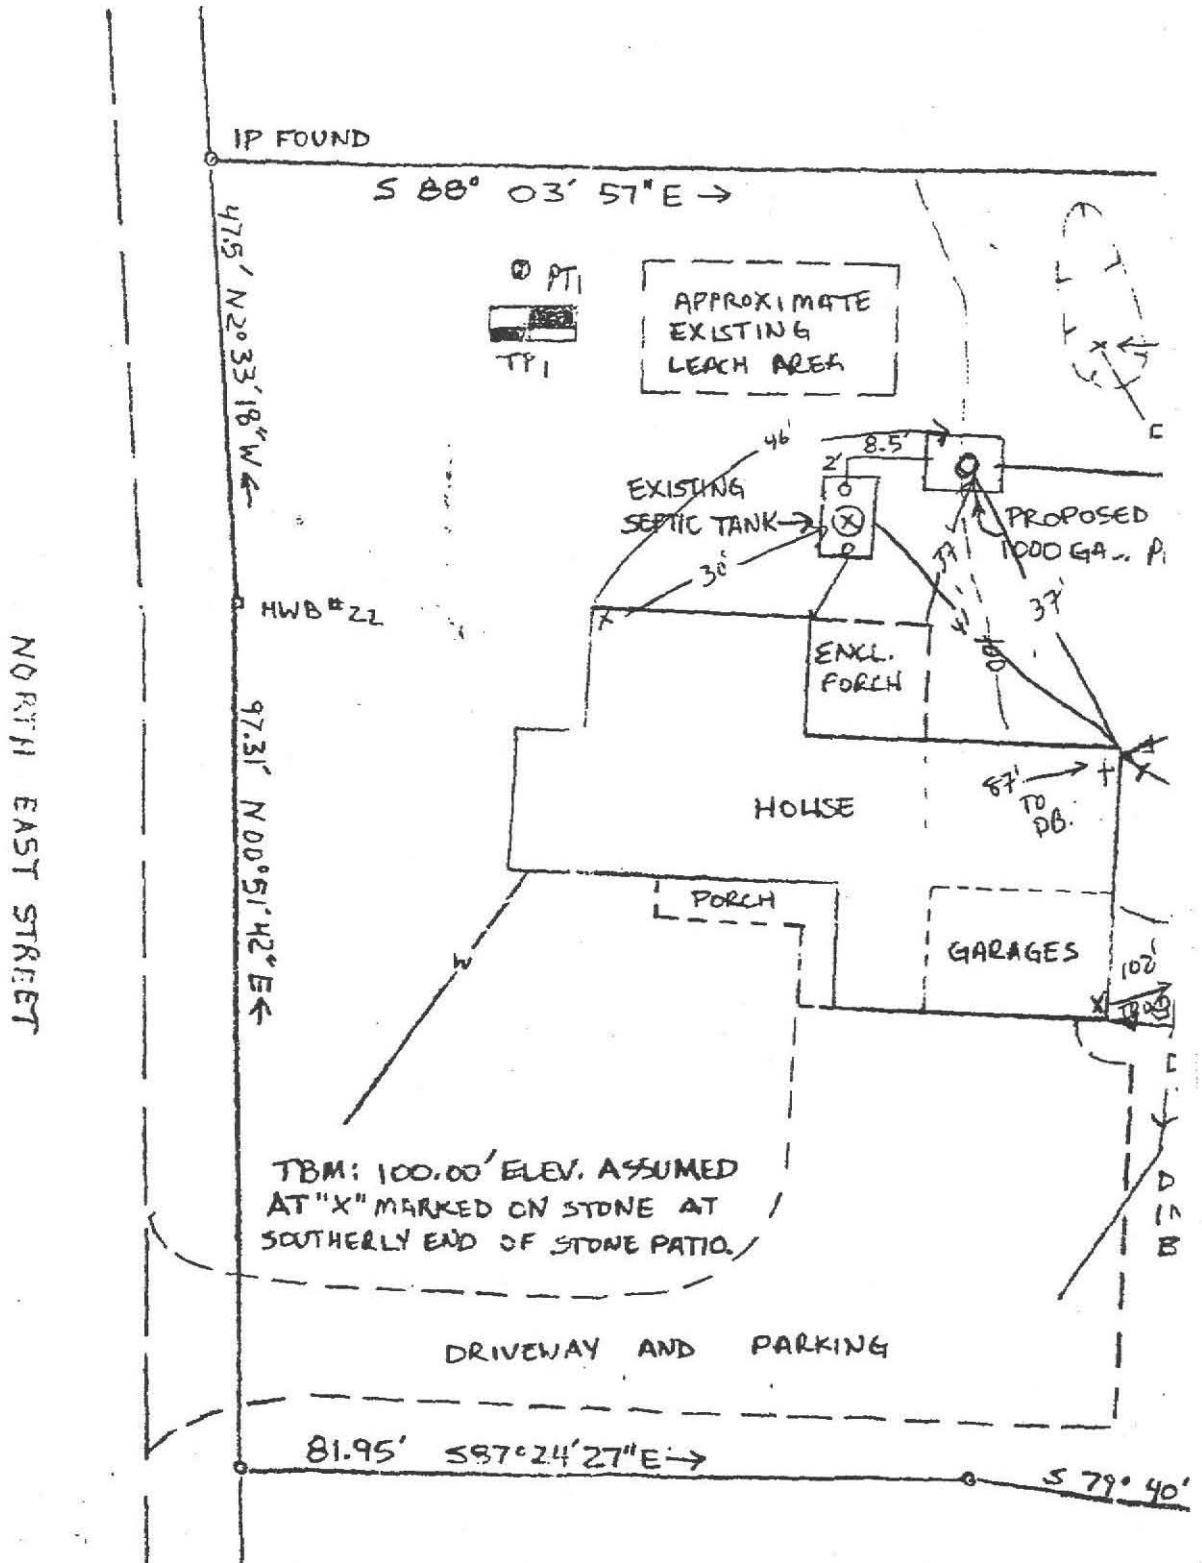

LEGEND

---XXX--- CONTOUR LINE (1' INTERVAL)

